












Monday, September 30, 2019

Weekly Progress Report











East Bethel Elementary School

Anticipated Substantial Completion – October 2019

Completed for Week Ending September 27, 2019:

-  Finish install casework in admin / media center areas
-  MEP final connections in admin area
-  Window trim installed throughout building
-  Paint finishing / touch ups ongoing throughout building
-  Basketball hoop installation in Gym
-  HVAC controls work ongoing
-  Contractor items cleared from Gym area
-  Smart board / projector installations ongoing
-  All other work is taking place around the school day schedule as necessary

Progress Planned for Week Ending October 4, 2019:

-  Finish branding walls in entry way
-  Site restoration around pump house
-  Vestibule heater installation throughout building
-  Finish window trim throughout building
-  Paint finishing / touch ups throughout building
-  Moisture mitigation applied to gym floor
-  Acoustical wall panels installed in gym
-  Paint parking lot light poles
-  Smart board / projector installations ongoing
-  All other work is taking place around the school day schedule as necessary

Weekly Progress Report

St. Francis Elementary School

Anticipated Substantial Completion (of the building) – January 2020

Completed for Week Ending September 27, 2019:

- ☒ Secure media center completed
- ☒ Finishes in progress for open media center
- ☒ Completion of Area E restrooms
- ☒ Roof deck installed on building addition
- ☒ Smart board / projector installations ongoing
- ☒ Punch list work ongoing

Progress Planned for Week Ending October 4, 2019:

- ☒ Finishes in progress for open media center
- ☒ Finished floor installation in open media center
- ☒ Continued finishes of Area E restrooms
- ☒ MEP rough ins for building addition
- ☒ Begin brick installation on building addition
- ☒ Smart board / projector installations ongoing
- ☒ Punch list work ongoing

St. Francis Middle School

Anticipated Substantial Completion – November 30, 2020

Completed for Week Ending September 27, 2019:

- ☒ Begin hallway VCT installation in Area E up to cafeteria
- ☒ SPED area flooring
- ☒ Continued tile work in cafeteria columns
- ☒ Continue MEP rough ins for Area B fitness room and restrooms
- ☒ Final plumbing connections in staff bathroom Area B
- ☒ Smart board / projector installations ongoing

Progress Planned for Week Ending October 4, 2019:

- ☒ Finish hallway VCT installation in Area E up to cafeteria
- ☒ SPED area flooring completed
- ☒ Finish demo in Area A
- ☒ Continue MEP rough ins for Area B fitness room and restrooms
- ☒ Turn over staff bathrooms in Area B
- ☒ Smart board / projector installations ongoing

Weekly Progress Report

St. Francis High School

Anticipated Substantial Completion – August 21, 2020

Completed for Week Ending September 27, 2019:

- ☒ Continue framing in Area J classrooms
- ☒ Begin structural steel for fitness addition
- ☒ Fire protection piping installation ongoing
- ☒ Prep for concrete pour in Area C locker rooms
- ☒ Casework and accessory (shelves, countertops) installations ongoing
- ☒ PAC stage rigging installation
- ☒ Metals lab classroom finishes in progress
- ☒ HVAC controls work ongoing
- ☒ Ongoing punch list work
- ☒ Ongoing SMART board installations.

Progress Planned for Week Ending October 4, 2019:

- ☒ Install storefront systems at greeter station and community ed locations upon arrival of materials
- ☒ PAC drapery installation
- ☒ Begin wiring for Upper L business lab work
- ☒ Continue framing in Area J classrooms
- ☒ Continue structural steel for fitness addition
- ☒ Begin framing in Area C locker rooms
- ☒ Casework installations ongoing
- ☒ Metals lab classroom finishes complete
- ☒ HVAC controls work ongoing
- ☒ Ongoing punch list work
- ☒ Ongoing SMART board installations.

St. Francis Learning Center

Anticipated Substantial Completion – August 16, 2019

Completed for Week Ending September 27, 2019:

- ☒ Punch list work ongoing

Progress Planned for Week Ending October 4, 2019:

- ☒ Front entry vestibule heater installation
- ☒ Punch list work ongoing

Weekly Progress Report

Progress Photos

Progress Photo: SFES Area D open media Center



Progress Photo: SFES Area D SPED resource area



Progress Photo: SFES School branding wall



Progress Photo: EBES Area B reception desk



Weekly Progress Report

Progress Photo: EBES Area B gym



Progress Photo: SFMS Area E hallway flooring install



Progress Photo: EBES Area C SPED resource area




Progress Photo: SFMS Area E SPED flooring install



Weekly Progress Report

Progress Photo: SFMS Area B cafeteria wall tile progress

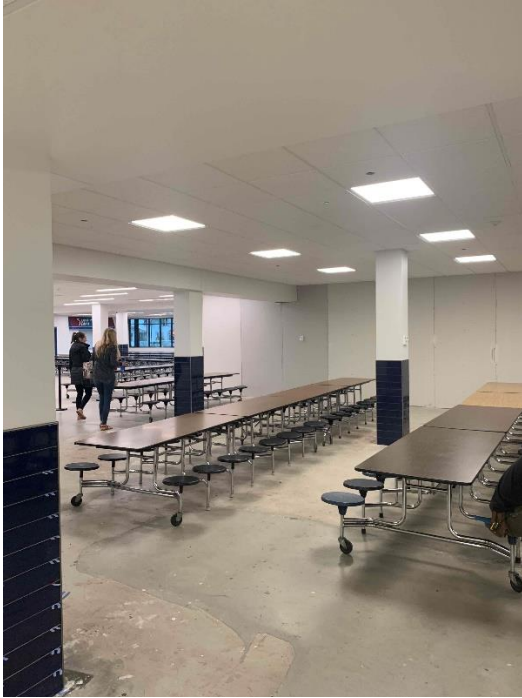


Progress Photo: SFHS Area C locker room progress



Progress Photo: SFHS Area H greeter station



Progress Photo: SFHS Upper Area H casework progress

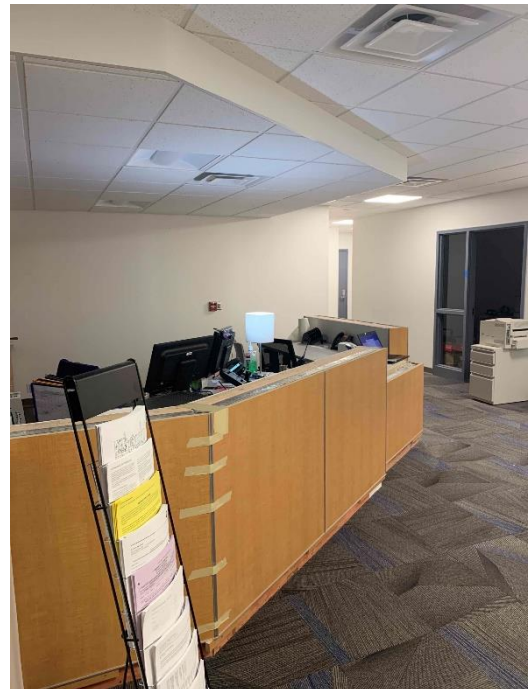

End of Report
