

ics | CONSULTING, INC



**ISD #15 St. Francis Area Schools  
Building Projects  
2017 - 2021**

**Tuesday, May 28, 2019**

**Weekly Progress Report**

**East Bethel Elementary School**

Anticipated Substantial Completion – August 16, 2019

**Completed for Week Ending May 24, 2019:**

- Continued brick installation on exterior walls
- Site silt fencing installed
- Existing brick demolition in progress

**Progress Planned for Week Ending May 31, 2019:**

- Complete brick installation on exterior walls
- Excavation for fire protection tank
- Begin setting structural steel

**St. Francis Elementary School**

Anticipated Substantial Completion (of the building) – January 2020

**Completed for Week Ending May 24, 2019:**

- Completed structural steel setting in area B
- Completed footing and foundation for classroom addition for interior columns
- Continued selective demolition of areas B & D as rooms become available
- Continued mechanical, electrical, plumbing rough-ins

**Progress Planned for Week Ending May 31, 2019:**

- Completed backfilling exterior walls
- Continued selective demolition of areas B & D as rooms become available
- Continued mechanical, electrical, plumbing rough-ins

## Weekly Progress Report

### St. Francis Middle School

Anticipated Substantial Completion – November 30, 2020

#### Completed for Week Ending May 24, 2019:

- ☒ Continuation of demolition in old cafeteria and adjacent work room area
- ☒ Continued masonry in Area A
- ☒ Finalize selective demolition in Area A
- ☒ Continued selective demolition in Area E vacant classrooms
- ☒ Begin setting structural steel in Area A

#### Progress Planned for Week Ending May 31, 2019:

- ☒ Structural steel setting complete in Area A
- ☒ Continued masonry in Area A
- ☒ Concrete replacement for selective demo Area A
- ☒ Begin rough-in wall framing

### St. Francis High School

Anticipated Substantial Completion – August 21, 2020

#### Completed for Week Ending May 24, 2019:

- ☒ Perform saw cutting concrete floors in locker room
- ☒ Finalize mechanical, electrical rough-ins for classrooms in area J
- ☒ Concrete floor demolition in locker rooms (area D)
- ☒ Begin drywall install in area J classrooms

#### Progress Planned for Week Ending May 31, 2019:



- ☒ Continued concrete floor removal from saw cutting in locker rooms
- ☒ Heavy equipment arrival onsite for fitness addition excavation
- ☒ Continued drywall in area J classrooms

## Weekly Progress Report

# St. Francis Learning Center

Anticipated Substantial Completion – August 16, 2019

### Completed for Week Ending May 24, 2019:

-  Construction kick off meeting
-  Continued contractor submittals

### Progress Planned for Week Ending May 31, 2019:

-  Continued contractor submittals

# Weekly Progress Report

## Progress Photos

**Progress Photo:** SFES Classroom addition foundation wall progress.



**Progress Photo:** SFES Media Center demo progress.



**Progress Photo:** SFES East side entry addition structural steel progress.



**Progress Photo:** EBES Classroom addition exterior wall demolition.



## Weekly Progress Report

**Progress Photo:** EBES classroom addition brick progress.



**Progress Photo:** SFMS old workroom demo progress.



**Progress Photo:** EBES admin addition exterior wall brick progress.



**Progress Photo:** SFMS Area A new band room progress.



## Weekly Progress Report


**Progress Photo:** SFMS Gym floor protection installed.



**Progress Photo:** SFHS Area C Locker Room floor cutting progress.



**Progress Photo:** SFHS Area J classroom progress lower level.

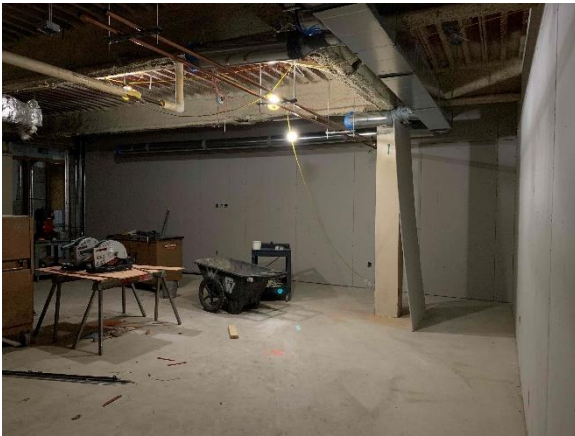

**Progress Photo:** SFHS Area J classroom progress upper level.



**End of Report**
