
	<p align="center">ICS Weekly Project Report January 13, 2020</p>
	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

East Bethel Elementary School

- **Week ending Friday, January 10, 2020**
 - Vinyl base patching in kindergarten area
 - Interior signage installation completed

- **Week ending Friday, January 17, 2020**
 - Ceiling tile and vinyl base repairs

St. Francis Elementary School

- **Week ending Friday, January 10, 2020**
 - Temporary occupancy inspection completed 1/10
 - Finish interior painting and trim
 - HVAC balancing completed
 - Interior signage installation completed
 - Contractor punch list work on building addition
 - Classroom content move from SFMS beginning
 - Classroom technology delivery completed

- **Week ending Friday, January 17, 2020**
 - Classroom technology installation
 - Continue move of classroom contents from SFMS to addition
 - Furniture delivery and install throughout the week
 - Contractor punch list work continuing

Weekly Project Report

January 13, 2020

St. Francis Middle School

- **Week ending Friday, January 10, 2020**
 - Drywall completed in cafeteria expansion
 - Ceiling grid installation in progress for cafeteria expansion
 - Wall tile in progress for staff restrooms in Area B
 - Electrical rough in for Area D classrooms underway
 - Drywall in progress for Area B fitness room

- **Week ending Friday, January 17, 2020**
 - Wall tile work in progress for cafeteria expansion
 - Interior painting of cafeteria expansion
 - Ceiling tile installation in cafeteria expansion
 - VCT flooring install in cafeteria expansion
 - Casework install in Area D classrooms
 - Interior painting of Area D classrooms
 - VCT flooring installation in Area D classrooms

St. Francis High School

- **Week ending Friday, January 10, 2020**
 - Complete epoxy flooring in Area C locker rooms
 - Begin demolition in Area L future school store
 - Continue Drywall in Lower J classrooms
 - Asbestos abatement in band/choir area
 - Shoring installation in band/choir area
 - CMU demo in band/choir area

- **Week ending Friday, January 17, 2020**
 - Prep for structural steel installation in band/choir area
 - Finish CMU demo in band/choir area
 - Fire proofing treatment in Area C locker room
 - Finish abatement in band choir/area
 - Interior finishes in Lower J classrooms beginning

Weekly Project Report

January 13, 2020

Early Childhood Family Center

- **Week ending Friday, January 10, 2020**

- **Week ending Friday, January 17, 2020**
 - Contract award by school board on 1/13
 - Schedule furniture meetings

Cedar Creek Elementary School

- **Week ending Friday, January 10, 2020**
 - Design coordination held with building admin

- **Week ending Friday, January 17, 2020**
 - Contract award by school board on 1/13
 - Schedule furniture meetings

Weekly Project Report

January 13, 2020

Progress Photos:



EBES ceiling repairs



SFES Addition Flex Resource Area



EBES masonry repairs



SFES Addition Flex / Conference Space

Weekly Project Report

January 13, 2020

Progress Photos:




SFES Typical Classroom in Addition



SFMS Cafeteria Expansion Ceiling Grid



SFMS Area B Fitness Room Drywall

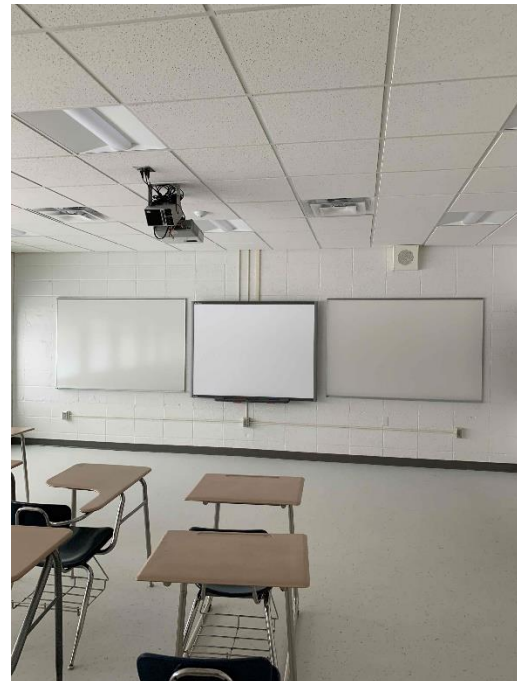

SFMS Area D Typical Classroom

Weekly Project Report

January 13, 2020

Progress Photos:



SFHS Band / Choir Area



SFHS Band / Choir Shoring



SFHS Area C locker room epoxy flooring

End of Report
