
	<p align="center"><b>ICS Weekly Project Report</b> February 3, 2020</p>
	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

### **East Bethel Elementary School**

- **Week ending Friday, January 31, 2020**
  - Cafeteria acoustical panels installed
  
- **Week ending Friday, February 7, 2020**
  - February 17<sup>th</sup> contractors to be in school finishing work.
    - Cafeteria VCT repair
    - Vinyl base in area A
    - "COLLABORATION" in media center replaced with white lettering
    - Fire caulking in area A
    - Terrazzo patching in area B

### **St. Francis Elementary School**

- **Week ending Friday, January 31, 2020**
  - Door Hardware Modifications in front office
  - Card reader installation in new addition
  - Contractor working on punch list completion
  
- **Week ending Friday, February 7, 2020**
  - Owner training
  - Door card reader installation in new addition
  - Contractor working on punch list completion

### **St. Francis Middle School**

- **Week ending Friday, January 31, 2020**
  - Finish Demo in area A
  - Drywall in lower area A
  - Finish Core drilling in upper area A
  
- **Week ending Friday, February 7, 2020**
  - Metal stud installation in upper A
  - Drywall in upper area A
  - Install metal handrails in cafeteria
  - Grout tile in cafeteria

# Weekly Project Report

February 3, 2020

## **St. Francis High School**

- **Week ending Friday, January 31, 2020**
  - Completed setting I beams in area F
  - Electrical Demo area L
  - Finish painting in Girls Locker room
  - Continue asbestos abatement in area F
  
- **Week ending Friday, February 7, 2020**
  - Continue asbestos abatement in area F
  - Begin setting foundation walls in area F
  - Electrical and Mechanical rough in area F
  - Setting lintels in area F

## **Early Childhood Family Center**

- **Week ending Friday, January 31, 2020**
  - General Contract Executed
  
- **Week ending Friday, February 7, 2020**
  - General Contractor sub-contracts to be issued.
  - ICS working with General Contractor to plan pre-construction meeting

## **Cedar Creek Elementary School**

- **Week ending Friday, January 31, 2020**
  - General Contract Executed
  
- **Week ending Friday, February 7, 2020**
  - General Contractor sub-contracts to be issued.
  - ICS working with General Contractor to plan pre-construction meeting


# Weekly Project Report

February 3, 2020

## Progress Photos:



SFMS Cafeteria addition wall tile complete

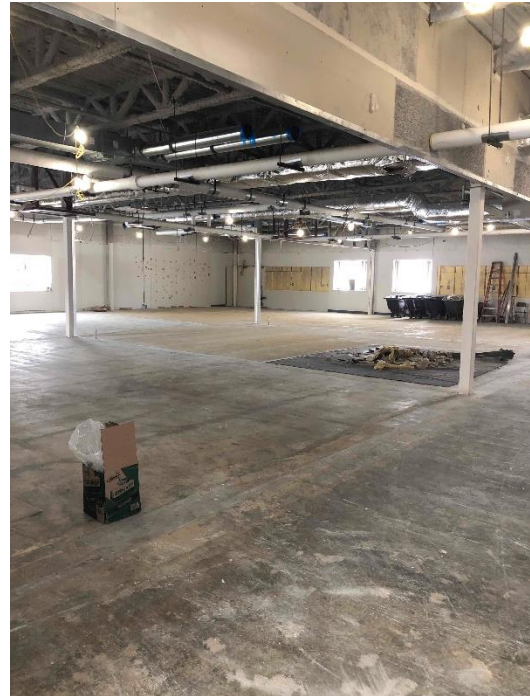

SFMS upper area A demo complete



SFMS Upper L Bathroom Demo



SFMS Lower A Drywall install

# Weekly Project Report

February 3, 2020

## Progress Photos:



SFHS Band/Choir I beam placed and shoring removed



SFHS Band/Choir new door openings prepped for framing



SFES new addition classrooms complete



SFES new addition hallway



# Weekly Project Report

February 3, 2020



SFES Student Lockers



SFES Student Common Area



SFES Student Learning Area

End of Report
