
	<p align="center">ICS Weekly Project Report February 10th, 2020</p>
	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

East Bethel Elementary School

- **Week ending Friday, February 7th, 2020**
 - No contractors on site until February 17th

- **Week ending Friday, February 14th, 2020**
 - February 17th new contractor finishing work
 - Cafeteria VCT Repair
 - Vinyl Base in area A
 - "COLLABORATION" in media center replaced with white lettering
 - Fire caulking in area A
 - Terrazzo patching in area B

St. Francis Elementary School

- **Week ending Friday, February 7th, 2020**
 - Door card reader installation in new addition
 - Owner training

- **Week ending Friday, February 14th, 2020**
 - Continue owner training

St. Francis Middle School

- **Week ending Friday, February 7th, 2020**
 - Plumbing and Electrical rough in upper area A
 - Taping in lower A
 - Cafeteria handrails installed
 - Fire Protection rough in lower A

- **Week ending Friday, February 14th, 2020**
 - Painting in cafeteria addition
 - Trim in cafeteria addition
 - Stair nosing for cafeteria addition

Weekly Project Report

February 10th, 2020

St. Francis High School

- **Week ending Friday, February 7th, 2020**
 - Coaches Locker room ceiling installed
 - Locker room grab bar installation
 - Upper K removed lighting and demoed outlets for future demo
 - Area F Installed 4 door frames
 - Saw cut floor in area F for plumbing
 - Area F plumbing rough in

- **Week ending Friday, February 14th, 2020**
 - Install remaining door frames in area F
 - Install steel beam in choir flex room area F
 - Cement block install around door frames in area F
 - Begin wall tile in area C
 - Install finishing items in bathrooms area C
 - Electrical Demo in upper area K

Early Childhood Family Center

- **Week ending Friday, February 7th, 2020**
 - Soils investigation complete

- **Week ending Friday, February 14th, 2020**
 - Soils report in progress
 - Plan review in progress

Cedar Creek Elementary School


- **Week ending Friday, February 7th, 2020**
 - Plan pre-construction meeting

- **Week ending Friday, February 14th, 2020**
 - Pre-construction meeting week of the 24th
 - Plan review in progress


Weekly Project Report

February 10th, 2020

Progress Photos:

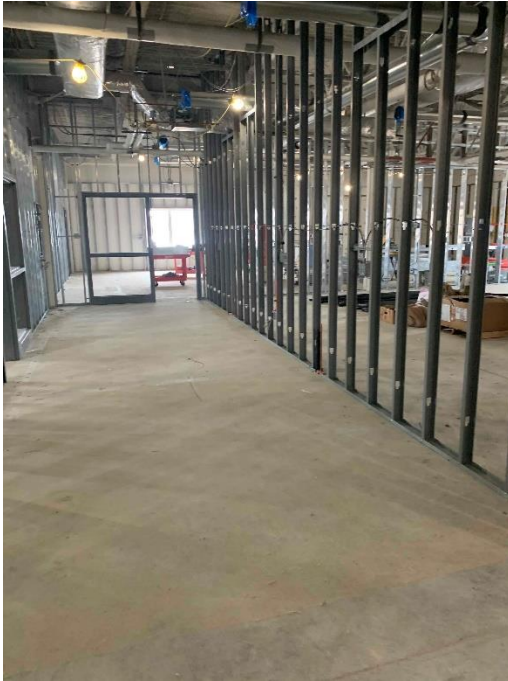


SFMS Metal stud walls upper A

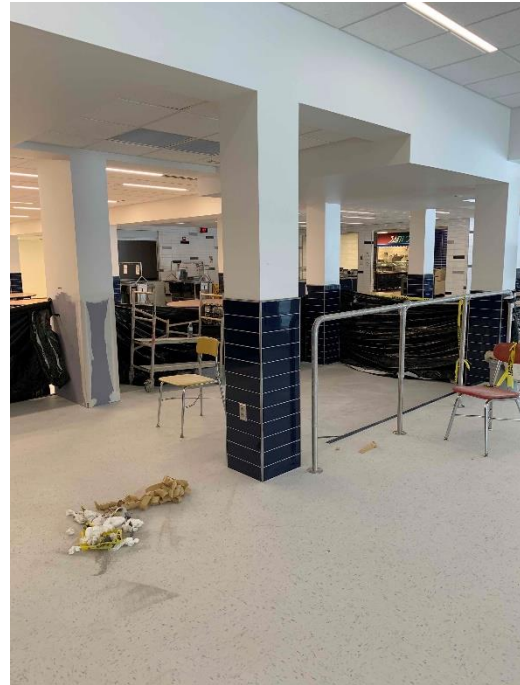

SFMS Cafeteria addition railings installed



SFMS cafeteria addition paint and tile

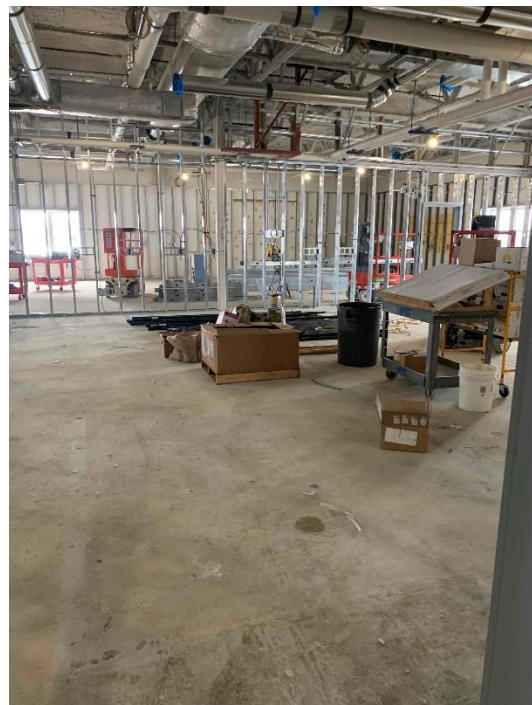

SFMS Upper A Metal Stud Walls

Weekly Project Report

February 10th, 2020

Progress Photos:



SFHS Weight room window openings



SFHS Band/Choir door frame install



SFHS ceiling install



SFES Classroom setup with smart TVs

Weekly Project Report

February 10th, 2020



EBES Media Center Furnished

End of Report
