
	<p align="center">ICS Weekly Project Report February 17th, 2020</p>
	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

East Bethel Elementary School

- **Week ending Friday, February 14th, 2020**
 - Vinyl Base in area A
 - Door hardware patching
 - Acoustic panels in Cafeteria painted
 - Media Center door installation
 - Casework repairs throughout school
 - Door hardware installation
- **Week ending Friday, February 21st, 2020**
 - Contractors to complete work over Spring Break
 - Cafeteria VCT replacement
 - Terrazzo Patching near front entrance
 - 2 hr fire wall in area A repair

St. Francis Elementary School

- **Week ending Friday, February 14th, 2020**
 - Owner Training
- **Week ending Friday, February 21st, 2020**
 - RTX low voltage in hallway to office/mailroom
 - Dimmer light switch change

St. Francis Middle School

- **Week ending Friday, February 14th, 2020**
 - Painting in Cafeteria Addition
 - Cafeteria addition turnover
 - Metal stud walls upper area A
 - Trim in cafeteria addition
- **Week ending Friday, February 21st, 2020**
 - Continue metal stud framing in area A
 - Install drywall in upper area A
 - Area A lower level floor mitigation
 - Begin painting in Lower area A
 - Window installation in maker lab

Weekly Project Report

February 10th, 2020

St. Francis High School

- **Week ending Friday, February 7th, 2020**
 - Installation of remaining door frames in area F
 - Installation of steel beam in choir room area F
 - Cement block installation around door frames in area F
 - Wall tile install in area C
 - Electrical Demo in upper area K

- **Week ending Friday, February 14th, 2020**
 - Saw cut outside wall for paint booth
 - Finish stud walls in area F
 - Continue structural work in choir/band area
 - Locker room water proofing
 - Continue locker room tile installation

Early Childhood Family Center

- **Week ending Friday, February 7th, 2020**
 - Soils report in progress
 - Plan review in progress

- **Week ending Friday, February 14th, 2020**
 - Plan review continued

Cedar Creek Elementary School

- **Week ending Friday, February 7th, 2020**
 - Plan review in progress

- **Week ending Friday, February 14th, 2020**
 - Pre-construction meeting week of the 24th
 - Plan review continued

Weekly Project Report

February 10th, 2020

Progress Photos:



SFMS Temp wall in area A



SFMS Cafeteria addition



SFMS cafeteria addition railing and step complete



SFMS Upper A Metal Stud Walls North Classrooms

Weekly Project Report

February 10th, 2020

Progress Photos:




SFHS upper area K demo



SFHS Area F block wall and I beam



SFHS Area B mezzanine work

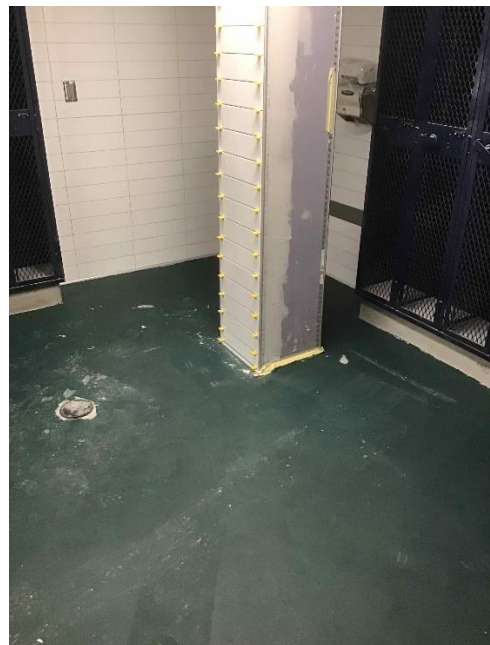

SFHS locker room waterproofing

Weekly Project Report
February 10th, 2020

End of Report
