
	<p align="center"><b>ICS Weekly Project Report</b> February 24, 2020</p>
	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

### **East Bethel Elementary School**

- **Week ending Friday, February 21st, 2020**
  - Acoustical Panel Repair
  - Door hardware installation in kitchen
  - Media center door hardware
  - Food storage ceiling installed
  - FRP installed in kitchen storage
  - Fire strobe lowered in kitchen storage
  
- **Week ending Friday, February 28th, 2020**
  - Basketball backboard corrected
  - ICS working on door repair
  - Contractors to complete work over Spring Break
    - Cafeteria VCT Replacement
    - Terrazzo patching near front entrance
    - 2 hr fire wall in area A repair

### **St. Francis Elementary School**

- **Week ending Friday, February 21st, 2020**
  - Dimmer light switch changes complete
  - RTX low voltage in hallway to office/mailroom
  - Ribbon Cutting Ceremony
  
- **Week ending Friday, February 28th, 2020**
  - Owner training
  - Exterior caulking front entry and west wall
  - RTX low voltage work on exterior doors

# Weekly Project Report

February 24th, 2020

## **St. Francis Middle School**

- **Week ending Friday, February 21st, 2020**
  - Grid placement in lower area A
  - Plumbing work in lower area A
  - Electrical exit signing work lower area A
  - Metal stud install in upper area A
  - Electrical rough-in in upper area A
  - Fire suppression rough-in upper area A
  - Hanging light fixtures-in lower area A
  
- **Week ending Friday, February 28th, 2020**
  - Continue metal stud installation in upper A
  - Continue grid install in lower area A
  - Drywall and taping in upper area A
  - Order tile for cafeteria
  - Electrical and Mechanical rough-in upper A

## **St. Francis High School**

- **Week ending Friday, February 21st, 2020**
  - Painting frames in kitchen area E
  - Installed floor tile in coach's locker room
  - Electrical work in area F
  - Removed old concrete floor in area F
  - Install door frames and steel studs in area F
  
- **Week ending Friday, February 28th, 2020**
  - Masonry work in area F
  - Electrical rough-in area F
  - Duct work area F
  - Floor prep area F
  - Ceiling grid in school store
  - Floor prep in school store

# Weekly Project Report

February 24th, 2020

## **Early Childhood Family Center**

- **Week ending Friday, February 21st, 2020**
  - General Contractor sub-contracts to be issued.
- **Week ending Friday, February 28th, 2020**
  - ICS working with General Contractor to plan pre-construction meeting

## **Cedar Creek Elementary School**

- **Week ending Friday, February 21st, 2020**
  - General Contractor sub-contracts to be issued.
- **Week ending Friday, February 28th, 2020**
  - ICS working with General Contractor to plan pre-construction meeting

# Weekly Project Report

February 24th, 2020

## Progress Photos:




SFES Ribbon Cutting Ceremony



SFES Students and Staff Celebrating



SFHS fitness room area B

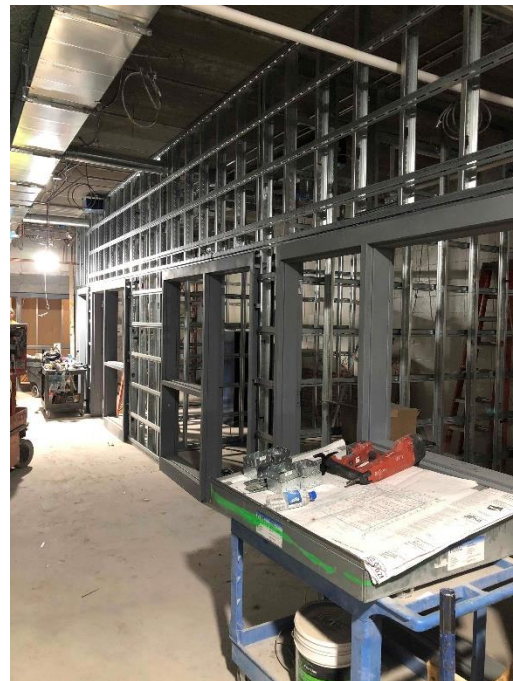


SFHS metal studs in area F

# Weekly Project Report

February 24th, 2020

## Progress Photos:

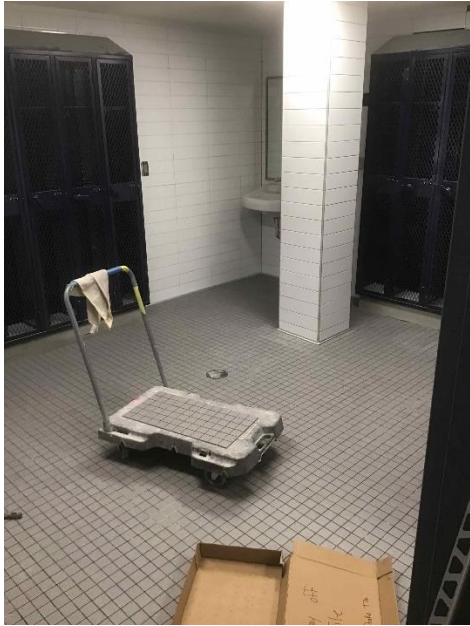


SFHS Locker room tile install



SFHS Area F metal stud walls




SFMS Metal stud walls upper A

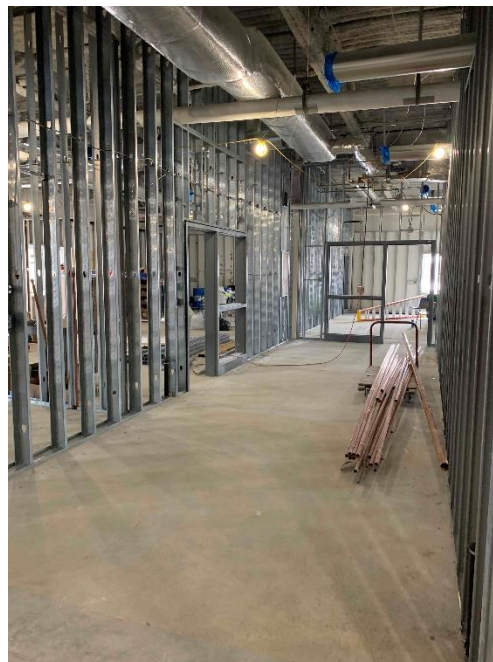

SFMS Metal studs south upper A

# Weekly Project Report

February 24th, 2020

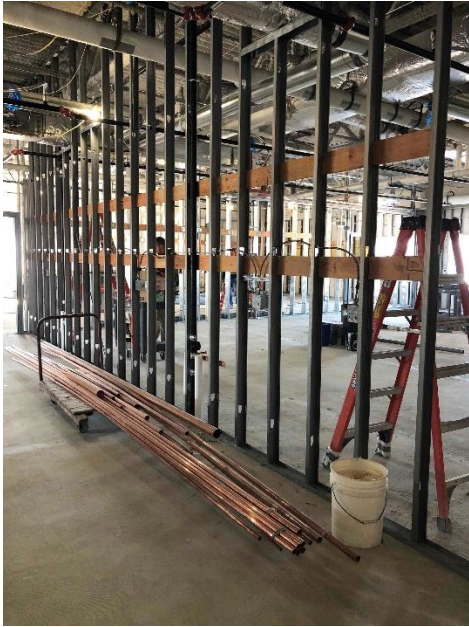

SFMS Electrical rough-in



SFMS area A water fountain rough-in

End of Report
