
	<p align="center"><b>ICS Weekly Project Report</b> March 9th, 2020</p>
	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

### **East Bethel Elementary School**

- **Week ending Friday, March 6th, 2020**
  - Cafeteria floor prep
- **Week ending Friday, March 13th, 2020**
  - Cafeteria VCT Replacement
  - Terrazzo patching near front entrance
  - 2 hr fire wall in area A repair
  - Misc. Painting
  - Door Hardware Correction
  - Misc Painting
  - SPED door hinge correction
  - Eye hook trim install
  - Low voltage lighting control
  - Locker Corrections

### **St. Francis Elementary School**

- **Week ending Friday, March 6th, 2020**
  - RTX low voltage work on exterior doors
  - Owner Training Completed
- **Week ending Friday, March 13th, 2020**
  - Lighting Control Work
  - Sliding Glass Corrections
  - RTX low voltage complete loading dock door
  - Pull up bar location swap in SPED
  - Gym Striping
  - Camera/lighting wiring

# Weekly Project Report

March 9th, 2020

## **St. Francis Middle School**

- **Week ending Friday, March 6th, 2020**
  - VCT in lower A complete
  - Carpeting in area A flex complete
  - Casework in lower A installed
  - Locker Bases installed
  - Begin drywall in upper A
  - Mechanical and Electrical work in upper A
- **Week ending Friday, March 13th, 2020**
  - Plumbing correction area E
  - Furniture move in for Area A and SPED
  - Locker Delivery and Install
  - Lower A classroom setup
  - Paint, sand, and tape in upper A
  - Furniture Install flex area A

## **St. Francis High School**

- **Week ending Friday, March 6th, 2020**
  - Area F masonry work
  - Electrical rough-in area F
  - Duct work Area F
  - Flooring in school store
  - Ceiling grid in school store
- **Week ending Friday, March 13th, 2020**
  - Electrical shutdown for power transfer

# Weekly Project Report

March 9th, 2020

## **Early Childhood Family Center**

- **Week ending Friday, March 6th, 2020**
  - Sub-Contracts issued
  
- **Week ending Friday, March 13th, 2020**
  - ICS working with General Contractor to plan pre-construction meeting

## **Cedar Creek Elementary School**

- **Week ending Friday, March 6th, 2020**
  - Sub-Contracts issued
  - Pre-Construction meeting Friday March 6<sup>th</sup>
  
- **Week ending Friday, March 13th, 2020**
  - Contractors in school doing pre-construction walk throughs

# Weekly Project Report

March 9th, 2020

## Progress Photos:



SFHS Demolition



SFHS Area F masonry wall



SFHS Electrical Work



SFHS Metals Lab window cutout

# Weekly Project Report

March 9th, 2020

## Progress Photos:



SFHS brick install at fitness area



SFMS area A classroom substantially complete



SFMS Locker Bases Install



SFMS Metal Stud Walls Upper A



# Weekly Project Report

March 9th, 2020




SFMS Upper A drywall install



SFMS door frame install upper A



SFMS Upper A water fountain rough in

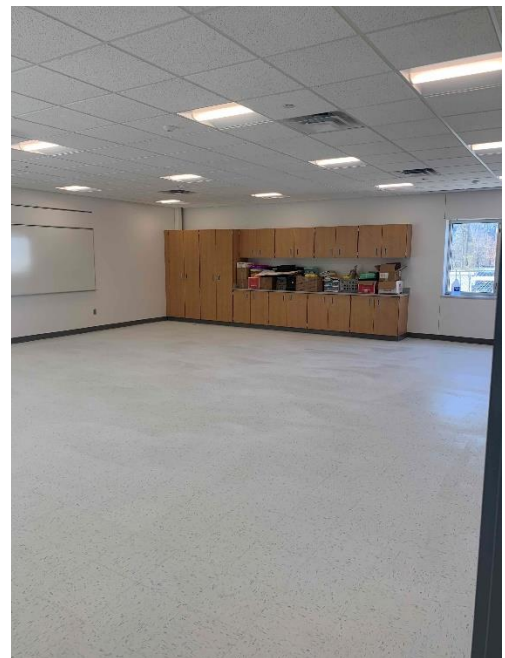

SFMS Area F classroom

End of Report
