



Board Meeting: April 27, 2020



Bond 2017 Update

Administration Building Renovations

Additional Projects Update



Bond 2017 – Leadership Support Center



Bond 2017 – Leadership Support Center



Bond 2017 – Leadership Support Center



Bond 2017 – Leadership Support Center



Bond 2017 – Leadership Support Center



Leadership Support Center Concrete Piers and Grade Beams



Bond 2017 – Leadership Support Center



Leadership Support Center – Concrete Piers and Grade Beams



Bond 2017 – Leadership Support Center



Leadership Support Center Concrete Piers and Grade Beams



Bond 2017 – Leadership Support Center



Bond 2017 – Leadership Support Center



Bond 2017 – Leadership Support Center



Bond 2017 – Leadership Support Center



Bond 2017 – Leadership Support Center



Perry Road Extension In Progress



PROJECT SCHEDULE

Package 1: Demolition, Earthwork, Building Pad and Underground Utilities

- Demolition – Complete January 15th – March 15th 2020

Package 2: Foundation, Structural Steel Purchase and MEP Underslab

- Building Pad: Completed on Schedule:
- Drill & Pour Foundation Piers/Grade Beams In Progress – on Schedule:
- Construction Start through Completion: March 2nd – June 15th 2020

Package 3: Remaining Building Package


- 90% Construction Documents Issue for Proposal: April 6th 2020
- Issue for Permit: April 9th 2020
- Develop GMP present to BOT for Approval/Award: May 18th 2020
- Construction Start through Substantial Completion: May 19th 2020 - June 15th 2021
- Move – In: July 15th 2021

ADDITIONAL PROJECTS

- **ADDITIONAL PROJECT UPDATES:**
- SUMMER PROJECTS STARTING UP:
 - MSS RENOVATIONS – INCLUDING ART ROOM, WEIGHT ROOM, BOYS & GIRLS COACHES OFFICES & LOCKER ROOMS, BUILDING PAINT AND VINYL GRAPHICS PACKAGE;
 - ECC – ADDITIONAL SHARED PARKING LOT WITH ESN, ADDITIONAL CANOPIES AND PAVING, COUNSELOR OFFICE/RECORD STORAGE MODIFICATION;
 - HS THEATER – SEATING AND FLOORING RENOVATIONS – PENDING SEATING PRODUCTION CURRENTLY ON HOLD IN MICH.;
 - PRIMARY BUILDING ASSESSMENT FOR POSSIBLE INSTRUCTIONAL USE NEXT SCHOOL YEAR – WILL ADDRESS AT MAY BOARD MEETING IF GOING FORWARD;
- BOND 2020: ESN – ESS ADDITIONS EARLY RELEASE PACKAGE 1 (DEMO) – MAY BOARD MEETING FOR GMP APPROVAL
- BOND 2020 – IS NORTH & SOUTH COMPLETING SCHEMATIC DESIGN THIS WEEK;


**INTERMEDIATE SCHOOL
NORTH
PRELIMINARY SCHEMATIC DESIGN**

BOND 2020 INTERMEIDATE NORTH & SOUTH SCHEMATIC DESIGNS

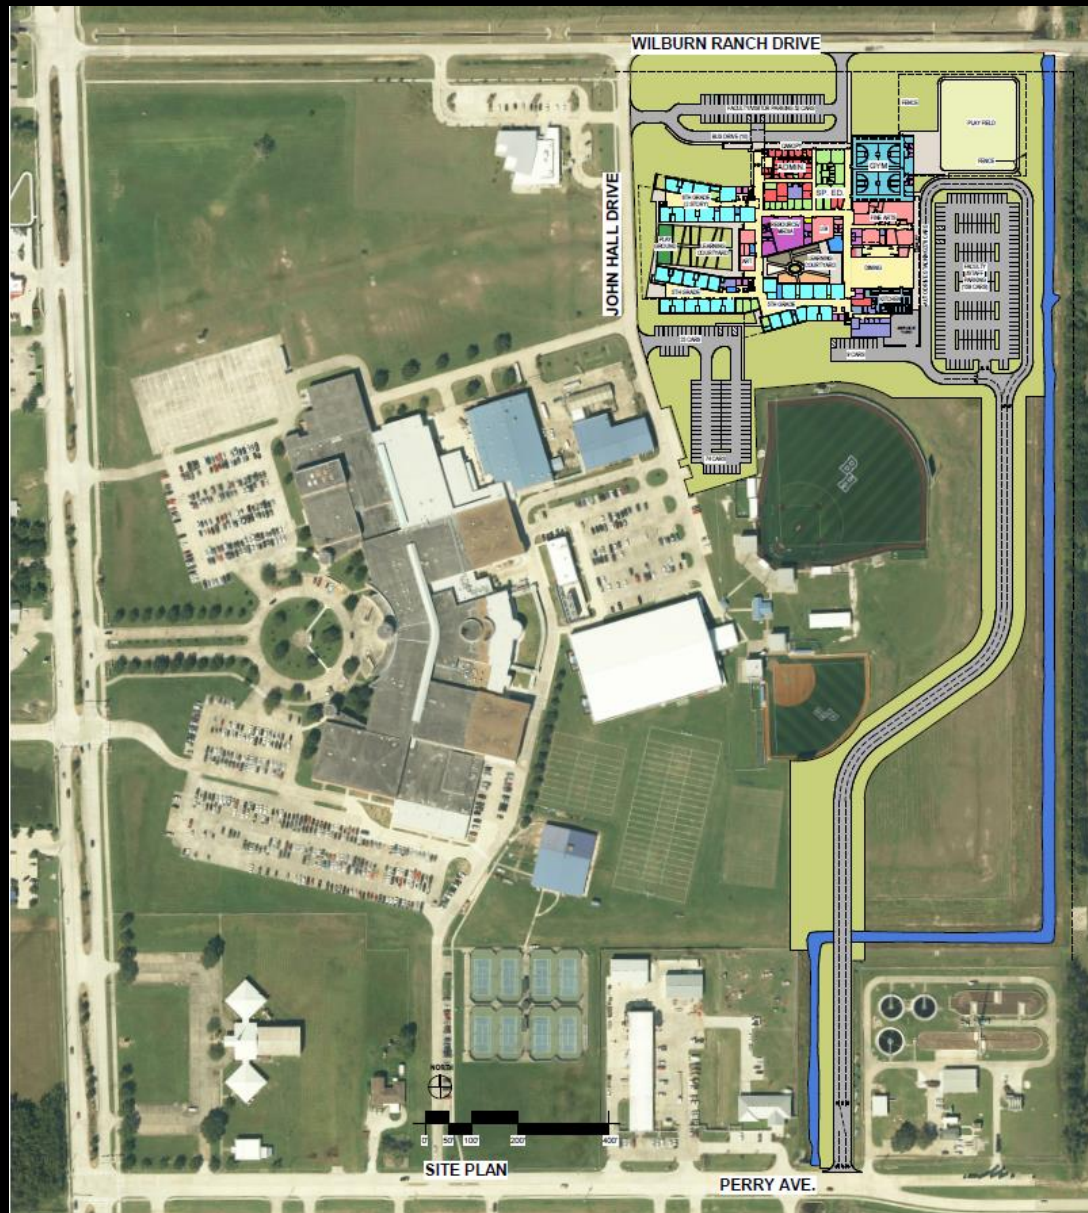


INTERMEDIATE SCHOOL NORTH

BOND 2020 INTERMEIDATE NORTH & SOUTH SCHEMATIC DESIGNS

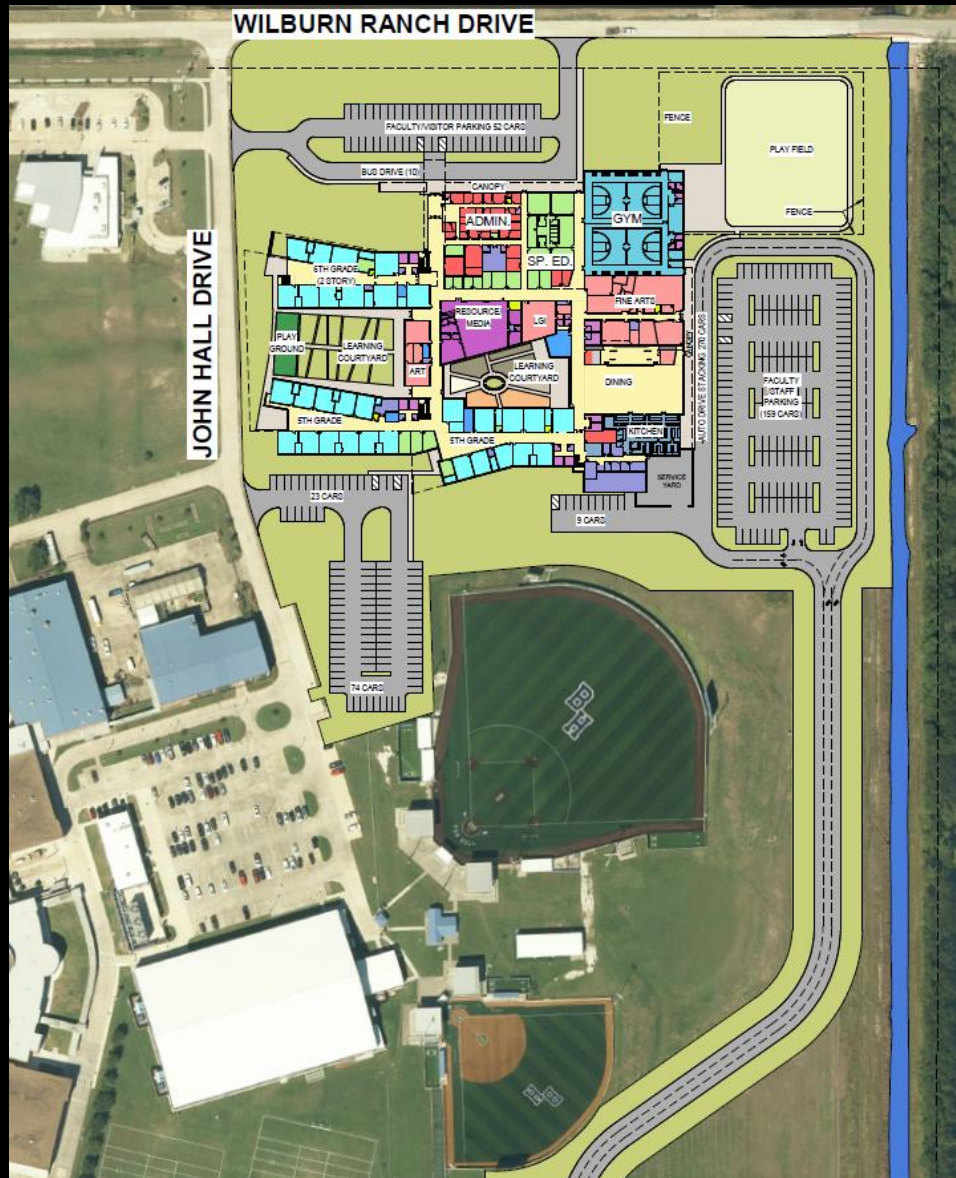

INTERMEDIATE SCHOOL NORTH

BOND 2020 INTERMEIDATE NORTH & SOUTH SCHEMATIC DESIGNS

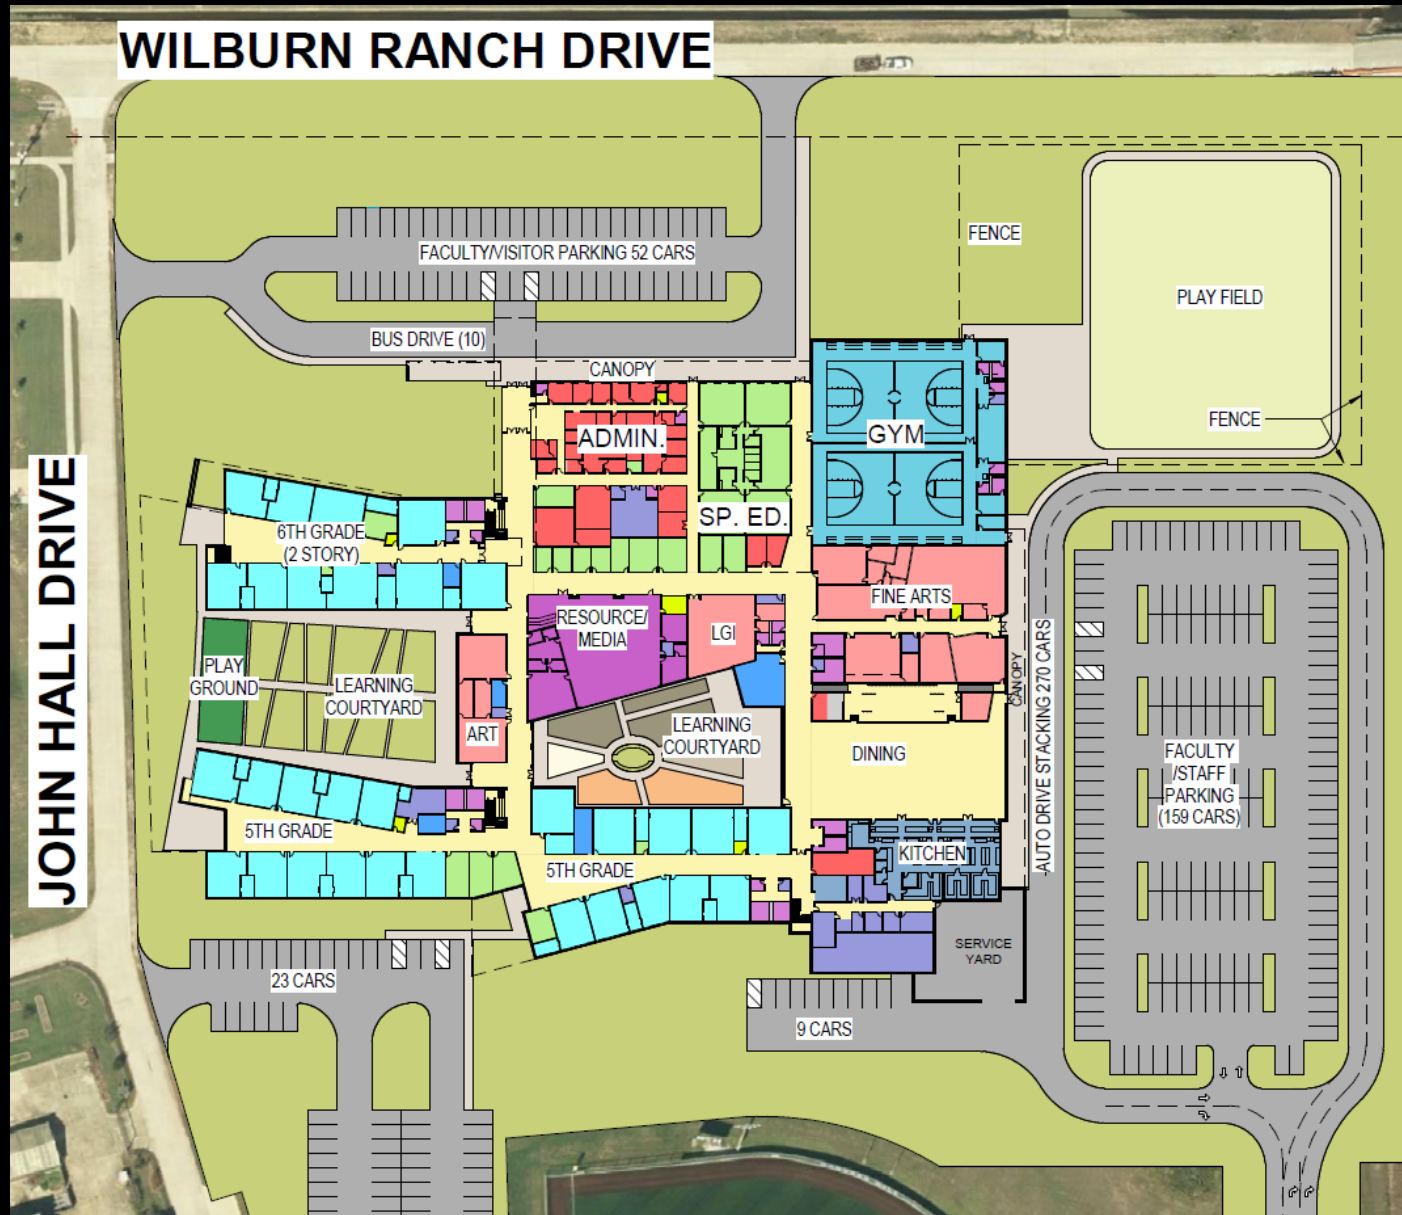

INTERMEDIATE SCHOOL NORTH

**INTERMEDIATE SCHOOL
SOUTH
PRELIMINARY SCHEMATIC DESIGN**

BOND 2020 INTERMEIDATE NORTH & SOUTH SCHEMATIC DESIGNS



INTERMEDIATE SCHOOL SOUTH

BOND 2020 INTERMEIDATE NORTH & SOUTH SCHEMATIC DESIGNS



INTERMEDIATE SCHOOL SOUTH

Bond 2017 – Leadership Support Center



Thank You

