











	<p align="center">ICS Weekly Project Report April 28th, 2020</p>
 	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

St. Francis Middle School

Week ending Friday, April 24th, 2020



-  Science classroom countertops being installed area A
-  Demo in areas B and C
-  Plumbing work in Gym Locker rooms
-  Window replacement in area
-  Complete cafeteria column tile

Week ending Friday, May 1st, 2020



-  Ceilings being installed in lower area A
-  Ceramic tile installed in bathroom in upper area A
-  Science classroom countertops still being installed in upper area A
-  Floor cutting and mitigation in areas C & D
-  Shoring in areas C & D

East Bethel Elementary School

Week ending Friday, April 24th, 2020

-  Finishing up mechanical identification
-  Electrical work for sensory room

Week ending Friday, May 1st, 2020

-  Awaiting pricing for card reader hookups
-  Installing glazing that arrived for kitchen door

St. Francis Elementary School

-  Sitework package under review and redesign

Weekly Project Report

April 28th, 2020

St. Francis High School

Week ending Friday, April 24th, 2020

- ☒ VCT install upper K
- ☒ Working on exterior grading area B
- ☒ Demo walls in area B
- ☒ Begin to remove lights and fire alarms from upper J
- ☒ Demolition of walls in upper J
- ☒ Fire protection wire to get installed around the school and new heating wires to VAVs
- ☒ Removal of existing unused wire throughout school
- ☒ Finish taping fire wall in wrestling room.
- ☒ Finish taping and drywall in band and choir room area F

Week ending Friday, May 1st, 2020

- ☒ Painting walls in band/choir rooms and prepping floors for VCT
- ☒ Set up shoring for removing walls in area B
- ☒ Removal of toilets of Upper J
- ☒ Removing ceiling and grid, electrical and start of demo in upper J
- ☒ Installing block around new door openings in area A

Early Childhood Family Center

Week ending Friday, April 24th, 2020

- ☒ Tree removal to begin
- ☒ High density units removed from portables

Week ending Friday, May 1st, 2020

- ☒ Finishing install of perimeter fence
- ☒ Preparing for demo to start week of May 4th

Weekly Project Report

April 28th, 2020

Cedar Creek Elementary School


Week ending Friday, April 24th, 2020

- ☞ Continue Demo in areas A/D
- ☞ Begin metal partitions in area D
- ☞ Saw cutting for plumbing and electrical rough-in

Week ending Friday, May 1st, 2020

- ☞ Metal wall framing of area D

Progress Photos:

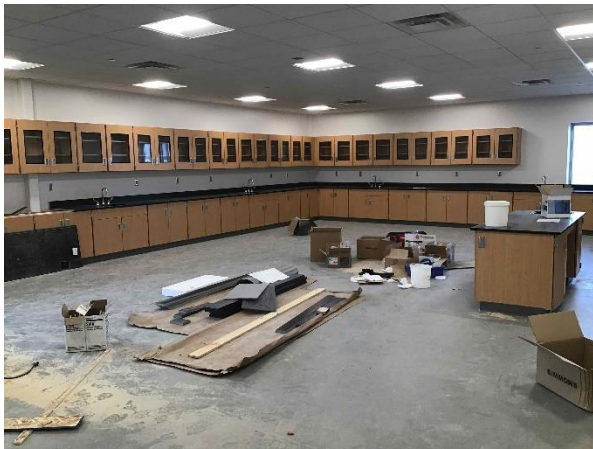

SFMS – Science classrooms continue to be installed



SFMS – Concrete finished in gym locker rooms

Weekly Project Report


April 28th, 2020



SFMS – ceramic tile being installed in bathroom in upper Area A



SFHS – Band/Choir rooms starting paint and floor prep

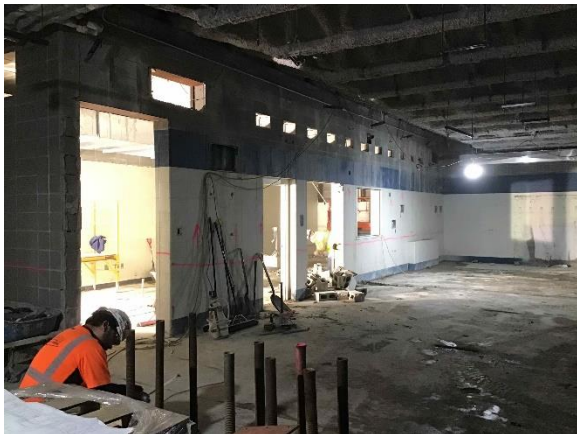

SFHS – Area B Locker Room Demo



SFHS – Wrestling room ceiling tiles installed

Weekly Project Report

April 28th, 2020



CCES – Saw cutting for plumbing rough-in in Area D



CCES – Prepping for metal wall installation in Area D

End of Report
