










	<p align="center">ICS Weekly Project Report May 19th, 2020</p>
 	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

St. Francis Middle School

Week ending Friday, May 15th, 2020



-  Tiling hallway of upper A
-  Install ceiling of lower A
-  Drywall and finishes in locker room showers
-  Area D Demo plumbing, mechanical, and casework
-  Upper area C&D install VCT

Week ending Friday May 22nd, 2020

-  Finish clean of Lower A and complete punch list for that area
-  Drywall finished in Showers
-  Painting of locker rooms
-  Tile wall and floor of locker rooms

East Bethel Elementary School


Week ending Friday May, 15th, 2020

-  Meet with contractor on site to see if new design for bar joist will work
-  Awaiting covers for Eyebolts

Week ending Friday May 22nd, 2020

-  Working on Completion of final punch list items

St. Francis Elementary School

-  Sitework package design being reviewed by Planning and Zoning

Weekly Project Report

May 19th, 2020

St. Francis High School

Week ending Friday May 15th, 2020

- ☒ Demo is continuing in lower and upper J
- ☒ Area F painting and HVAC
- ☒ Area A locker room Demo
- ☒ Area B locker room/new fitness area demo
- ☒ Room finishes in area K

Week ending Friday May 22nd, 2020

- ☒ Continuing HVAC in Area F
- ☒ Framing walls in Upper J
- ☒ 5/6 classrooms in Area K turned back to owner
- ☒ Continuing demo of Lower J
- ☒ Shoring and demo continuing in Area B
- ☒ Underground plumbing in Area A locker rooms

Early Childhood Family Center

Week ending Friday, May 15th, 2020

- ☒ Pole adjustment by 3rd party vendor
- ☒ Demo of interior of building
- ☒ Plumbing demo of building
- ☒ HVAC demo of building

Week ending Friday May 22nd, 2020

- ☒ Finish Demo of building
- ☒ X-ray, saw-cut and remove concrete on South end
- ☒ Start on new underground plumbing
- ☒ Start on metal wall framing

Weekly Project Report

May 19th, 2020

Cedar Creek Elementary School

Week ending Friday, May 15th, 2020

- ☒ Area A demo of casework and electrical
- ☒ Pour flooring for new bathroom in Area A
- ☒ Finish rough-ins and HVAC in area D
- ☒ Area B new lighting install


Week ending Friday May 22nd, 2020

- ☒ Finish demo in Area A
- ☒ Finish framing new walls in Area A
- ☒ Finish new light install of Area B
- ☒ Begin demo of walls and case work of Area B
- ☒ Being framing of new walls in Area B

Progress Photos:



SFMS – Demo of plumbing, casework, and mechanical in Area D

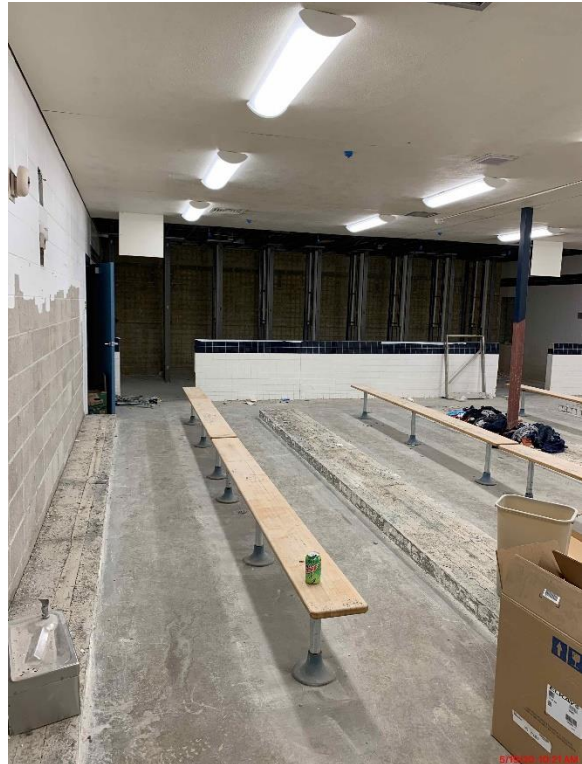

SFMS – Prepping for drywall and finishes to be installed this week

Weekly Project Report

May 19th, 2020



SFHS – Fitness center demo and shoring



SFHS – Locker room in Area A ready for underground plumbing



ECFC – demo of bathrooms and plumbing fixtures



ECFC – demo of partition walls in Indoor Play area

End of Report
