

	<p align="center">ICS Weekly Project Report June 15th, 2020</p>
 	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

St. Francis Middle School

Week ending Friday, June 12th, 2020

- ☞ Install drywall and wall/floor tile in boys/girls locker rooms
- ☞ Continue demo of mechanical/electrical/plumbing in areas C & D
- ☞ Pour footings in areas C & D
- ☞ Demo tile and walls in boys/girls bathrooms upper C & D
- ☞ Paint classrooms in upper C & D
- ☞ Install casework and VCT flooring in upper C & D

Week ending Friday, June 19th, 2020

- ☞ Continue install of wall/floor tile in boys/girls' locker rooms
- ☞ Dig and pour exterior footings around area C & D
- ☞ Continue casework install in upper C & D
- ☞ Continue demo of mechanical/electrical/plumbing in upper C & D
- ☞ Install steel lintels in area E for structural support

East Bethel Elementary School

- ☞ Warranty walk scheduled for mid-summer

St. Francis Elementary School

- ☞ Proposed sitework approved by City of St. Francis City Council. Phase 1 is scheduled to start mid-June.

St. Francis High School

Week ending Friday June 12th, 2020

- ☞ Continue demo of wall for new central staircase opening between J & G
- ☞ Hanging drywall in upper J media center
- ☞ Saw cutting floors in lower J
- ☞ Tiling corridor walls in upper K
- ☞ Pour new footings in area B

Weekly Project Report

June 15th, 2020

Week ending Friday June 19th, 2020

- ☞ Continue tiling corridor walls in upper K
- ☞ Begin running underground utilities in lower area J
- ☞ Rebuild CMU walls and openings in area B fitness center
- ☞ Pour concrete in new locker rooms in areas A & C
- ☞ Finish handing drywall in upper J
- ☞ Rebuild CMU walls and openings for new staircase in area J/G border

Early Childhood Family Center

Week ending Friday June 12th, 2020

- ☞ Demo of new wall openings in area A
- ☞ Continue metal wall framing in areas A & B
- ☞ Complete new wall finishes in gym in area B
- ☞ Flooring demo in bathrooms in area B
- ☞ Concrete infill over underground plumbing in areas A & B
- ☞ Metal wall framing in area C indoor playroom

Week ending Friday June 19th, 2020

- ☞ Pouring new concrete sidewalks on North side of building
- ☞ Removing temporary shoring in area A
- ☞ Backfill holes in slab and pour new concrete in areas A & B
- ☞ Floor mitigation of old concrete in areas A, B, & C
- ☞ Selective asbestos removal in areas A & B

Cedar Creek Elementary School

Week ending Friday June 12th, 2020

- ☞ Hanging drywall in area A classrooms
- ☞ Pouring new concrete over underground plumbing in area A
- ☞ Install lighting and metal wall framing in area C
- ☞ Painting and installing ceiling grid in area D
- ☞ Demo of casework in area F

Weekly Project Report

June 15th, 2020

Week ending Friday June 19th, 2020

- ☞ Hanging drywall in areas B & C
- ☞ Finish demo of plumbing fixtures in all gang bathrooms
- ☞ Finish wall demo in area F
- ☞ Begin metal wall framing in areas E & F
- ☞ Begin electrical rough ins for areas E & F
- ☞ New lighting install in area A

Progress Photos:



SFMS – temporary structural support in upper C & D



SFMS – new fitness room in area B West

Weekly Project Report

June 15th, 2020



SFHS – new finished opening in area B fitness center



SFHS – vapor barrier installed in preparation for new concrete in boys' locker room area A



ECFC – digging out for vestibule alterations in area A




ECFC – new curb complete, bus loop is ready to for pavement

Weekly Project Report

June 15th, 2020



CCES – area a classroom drywall is complete

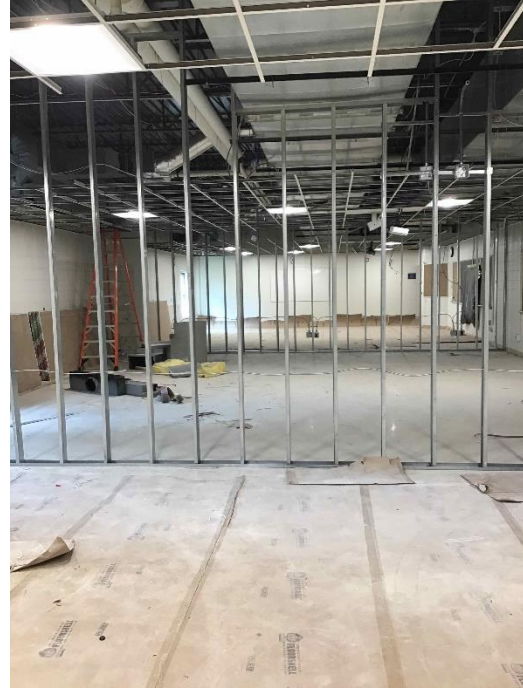

CCES – Area C classroom metal studs are installed

End of Report
