

	ICS Weekly Project Report May 08, 2020
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Centennial Elementary

- Ⓜ Completed week ending Friday, May 8, 2020
 - Completed packing and moving efforts throughout the building.
 - Completed an on-site coordination meeting with District Food Services and Trimark (Kitchen Eq. contractor).
 - Completed plumbing fixture demolition in all of Area A.
 - Abatement contractor continued flooring and chalkboard removal.
 - Completed hanging and taping of drywall in the former Media Center area.
 - Completed MEP rough-in in the former Media Center area.
 - Completed mechanical insulation in the former Media Center area.

- Ⓜ Planned week ending Friday, May 15, 2020
 - Continue electrical rough-in at the new transformer location.
 - Begin painting in the former Media Center area.
 - Abatement contractor to complete remaining abatement scope.
 - Continue plumbing fixture demolition in Area B.
 - Continue MEP demo in Area A.
 - Begin MEP rough-in in Area A.

Middle School

- Ⓜ Completed week ending Friday, May 8, 2020
 - Moved third floor existing classroom furniture into storage trailers
 - Finished abatement on third floor
 - Started abatement on main level
 - Finished mechanical and electrical rough ins in the Media Center
 - Finished drywall in the Media Center
 - Started putting floor protection down in corridors

- Ⓜ Planned week ending Friday, May 15, 2020
 - Finish abatement on main level
 - Start demolition on third level
 - Install locker protection

	ICS Weekly Project Report May 08, 2020
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Move existing furniture out of second and main level

Sheridan Hills Elementary

- Ⓜ Completed week ending Friday, May 8, 2020
 - District staff continued packing efforts in anticipation of the renovation.
 - District IT began removing technology items from rooms in anticipation of the renovation.
 - Material submittals continue to be submitted and reviewed.
 - Corval Constructors installed temporary fencing around the staging areas.

- Ⓜ Planned week ending Friday, May 15, 2020
 - Abatement contractor to begin flooring, chalkboard and pipe insulation removal in Area C.
 - District IT to continue removal of technology items.
 - Corval Constructors to continue mobilization efforts and begin installing temporary protection throughout the building.

High School

- Ⓜ Completed week ending Friday, May 8, 2020
 - Area C (new IT tech space/health classroom/flex)
 - Finish low voltage and punch list items
 - Area C (third floor conference room)
 - Completed mechanical and electrical finishes
 - Finish wall tile and punch list
 - Old courtyard (expanded commons)
 - Finished polishing of terrazzo flooring
 - Front Entrance Stair Tower
 - Punch list and final clean
 - Area P
 - Continued above grade masonry wall installation
 - Started underground sewer work
 - Area D and E Bathrooms
 - Mechanical and electrical rough ins for Area D

	ICS Weekly Project Report May 08, 2020
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Sheetrocked walls in Area D
- Old Concession Stand
 - Completed room finishes and punch list.
- Old Board Room
 - Finished mechanical and electrical rough ins.
 - Started drywall work
- Lower Level Area F (Old locker rooms, new weight room)
 - Started demolition
- Area G/H 1st and 2nd Level (Classrooms)
 - Demolition
 -

Ⓜ Planned week ending Friday, May 15, 2020

- Area P Link
 - Continue exterior masonry walls
 - Finish sewer work
- Area D and E Bathrooms
 - Mechanical and electrical rough ins for Area D
 - Sheetrocking walls in Area D
- Old Concession Stand
 - Ceiling work and final clean.
- Old Board Room
 - Finish drywall work
 - Start painting
- Lower Level Area F (Old locker rooms, new weight room)
 - Continue demolition
- Area G/H 1st and 2nd Level (Classrooms)
 - Start wall framing
 - Mechanical and electrical rough ins

STEM

Ⓜ Completed week ending Friday, May 8, 2020

- Old Admin area (New Classrooms)
 - Continued glazed block wall installation and patching

	ICS Weekly Project Report May 08, 2020
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Started demolition in the main level music suites

Ⓜ Planned week ending Friday, May 15, 2020

- Continue demolition of music suite and kindergarten classrooms
- Abatement in boiler room

Dual Language

Ⓜ Completed week ending Friday, May 8, 2020

- Punch list items continue to be addressed.
- Resumed testing and balancing efforts of the mechanical & HVAC system.
- ICS Commissioning continued commissioning efforts.

Ⓜ Planned week ending Friday, May 15, 2020

- Continue to address punch list items.
- Continue testing and balancing of the mechanical/HVAC system.
- ICS Commissioning to continue commissioning efforts.



ICS Weekly Project Report
May 08, 2020



RICHFIELD
PUBLIC SCHOOLS

ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423

CURRENT PROJECT PHOTOS

Centennial – Kitchen has been packed and existing equipment has been tagged.



Centennial – Abatement efforts continued.



	<p>ICS Weekly Project Report May 08, 2020</p>
 <p>RICHFIELD PUBLIC SCHOOLS</p>	<p>ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423</p>

Centennial – Drywall hanging and taping progress in the former Media Center area.



Sheridan Hills – Packing and moving efforts continued.



Sheridan Hills – Corval Constructors installed temp. fencing around the job-site trailer/staging area.





ICS Weekly Project Report
May 08, 2020



RICHFIELD
PUBLIC SCHOOLS

ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423


High School – Front Entrance and New Stair Tower



High School – 1st Level and 3rd Level Area C (IT, Health Classroom, Flex)



High School – Area D Bathrooms and Flex Space

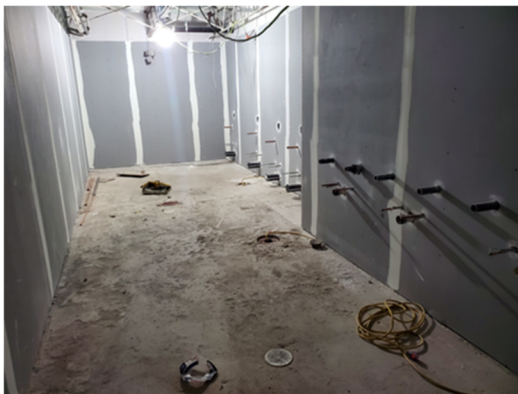



ICS Weekly Project Report
May 08, 2020



RICHFIELD
PUBLIC SCHOOLS

ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423

High School – Area P Link



High School-Lower Level Locker Room and Third Level Science Classroom Demolition



STEM – Music Suite Demolition





ICS Weekly Project Report
May 08, 2020



RICHFIELD
PUBLIC SCHOOLS

ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423

Middle School – Classroom Abatement and Demolition



Middle School – Floor Protection

