

	<b>ICS Weekly Project Report</b> June 5, 2020
	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

## Centennial Elementary

- Ⓡ Completed week ending Friday, June 5, 2020
  - Electrical connection cabinet placed on the exterior prefabricated pad.
  - Electrical main switchboard cabinet installed.
  - Wall finishes completed in the Special Ed. Suite.
  - Began acoustical ceiling grid install in the Special Ed. Suite.
  - Began concrete slab saw-cutting in the Boiler Room.
  - Began painting in the classrooms and corridors.
  - Completed metal stud framed walls in the Resource/Flex Classrooms (Area A)
- Ⓡ Planned week ending Friday, June 12, 2020
  - Complete concrete slab saw-cutting in the Boiler Room.
  - Continue above ceiling mechanical and electrical as well as underground electrical in the Media Center.
  - Continue acoustical ceiling grid installation in the Special Ed. Suite.
  - Continue mechanical and electrical rough-in in the Resource area.
  - Continue wall finishes throughout the classrooms and corridors.

## Middle School

- Ⓡ Completed week ending Friday, June 5, 2020
  - Ductwork demolition on 2<sup>nd</sup> and 3<sup>rd</sup> floor
  - Demolition of walls and soffits on 3<sup>rd</sup> floor
  - Framing walls and soffits on 2<sup>nd</sup> floor stairwell entrances
  - Mechanical and electrical rough ins in 2<sup>nd</sup> floor classrooms
  - Wall framing and drywall work in Media Center
- Ⓡ Planned week ending Friday, June 12, 2020
  - Removal and demolition of classroom louvers
  - Continue framing walls and soffits on 2<sup>nd</sup> floor stairwell entrances
  - Continue mechanical and electrical rough ins in 2<sup>nd</sup> floor classrooms
  - Wall framing and drywall work in Media Center
  - Start mechanical and electrical rough ins on 3<sup>rd</sup> floor
  - Start framing walls and soffits on 3<sup>rd</sup> floor stairwell entrances

	<b>ICS Weekly Project Report</b> June 5, 2020
	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

## Sheridan Hills Elementary

- Ⓡ Completed week ending Friday, June 5, 2020
  - Completed Level 2 C wing demolition.
  - Abatement contractor continued flooring and insulation removal in the Level 1 restrooms.
  - Completed architectural demo in the Level 1 restrooms.
  - Completed acoustical ceiling demolition in the Level 1 corridors.
  - Continued above ceiling mechanical and electrical rough-in the Level 2 C wing.
  - Begin masonry and hollow metal frame demo on Level 1.
- Ⓡ Planned week ending Friday, June 12, 2020
  - Complete excavation for footings and foundations at the Front Entrance expansion.
  - Begin footings and foundations at the Front Entrance expansion.
  - Continue mechanical and electrical rough-in in Level 2 C wing.
  - Continue mechanical and electrical rough-in in the future Front Admin Office.
  - Demo acoustical ceilings in the existing Admin Office,

## High School

- Ⓡ Completed week ending Friday, June 5, 2020
  - Boiler Room
    - Continued mechanical and electrical connections of the boilers
  - Area P Link
    - Finished exterior wall and removed scaffolding
  - Area D and E Bathrooms
    - Finished tile work
  - Old Concession Stand
    - Ductwork and ceiling work
  - Old Board Room
    - Punch list work and cleaning
  - Lower Level Area F (Old locker rooms, new weight room)
    - Mechanical and electrical rough ins
    - Build interior masonry walls
    - Wall sawing

	<b>ICS Weekly Project Report</b> June 5, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Set door and frames
- 2<sup>nd</sup> and 3<sup>rd</sup> level science rooms
  - Mechanical and electrical rough ins
- Old Special Ed./New Athletics Commons
  - Drywall work
  - Painting and ceiling installation
- New Athletic Corridor/Elevator
  - Footings and masonry walls for elevator and storage room
- Area A & B Art and Shop Classes
  - Demolition

Ⓜ Planned week ending Friday, June 12, 2020

- Boiler Room
  - Continue mechanical and electrical connections of the boilers
- Area P Link
  - Structural steel
- Area D and E Bathrooms
  - Start installing plumbing fixtures and painting
- Old Concession Stand
  - Ceiling and floor
- Lower Level Area F (Old locker rooms, new weight room)
  - Continue interior masonry walls
- 2<sup>nd</sup> and 3<sup>rd</sup> level science rooms
  - Mechanical and electrical rough ins
- Old Special Ed./New Athletics Commons
  - Ceiling work and painting
- New Athletic Corridor/Elevator
  - Below grade masonry for elevator and storage room
  - Start tiling in bathrooms
- Area A & B Art and Shop Classes
  - Continue mechanical and electrical demolition
  - Start wall framing

	<b>ICS Weekly Project Report</b> June 5, 2020
	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

## STEM

- Ⓡ Completed week ending Friday, June 5, 2020
  - Wall framing in Special Education suite
  - Electrical work in Special Education suite
  - Set unit ventilators and connections in Music suite
  - Hydronic piping in Special Education and Music suite
  - Set pre-kindergarten unit ventilator
  - Drywall work in pre-kindergarten classroom
  - Abatement in boiler room and tunnel areas
- Ⓡ Planned week ending Friday, June 12, 2020
  - Finish in wall electrical work in Special Education Suite
  - Hydronic piping in Special Education and Music suite
  - Drywall work in Special Education and Music suite
  - Ceiling grid work in main level corridors
  - Bathroom tile work in pre-kindergarten classroom
  - Start demo work in kitchen area
  - Abatement in boiler room and tunnel areas

## Dual Language


- Ⓡ Completed week ending Friday, June 5, 2020
  - Punch list items continue to be addressed.
  - Continued to address mechanical/HVAC test and balance deficiencies.
  - Contractors worked to address action items on the Commissioning Corrective Action Log.
- Ⓡ Planned week ending Friday, June 12, 2020
  - Continue to address punch list items.
  - Continue testing and balancing of the mechanical/HVAC system.
  - ICS commissioning continued commissioning of the mechanical and HVAC systems.



	<b>ICS Weekly Project Report</b> June 5, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

## CURRENT PROJECT PHOTOS

Centennial – Prefab concrete pad and elec. connection cabinet set. New main elec. switchboard.

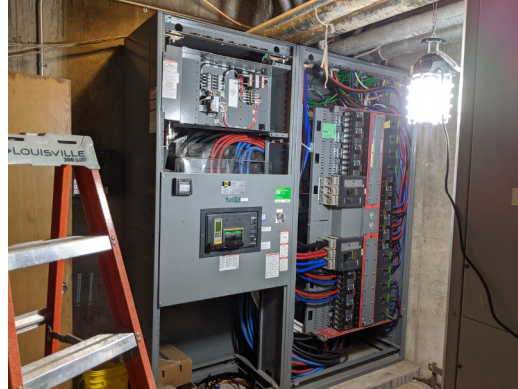

Centennial – Concrete slab saw-cutting in the boiler room and existing kitchen demolition progress.



Centennial – Media above ceiling mech. and underground elect. in progress. Resource area framing.





	<b>ICS Weekly Project Report</b> June 5, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Sheridan Hills – Photos showing typical demolition progress made in Level 1 classrooms.



Sheridan Hills – Existing Staff Lounge and Admin Office demolition progress.



Sheridan Hills – Level 2 classroom demolition complete with HVAC rough-in in progress. Level 2 corridor ceiling demolition complete.



	<b>ICS Weekly Project Report</b> June 5, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423


### High School – New Athletic Commons/Old Special Education



### High School – Second Level Special Education Suites



### High School – Art and Shop Demolition

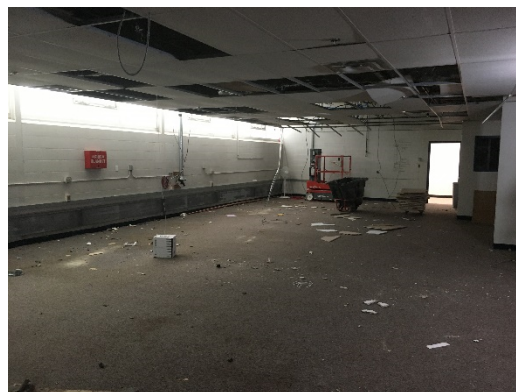



	<b>ICS Weekly Project Report</b> June 5, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

High School – P Link



High School – Lower Level Locker Rooms



High School – Science Classrooms



	<b>ICS Weekly Project Report</b> June 5, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

STEM – Main Level Branding Wall and Lobby



STEM – Kindergarten Classrooms



STEM – Pre - Kindergarten Classroom







## ICS Weekly Project Report

June 5, 2020



**RICHFIELD**  
**PUBLIC SCHOOLS**

ISD #280 Richfield Public Schools  
7001 Harriet Avenue S.,  
Richfield, MN 55423

### STEM – Music and Special Education Suite



	<b>ICS Weekly Project Report</b> June 5, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Middle School – Main Level New Art and Health Classroom



Middle School – Media Center





	<b>ICS Weekly Project Report</b> June 5, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Middle School – Second Floor Stairwell Entrance and Flex Areas



Middle School – Third Floor Resource and Flex Areas

