

	<p align="center">ICS Weekly Project Report June 30th, 2020</p>
 	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

St. Francis Middle School

Week ending Friday June 26th, 2020

- ☞ Complete drywall and plumbing finishes in boys' showers
- ☞ Finish tiling wall/floor in boys'/girls' locker rooms
- ☞ Finish pouring interior and exterior footings in areas C & D
- ☞ Begin steel wall framing in areas C & D
- ☞ Follow wall framing in C & D with mechanical/electrical/plumbing rough ins
- ☞ Hang drywall in science classrooms in areas C & E

Week ending Friday July 3rd, 2020

- ☞ Paint drywall in boys'/girls' locker rooms
- ☞ Continue pier installation and pouring of footings in areas C & D
- ☞ Continue framing walls in areas C & D
- ☞ Continue with mechanical/electrical/plumbing rough ins for areas C & D
- ☞ Follow rough ins with hanging drywall in areas C & D
- ☞ Install VCT flooring in upper C & D

East Bethel Elementary School

- ☞ Warranty walk scheduled for mid-summer

St. Francis Elementary School

- ☞ Proposed sitework approved by City of St. Francis City Council. Phase 1 to start once construction permits have been issued.

Weekly Project Report

June 30th, 2020

St. Francis High School

Week ending Friday June 26th, 2020

- ☞ Begin to build CMU walls in area A
- ☞ Continue installing ceiling grid and lighting in upper K
- ☞ Finish tiling corridor walls in upper K
- ☞ Finish painting drywall in upper J and begin on ceiling grid
- ☞ Start pouring concrete over underground utilities in lower J
- ☞ School store casework to arrive

Week ending Friday July 3rd, 2020

- ☞ Demo of old staircase in area G
- ☞ Begin demo bridge street room in area G
- ☞ Begin framing metal walls in area A
- ☞ Begin framing metal walls in lower J
- ☞ Install lighting and finish ceiling grid in upper J

Early Childhood Family Center

Week ending Friday June 26th, 2020

- ☞ Pave and stripe bus loop parking lot (weather dependent)
- ☞ Setting door framing in areas A & B
- ☞ Begin to hang drywall in areas A, B, & C
- ☞ Remove and install new exterior windows in areas A, B, & C

Week ending Friday July 3rd, 2020

- ☞ Continue hanging and taping drywall and A & B
- ☞ Begin painting new drywall in areas A & B
- ☞ Begin VCT install in areas A & B
- ☞ Finish installing exterior windows
- ☞ Install high density storage unit in new location in area A

Weekly Project Report

June 30th, 2020

Cedar Creek Elementary School

Week ending Friday June 26th, 2020

- ☞ Finish setting door frames in area D
- ☞ Finish metal wall framing in areas E & F
- ☞ Continue mechanical/electrical/plumbing rough ins for areas E & F
- ☞ Start hanging drywall in areas D, E & F
- ☞ Begin ceiling grid and lighting install for classrooms in areas B & C


Week ending Friday July 3rd, 2020

- ☞ Finish ceiling grid and tile in area A classrooms
- ☞ Frame in doorways in CMU walls and frame in bathrooms in area A, C, D, E
- ☞ Continue painting and installing ceiling grid/tile in area B & C classrooms
- ☞ Continue hanging drywall in D, E, and F classrooms
- ☞ Infill slabs for underground plumbing and install tile in bathrooms in areas A & D

Progress Photos:



SFMS – Flooring being removed in upper C & D classrooms

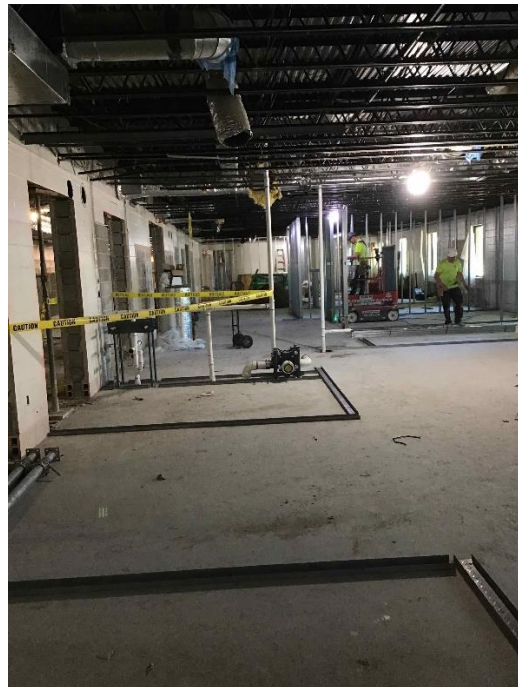

SFMS – Steel walls beginning to be framed in for lower C & D

Weekly Project Report

June 30th, 2020




SFHS – Beginning work on removal of old stairwell in area G



SFHS – CMU walls being built in area A locker rooms



ECFC – New windows on East side of building Area A/B

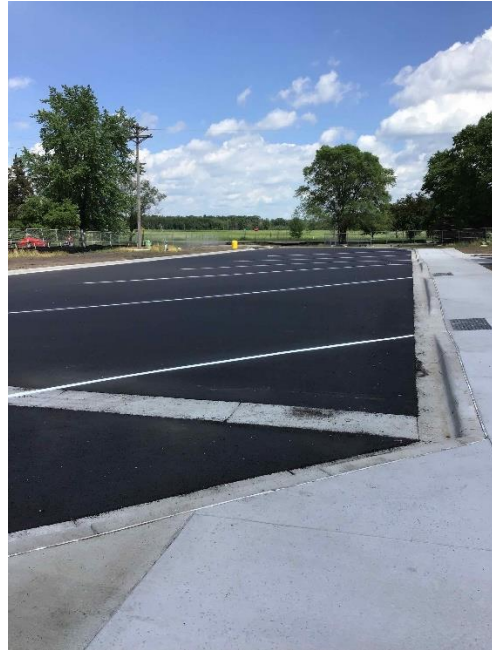

ECFC – Paving and striping complete in bus drop off

Weekly Project Report

June 30th, 2020



CCES – Underground plumbing ready for concrete in new Kids Connection room



CCES – Walls of old classrooms removed to create new Kids Connection space
