


Irvin ES, HS Athletics, Roesler, & MS #3 Construction Update

November 12, 2018

Irvin Elementary School Construction Update



Concrete Poured (Irvin ES)

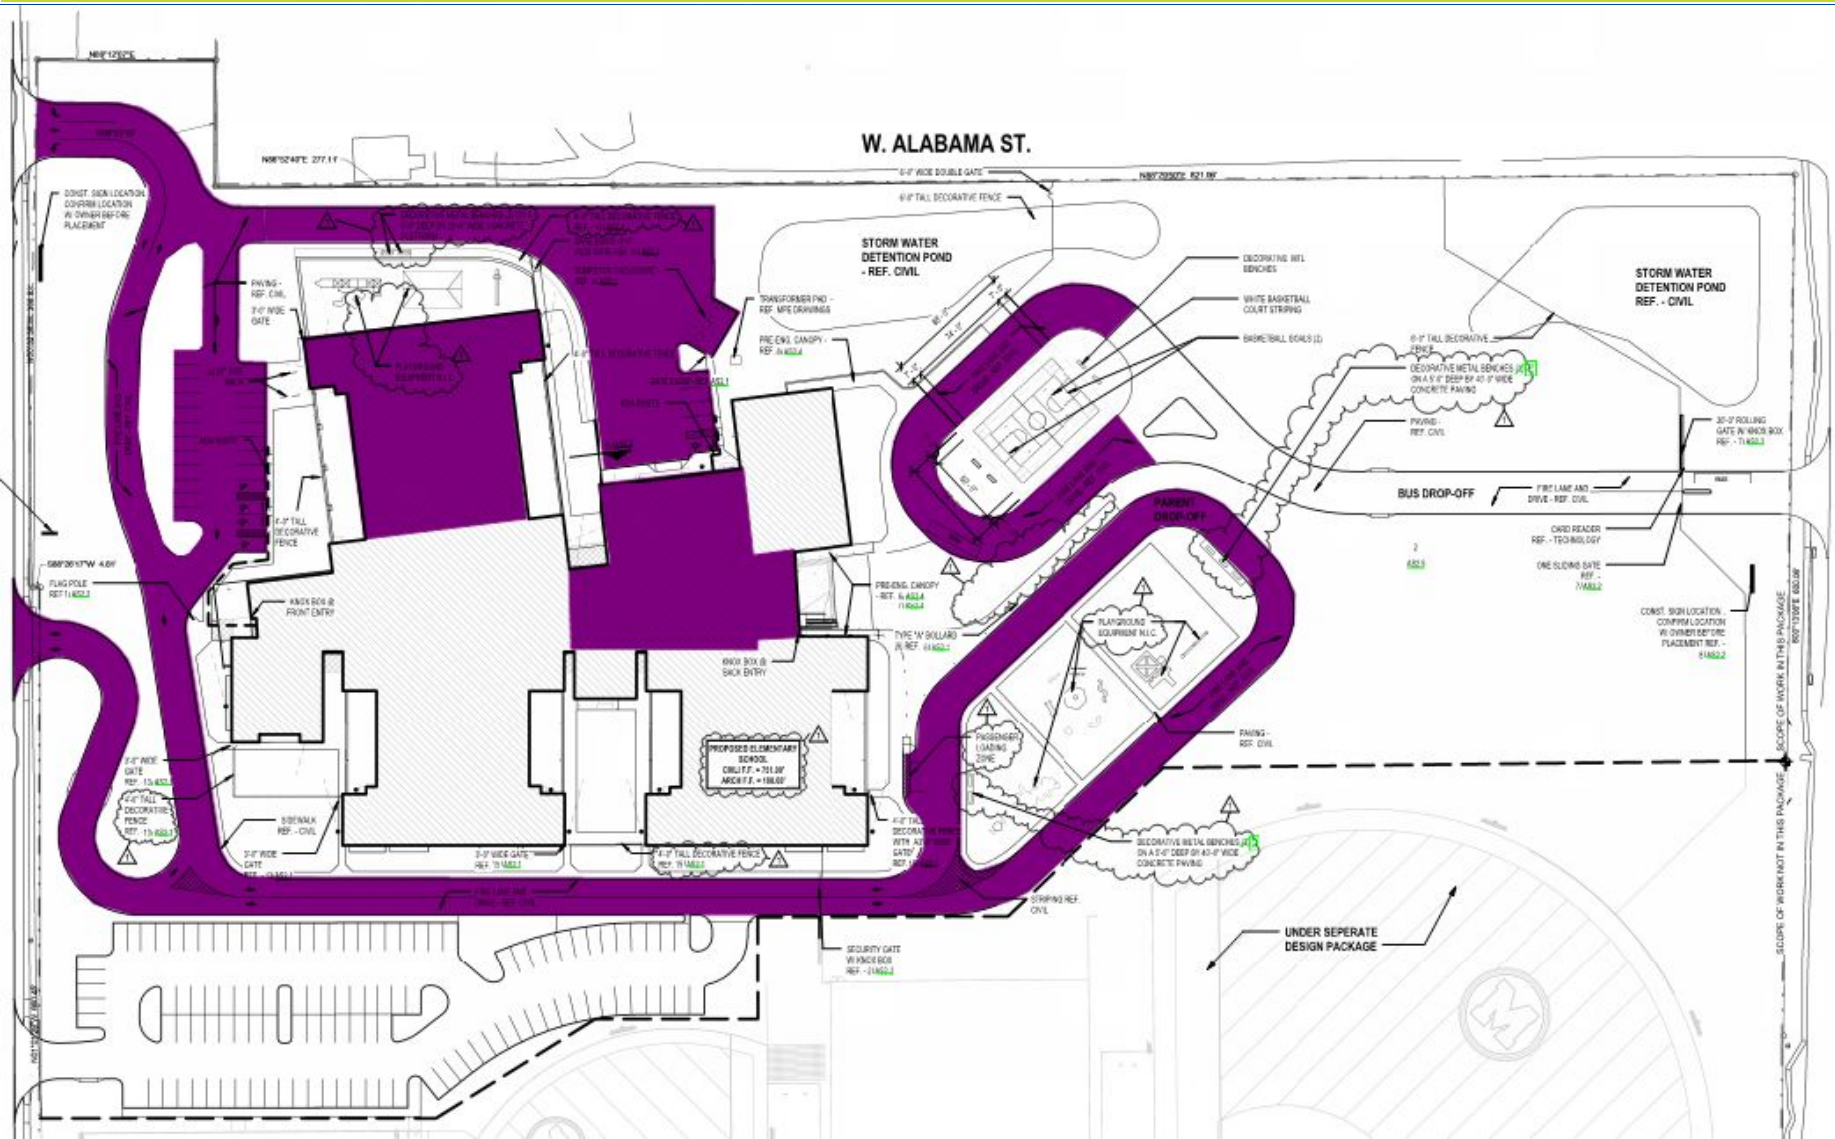

Structural Steel Area 3 (Irvin ES)



Steel Area 3 and 4 (Irvin ES)



Crane and Brick Mockup Panel (Irvin ES)



South Parking Lime Processing (Irvin ES)



Schedule Update Irvin ES

- Erected steel frame @ area 3 (Kinder/1st)
Started steel frame @ area 4 (Kitchen)
- Poured 48,000 sq ft of Fire lane and parking area
- Poured 15,000 sq. ft of slab @ kitchen
- Prepared 15,000 sq ft for next slab pour @ Stage, Commons and Dining area

Look Ahead Schedule for Irvin ES

- Pour balance of commons area 11/15
- Pour area 2 (Reception and Admin area) by 11/21
- Pour drive out to 9th st 11/14
- Erect area 4 steel (Kitchen)
- Deck roof at area 3 (Kinder/1st grade)
- Fireproof steel @ area 3 (Kinder/1st grade)
- Exterior wall framing to begin 11/12 (Kinder/1st grade)
- Start framing interior walls area 3 following fireproofing
- Start off site fabrication of Storm Shelter 12/15
- Current Completion Date is 05/22/2019

MISD Drone Video



Tennis Court Forms (HS Athletics)



Baseball Fencing and Light Poles (HS Athletics)



Baseball Dugout Slabs (HS Athletics)



Construction Update for HS Athletics

- Graded and prepared Softball and Baseball fields
- Set lights at Softball, Baseball and Tennis courts
- Poured all 4 dugout foundations
- Completed Exterior CMU @ Field house and erected steel frame and deck.
- Set fence posts and started mow strip @ baseball field

Look Ahead Schedule HS Athletics

- Form and Pour Tennis courts week of 11/12
- Piers for bleachers 11/12
- Start Brick @ field house 11/14
- Start interior @ field house
- Pour Tennis support building slab 11/19
- Concrete walls @ dugouts week of 11/19
- Fencing @ Baseball 11/26
- Current Field completion dates:
 - Baseball - 01/23/19 Softball 11/18/19
 - Project Completion: 02/25/19

MISD Drone Video



Roesler Athletics Construction Update



Schedule Update (Roesler Athletic Complex)

- Mobilize on site set temp fencing
- Saw cut paving and started demo
- Building Permit issued 11/09/19

Look Ahead Schedule (Roesler Athletic Complex)

- Start site demolition 11/12
- Dirt contractor to bring equipment and follow demolition. 3 week duration
- Circle H Utilities will begin 11/19
- Piers will start 12/03
- Current Completion Date is 07/15/2019

MISD Drone Video



MS #3 Construction Update



Construction Schedule Update (MS #3)

- Office trailer pad and laydown yard installed.
- Site has been stripped and initial grade is being established.
- Building Permit is pending

Look Ahead Schedule (MS #3)

- Job Site Trailer to be delivered 11/12.
- Build building pad 11/12. (3 weeks)
- Continue dirt work to set final grade for paving, tennis courts and field/track
- Once building permit is issued
 - Site utilities will begin
 - Piers
 - Excavation of fire lanes
 - Current Completion Date: 05/14/2020

MISD Drone Video



Thank You

