

	<p align="center"><b>ICS Weekly Project Report</b> July 7th, 2020</p>
 	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

## **St. Francis Middle School**

### **Week ending Friday July 3<sup>rd</sup>, 2020**

- ☞ Paint drywall in boys'/girls' locker rooms
- ☞ Continue pier installation and pouring of footings in areas C & D
- ☞ Continue framing walls in areas C & D
- ☞ Continue with mechanical/electrical/plumbing rough ins for areas C & D
- ☞ Follow rough ins with hanging drywall in areas C & D
- ☞ Install VCT flooring in upper C & D

### **Week ending Friday July 10<sup>th</sup>, 2020**

- ☞ Installing windowsills in upper and lower area A
- ☞ Finish mechanical/electrical/plumbing rough ins for areas C & D
- ☞ Finish hanging drywall in areas C & D
- ☞ Paint and install ACT grid in science rooms
- ☞ Install structural lintels for new doors in area E classrooms

## **East Bethel Elementary School**

- ☞ Warranty walk scheduled for mid-summer

## **St. Francis Elementary School**

- ☞ Proposed sitework approved by City of St. Francis City Council. Phase 1 to start once construction permits have been issued.

## Weekly Project Report

July 7th, 2020

### St. Francis High School

#### Week ending Friday July 3<sup>rd</sup>, 2020

- ☒ Demo of old staircase in area G
- ☒ Begin demo bridge street room in area G
- ☒ Begin framing metal walls in area A
- ☒ Begin framing metal walls in lower J
- ☒ Install lighting and finish ceiling grid in upper J

#### Week ending Friday July 10<sup>th</sup>, 2020

- ☒ Finish CMU wall construction in area A
- ☒ Finish framing metal walls in lower J
- ☒ Begin mechanical/electrical/plumbing rough in for lower J
- ☒ Complete install of architectural ceiling clouds in area G
- ☒ Finish VCT flooring in upper K

### Early Childhood Family Center

#### Week ending Friday July 3<sup>rd</sup>, 2020

- ☒ Continue hanging and taping drywall and A & B
- ☒ Begin painting new drywall in areas A & B
- ☒ Begin VCT install in areas A & B
- ☒ Install high density storage unit in new location in area A

#### Week ending Friday July 10<sup>th</sup>, 2020

- ☒ Finish metal framing of all areas
- ☒ Finish mechanical/electrical/plumbing rough in of all areas
- ☒ Continue hanging and taping drywall in areas A & B
- ☒ Continue installing exterior windows, East portion is complete
- ☒ Continue VCT install in areas A & B

# Weekly Project Report

July 7th, 2020

## Cedar Creek Elementary School

### Week ending Friday July 3<sup>rd</sup>, 2020

- ☞ Finish ceiling grid and tile in area A classrooms
- ☞ Frame in doorways in CMU walls and frame in bathrooms in areas A, C, D, E
- ☞ Continue painting and installing ceiling grid/tile in area B & C classrooms
- ☞ Continue hanging drywall in D, E, and F classrooms
- ☞ Infill slabs for underground plumbing and install tile in bathrooms in areas A & D


### Week ending Friday July 10<sup>th</sup>, 2020

- ☞ Finish framing of bathrooms in A, C, D, E
- ☞ Being plumbing rough ins for corresponding bathrooms
- ☞ Install tile (walls and floor) in area A, B, and C
- ☞ Install base cabinets in area A & C classrooms
- ☞ Finish hanging drywall in area D

### Progress Photos:



SFMS – Mechanical rough in complete in lower C & D classrooms

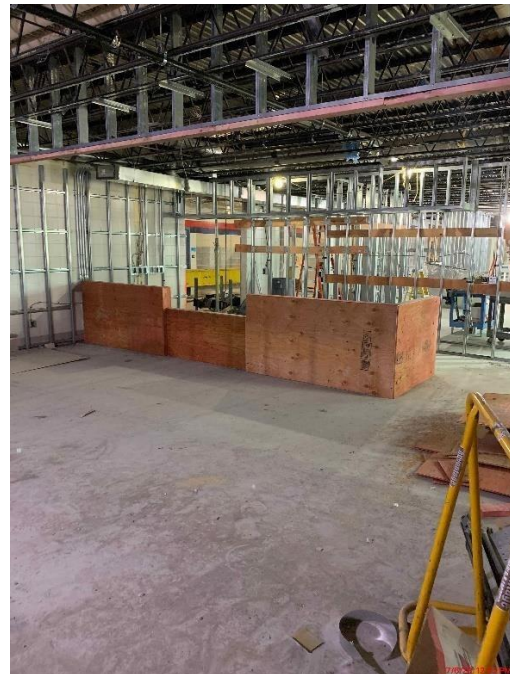

SFMS – Framing complete for lower area C

# Weekly Project Report

July 7th, 2020



SFHS – Tile complete in upper area K



SFHS – Steel framing complete in lower J



ECFC – Drywall and door frames installed in area B classrooms



ECFC – Begin construction of North vestibule

# Weekly Project Report

July 7th, 2020



CCES – steel framing complete in area E classrooms



CCES – new steel lintels being installed in area C

**End of Report**
