

	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

## Centennial Elementary

### Ⓡ Completed week ending Friday, July 24, 2020

- Began casework installation in the classrooms.
- Continued tile work in the multi-user Toilet Rooms.
- Placed the concrete pad for the new chiller unit.
- Continued painting in the classrooms.
- Installed exhaust hoods in the Kitchen area.
- Started setting mechanical equipment in the Boiler Room.

### Ⓡ Planned week ending Friday, July 31, 2020

- Set the new chiller unit in the chiller enclosure.
- Begin door and hardware installation in the SPED Suite.
- Continue classroom casework installation.
- Complete tile work in the Area A multi-user Toilet Rooms.
- Start acoustical ceiling grid installation in the Flex areas.
- Complete drywall installation in the Media Center area.
- Complete metal stud wall framing in the Kitchen and continue plumbing, mechanical and electrical rough-in in that area.

## Middle School

### Ⓡ Completed week ending Friday, July 24, 2020

- Casework deliveries received for several areas
- Roughed in art room display cases on main level
- Finished drywall framing on second level
- Started carpet installation in classrooms on third level
- Started painting walls on first and third level
- Installed structural steel on roof for mechanical equipment
- Mechanical ductwork insulation installation in Special Education Suites
- Installed ceiling grid on second and third floor corridors

### Ⓡ Planned week ending Friday, July 31, 2020

- Continue painting on third level
- Continue installing ceiling grid on third and second level

	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Start installing casework on third and second level
- Continue flooring installation on third level
- Tile walls in staff bathrooms on third level
- Start flooring in classrooms on second level
- Start installing ceiling grid on main level

### Sheridan Hills Elementary

Ⓡ Completed week ending Friday, July 24, 2020

- Began setting unit ventilators in the Area C classrooms.
- Complete hollow metal door and window frame installation in Area C.
- Continued drywall installation in Area C and the new Admin Office areas.
- Began structural steel erection at the Front Entry addition.
- Completed waste and vent plumbing piping in Area A.

Ⓡ Planned week ending Friday, July 31, 2020

- Complete drywall installation in Area C.
- Begin making final mechanical connections to the unit ventilators.
- Begin painting walls in Area C.
- Begin acoustical ceiling grid installation in Area C.
- Complete steel erection at the Front Entrance addition.
- Complete concrete ramp at the Front Entry corridor.

### High School

Ⓡ Completed week ending Friday, July 24, 2020

- Boiler Room
  - Continued piping of boilers
- Area P Link
  - Poured concrete on third floor
  - Mechanical and electrical rough in on first and second level
  - Continued exterior finish system
  - Started interior wall framing on second level
- Area D Main Lower Level Classroom
  - Continued ceilings in classrooms and corridor
- Lower Level Area F Dance Studio and Weight Room
  - Cleaned and assessed mechanical and electrical equipment due to water

	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- 2<sup>nd</sup> and 3<sup>rd</sup> level science rooms
  - Continued casework and plumbing installation
- New Athletics Commons and concessions
  - Started flooring in athletic commons
  - Started fiber reinforce wall finishes in concessions
- New Athletic Corridor/Elevator
  - Continued above grade masonry
- Main Gym
  - Continued wood flooring installation
- Area A & B Art, FACS and Shop Classes
  - Painted walls in Art Rooms
- Loading Dock
  - Poured concrete for foundation walls

Ⓡ Planned week ending Friday, July 31, 2020

- Boiler Room
  - Continue boiler connections
- Area P Link
  - Mechanical and electrical rough ins
  - Continue exterior finish system
  - Continue interior wall framing
- Area D Main Lower Level Classroom
  - Install flooring
- Lower Level Area F Dance Studio and Weight Room
  - Start ceiling grids in corridors
- 2<sup>nd</sup> and 3<sup>rd</sup> level science rooms
  - Continue casework and plumbing installation
- New Athletics Commons and concessions
  - Floor tile in concessions
  - Install mechanical and electrical finishes
  - Fin tube installation
- New Athletic Corridor/Elevator
  - Above grade masonry
- Main Gym
  - Continue wood flooring installation

	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Area A & B Art, FACS and Shop Classes
  - Casework Installation
  - Mechanical and electrical finishes
- Loading Dock
  - Install trench drains
- Exterior Work
  - Irrigation at front entrance

## STEM

- Ⓡ Completed week ending Friday, July 24, 2020
  - Installed flooring in Music and Special Education Suites
  - Classroom furniture delivered and installation began
  - Installed sinks in classrooms
  - Installed dishwashing equipment
- Ⓡ Planned week ending Friday, July 31, 2020
  - Install tack wall in kindergarten rooms
  - Continue furniture installation
  - Install ceiling pads in vestibule and front lobby
  - Connect dishwashing equipment
  - Continue boiler room mechanical connections
  - Punchlist Kindergarten and Pre-kindergarten classrooms

## Dual Language

- Ⓡ Completed week ending Friday, July 24, 2020
  - Contractors continued working to address punch list items.
  - ICS Commissioning continued performing the commissioning of the building's mechanical and HVAC systems.
- Ⓡ Planned week ending Friday, July 31, 2020
  - Contractors to continue working to address punch list items.  
Contractors to continue working to address items noted on the commissioning corrective action log.



	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

## CURRENT PROJECT PHOTOS


Centennial – Chiller concrete pad. Kitchen progress.



Centennial – Classroom progress photos.



Centennial – Multi-user Toilet Room tile work. Resource Area progress.

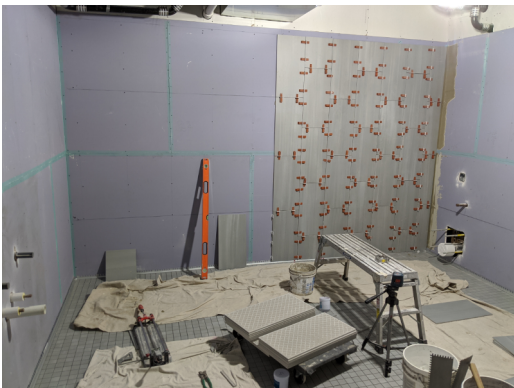

	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Sheridan Hills – Front Entry addition progress. Admin area progress showing reception desk framing.



Sheridan Hills – Staff Lounge area progress. Staff Toilet and Quiet Room progress.



Sheridan Hills – SPED Suite progress.





	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

### High School – New Link Area P Exterior Wall Finish System



### High School – New Link Area P Third Level Poured and Second Level Wall Framing



### High School – Photo Lab and Computer Lab Floors Installed





	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

High School – Exterior Work Loading Dock and Front Entrance



High School – Art Room Painting and Floor Infills



High School – Gym Floor Installation





	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423


### High School – Athletics Commons Flooring and Concession Wall Finishes



### High School – Science Room Casework and Plumbing



### High School – Athletic Corridor Exterior and New Bathrooms

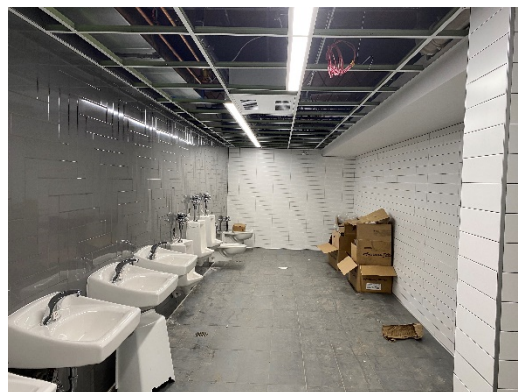

	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

STEM – Pre-Kindergarten Classroom Delivered and Staged



STEM – Kindergarten Rooms Furniture Installed



STEM – Boiler Room Mechanical Equipment Concrete Pads





	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

### STEM – Special Education Suite Flooring Installed



### STEM – Dishwash Equipment Installation



	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Middle School – Main Level Art Room Drywall and Display Cases



Middle School – Classroom Carpet Installation on Third Level



Middle School – Special Education Suite HVAC Ductwork Insulation





	<b>ICS Weekly Project Report</b> July 24, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Middle School – Third Level Resource and Breakout Spaces Walls and Soffits Painted



Middle School – Casework delivered and science rooms plumbing chases



Middle School – Ceiling and Soffits in Corridors

