

	<p align="center">ICS Weekly Project Report July 27th, 2020</p>
 	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

St. Francis Middle School

Week ending Friday July 24th, 2020

- ☞ Continue casework install in upper C&D classrooms
- ☞ Continue hanging drywall in lower area C media center
- ☞ Begin backfilling and concrete infills on remaining footing openings
- ☞ Finish drywall in area A new locker commons
- ☞ Finish concrete pouring over underground plumbing in area E

Week ending Friday July 31st, 2020

- ☞ Finish hanging drywall in lower area C media center
- ☞ Paint drywall in area A locker commons
- ☞ Begin hanging drywall in area E science rooms
- ☞ Finish tiling girls locker room in area A
- ☞ Begin CMU demo in upper C & D hallway

East Bethel Elementary School

- ☞ Warranty walk scheduled for mid-summer

St. Francis Elementary School

- ☞ Sitework at SFES began Friday July 24th. Substantial completion is currently scheduled for early September.

Weekly Project Report

July 27th, 2020

St. Francis High School

Week ending Friday July 24th, 2020

- ☞ Begin hanging drywall in lower J
- ☞ Install grid in lower K hallways
- ☞ Finish MEP rough in for areas A and lower J
- ☞ Finish CMU wall construction in area A
- ☞ Begin plumbing work in upper J bathrooms
- ☞ Continue with dirt infills of area G to bring flooring up to grade

Week ending Friday July 31st, 2020

- ☞ Begin install of new central staircase in area G
- ☞ Setting locker bases in area A locker rooms
- ☞ Continue grid install in upper J media center
- ☞ Continue demolition in area G cafeteria expansion
- ☞ Continue hanging drywall in lower J and prep for mud/tape

Early Childhood Family Center

Week ending Friday July 24th, 2020

- ☞ Continue painting of new drywall
- ☞ Begin installing mechanical/electrical/plumbing fixtures for classrooms and individual stalls starting in area B
- ☞ Begin tile work in individual bathroom stalls
- ☞ Finish glazing on exterior store fronts

Week ending Friday July 31st, 2020

- ☞ Begin landscaping work in new bus drop off area
- ☞ Continue tile work in individual bathroom stalls
- ☞ Finish painting in areas A & B
- ☞ Continue installing mechanical/electrical finishes in individual bathroom stalls
- ☞ Install gym divider curtain

Weekly Project Report

July 27th, 2020

Cedar Creek Elementary School


Week ending Friday July 24th, 2020

- ☞ Begin mudding/taping drywall in area D
- ☞ Finish framing of walls in areas A & B
- ☞ Infill masonry openings in areas B & D
- ☞ Continue tile install in area A and C bathrooms
- ☞ Continue install of ACT ceiling pads in corridor hallways
- ☞ Patch terrazzo flooring in areas A and B


Week ending Friday July 31st, 2020

- ☞ Start framing and drywall of offices in area E
- ☞ Finish tile install of area A and C bathrooms
- ☞ Finish terrazzo patching in flooring of A & B
- ☞ Continue install of ACT ceiling tiles in corridor hallways
- ☞ Begin painting of area D SPED suite

Progress Photos:

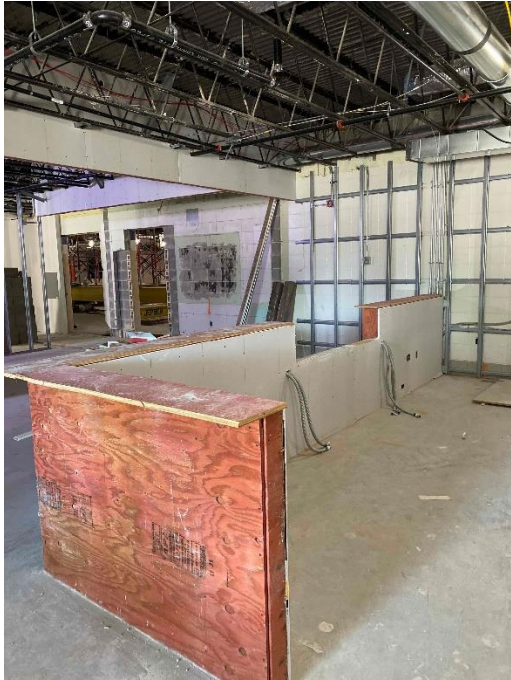


SFMS – Installing drywall in area C reception

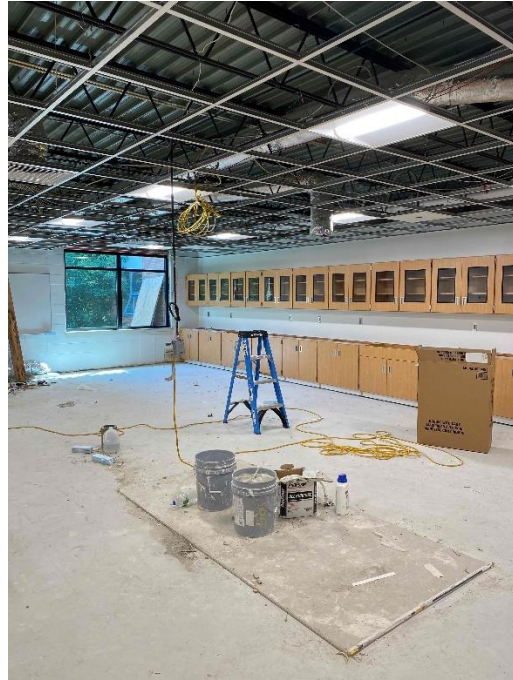


SFMS – Installing casework in area C science classrooms

Weekly Project Report

July 27th, 2020

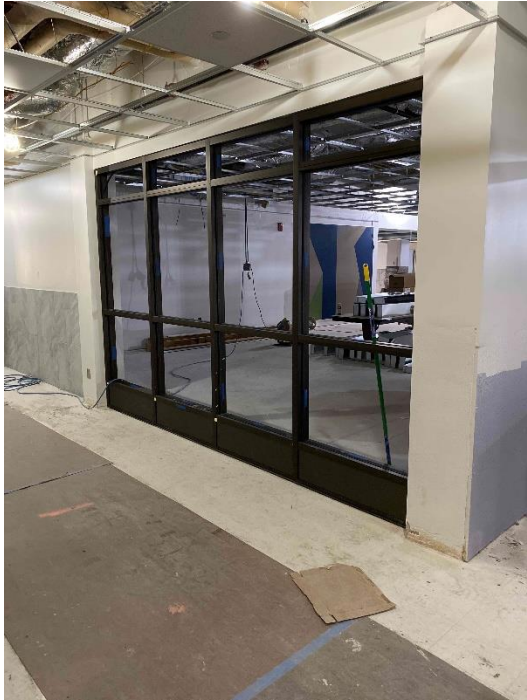


SFHS – Installing metal frames in upper J media center

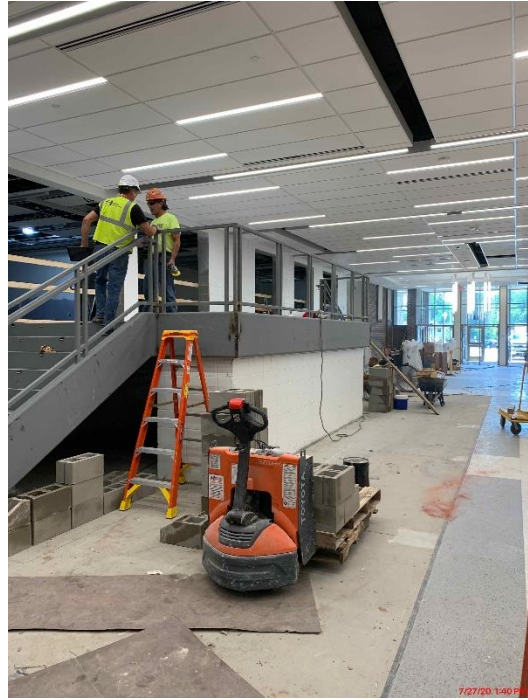

SFHS – Installing new central staircase in area G



ECFC – New entrance on North side of building

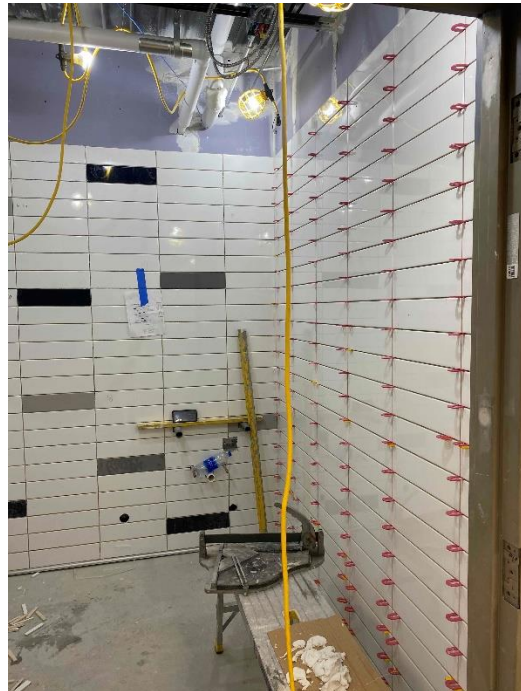

ECFC – Tile work in progress in individual bathroom stalls

Weekly Project Report

July 27th, 2020



CCES – Tile being installed in bathrooms in area A



CCES – Framing in progress in new entrance vestibule for area E

End of Report
