



MORE THAN ARCHITECTS

Huckabee

2017 BOND PROJECTS – BOARD UPDATE

Buffalo Creek Elementary Renovation

Spring Branch Independent School District

Architect Name Project No. 01809-01-02

Date: March 31, 2020



1) **PROJECT TEAM:**

Owner: Spring Branch ISD

Associate Superintendent for Operations:
Travis Stanford

SBISD Project No.: 67207

Project Manager: Matisia Hollingsworth

Architect: Huckabee

Principal-in-Charge: Steve Daylor, AIA
Principal-in-Charge: John Haskew, AIA
AP & Project Manager: Timothy Barnes, AIA

Contractor: Division One Construction

Competitive Sealed Proposal

2) **GENERAL SCOPE OF WORK:**

Interior and exterior renovation of existing 82,149 square footage Elementary School. Scope of work includes: Replacement of the existing roofing system including the standing seam metal roof, mechanical system upgrades, Library and Collaboration spaces renovation, replacement of skylight panels, new building marquee, replacement of door hardware at classrooms, fire alarm system, security alarm & access control improvements, renovation of existing restrooms, new kindergarten playground equipment, regrading at the existing detention pond, and providing new clearstory windows at collaboration areas.

Off-Site Transition:

Campus will remain at current location during renovation. No off-site transition is anticipated until Summer 2020.



MORE THAN ARCHITECTS

Huckabee

3) **BOND PLAN PROJECT TIMELINE:**

| | |
|---------------------------|--------------------------------|
| PROJECT ADVISORY TEAM | SEPTEMBER/2018 – DECEMBER/2018 |
| CONTRACTOR SELECTION | JANUARY/2019 – MARCH/2019 |
| SCHEMATIC DESIGN | MAY/2018 – SEPTEMBER/2018 |
| DESIGN DEVELOPMENT | AUGUST/2018 – OCTOBER/2018 |
| CONSTRUCTION DOCUMENTS | OCTOBER/2018 – DECEMBER/2018 |
| BIDDING / BOARD APPROVAL | APRIL/2019 – JUNE/2019 |
| PERMIT RECEIVED | JULY/2019 |
| CONSTRUCTION PHASE | JULY/2019 – JUNE/2020 |
| OCCUPANCY | AUGUST 2020 |

Current
Point

4) **PROJECT STATUS OVERVIEW**

- Final Design Presented to Board Workshop on April 8, 2019
- Proposals Received on April 17, 2019
- Board Approval of CSP Contractor Division One on June 24, 2019

5) **PAST 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:**

- Completed installation of Structural Framing for Pop-ups.
- New Playground Equipment set at playground.
- Completed grading at playground areas.

6) **NEXT 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:**

- Bi-Weekly OAC Meetings are being held on Wednesdays at 1:30 PM.
- Starting demolition of restrooms near Gymnasium.
- Low voltage wiring being pulled at Collaboration areas.



MORE THAN ARCHITECTS

Huckabee

7) **PHOTOGRAPHS:**



Installation of equipment and concrete poured at playgrounds






MORE THAN ARCHITECTS

Huckabee

Temporary wall constructed at restrooms near gymnasium

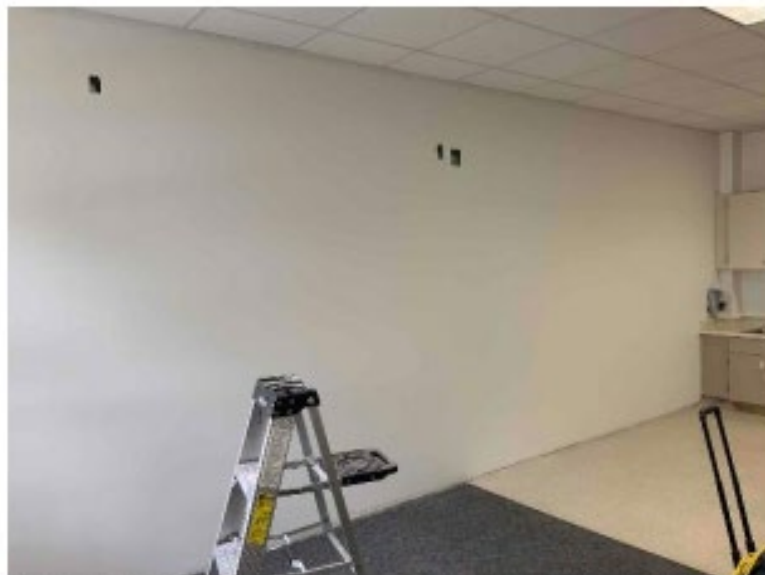

Preparing wall for active wall mock-up



Completing Mock-up Wall in Classroom
