











	<p align="center">ICS Weekly Project Report August 10th, 2020</p>
 	<p align="center">ISD #15 St. Francis Area Schools 4111 Ambassador Blvd NW St. Francis, MN Bond Construction Projects</p>

St. Francis Middle School

Week ending Friday August 7th, 2020



-  Install structural steel in lower C&D hallway
-  Complete CMU demo in upper area C & D hallway
-  Finish mechanical/electrical/plumbing rough ins for upper C bathrooms
-  Begin hanging drywall in upper C bathrooms
-  Finish exterior glazing in lower area C

Week ending Friday August 14th, 2020




-  Finish hanging bathroom fixtures in lower A
-  Finish installing casework for science rooms in lower area C
-  Finish structural steel install in lower C & D hallway
-  Begin structural steel for new entrance
-  Begin tiling walls in upper C bathrooms

St. Francis Elementary School

Week ending Friday August 7th, 2020

-  Removal of existing pavement complete
-  Begin site grading for new infiltration basin

Week ending Friday August 14th, 2020

-  Finish Electrical underground wiring
-  Finish prep work on sub grade
-  Pour sidewalks/curb and gutter

Weekly Project Report

August 10th, 2020

St. Francis High School

Week ending Friday August 7th, 2020

- ☞ Pour concrete for new learning staircase in area G
- ☞ Finish grid install in upper J media center
- ☞ Finish hanging drywall in lower J and begin mud/tape
- ☞ Finish exterior glazing in new addition for area B
- ☞ Continue structural steel install and CMU infill of area B

Week ending Friday August 14th, 2020

- ☞ Finish epoxy flooring for boys' locker rooms in area A
- ☞ Begin finishes on learning stair in area G
- ☞ Infill concrete in lower level J around chemical filtration tank
- ☞ Frame in media center reception desk in upper area J
- ☞ Finish setting tile in upper J hallway

Early Childhood Family Center

Week ending Friday August 7th, 2020

- ☞ Begin tile work in girls gang bathroom stall in area B
- ☞ Continue wall framing and drywall in boys gang bathroom in area B
- ☞ Install high density storage unit in new location

Week ending Friday August 14th, 2020

- ☞ Finish tile work in girl's gang bathroom and move to boy's gang bathroom
- ☞ Install VCT flooring in hallways in areas A & C
- ☞ Complete ceiling grid pad out in areas A & B
- ☞ Finish installing new locksets on existing doors in areas B & C
- ☞ Prepare rooms for final punch list

Weekly Project Report

August 10th, 2020

Cedar Creek Elementary School

Week ending Friday August 7th, 2020

- ☞ Complete framing and begin drywall of new entrance vestibule in E
- ☞ Continue casework install, starting in area A
- ☞ Continue tile install of gang bathrooms in A & C
- ☞ Complete ceiling pad install in all classrooms
- ☞ Hang drywall in area B Kids Connection


Week ending Friday August 14th, 2020

- ☞ Mud/tape new drywall in areas B & E
- ☞ Finish tile work in area A gang bathrooms
- ☞ Finish framing of walls in area E gang bathrooms
- ☞ Finish countertop install in A, B, and C
- ☞ Begin finishes for office suite in area E


Weekly Project Report

August 10th, 2020

Progress Photos:

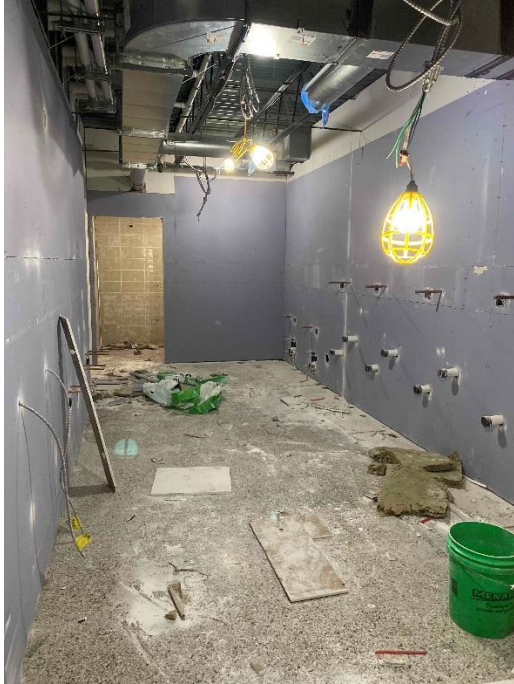


SFMS – Upper C bathrooms ready for tile install

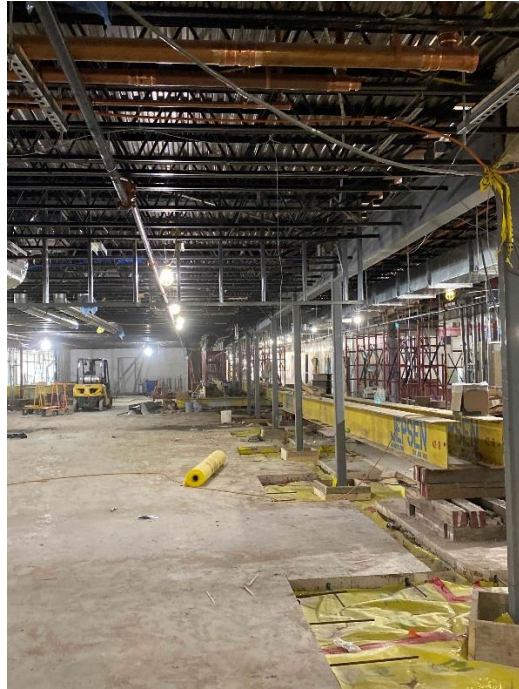

SFMS – Lower C&D shoring and structural steel



SFHS – Beginning finishes of new learning stair in area G

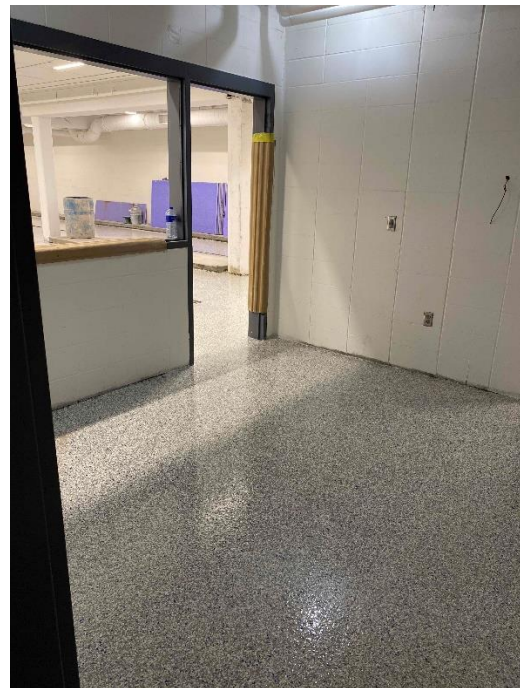

SFHS – New epoxy floors in boys' PE and athletic locker rooms

Weekly Project Report

August 10th, 2020



ECFC – New reception area and office suite in area A



ECFC – New private bathroom in area A nearly complete



CCES – Fixtures mounted in area A washroom



CCES – Drywall nearly complete for secure media center

End of Report
