











|   |   |
|---|---|
|    | <p align="center"><b>ICS Weekly Project Report</b><br/>August 24th, 2020</p>  |
|   | <p align="center">ISD #15 St. Francis Area Schools<br/>4111 Ambassador Blvd NW St. Francis, MN<br/>Bond Construction Projects</p> |

## St. Francis Middle School

### Week ending Friday August 21<sup>st</sup>, 2020



-  Install mechanical/electrical/plumbing finishes in areas C&D
-  Begin casework install in lower C&D - West of main hallway
-  Begin grid install and painting in lower C&D – East of main hallway
-  Begin painting of upper C&D classrooms

### Week ending Friday August 28<sup>th</sup>, 2020



-  Install framing for secure media center in area C/D
-  Pour footings for new entrance in area C
-  Install framing for new entrance in area C
-  Continue grid install in lower C&D along with lighting
-  Continue painting upper C&D
-  Begin tile work in upper C&D bathroom

## St. Francis Elementary School

### Week ending Friday August 21<sup>st</sup>, 2020

-  Lay base course and 1<sup>st</sup> layer of asphalt for new parking lot surfaces
-  Finish excavation and grading of retention ponds

### Week Ending Friday August 28<sup>th</sup>, 2020

-  Saw cutting for electrical poles in parking lot
-  Continue base layer of asphalt for new parking surfaces

## Weekly Project Report

August 24th, 2020

### St. Francis High School

#### Week ending Friday August 21<sup>st</sup>, 2020

- ☞ Flooring installation in progress for upper J media center and offices
- ☞ Terrazzo in progress for learning stair
- ☞ Casework installation in progress for lower J science rooms
- ☞ Floor prep for finish floor happening in upper L staff resource
- ☞ Wall tile taking place throughout upper J
- ☞ Lockers being installed in area A locker rooms
- ☞ Athletic storage room ready for owner use
- ☞ Continued flooring demo in area g cafeteria expansion

#### Week ending Friday August 28<sup>th</sup>, 2020

- ☞ Upper J media center turning over for owner use
- ☞ Finish terrazzo and finishes on learning stair
- ☞ Install flooring in upper L staff resource rooms
- ☞ Finish wall tile in upper J hallways
- ☞ Paint railings around learning stair
- ☞ Install backerboard in upper J bathrooms

### Early Childhood Family Center

#### Week ending Friday August 21<sup>st</sup>, 2020

- ☞ Finish ceiling grid pad out in areas A & B
- ☞ Finish installing coiling door in area A
- ☞ Finish VCT flooring install for remainder of school
- ☞ Install casework in area A

#### Week ending Friday August 28<sup>th</sup>, 2020

- ☞ Finish wall/floor tile in boys gang bathroom area B
- ☞ Install bathroom partitions in both girl's and boy's bathroom area B
- ☞ Finish Low Voltage and handicap wiring in area A
- ☞ Finish casework/countertop installs in areas A&B

## Weekly Project Report

August 24th, 2020

### Cedar Creek Elementary School

#### Week ending Friday August 21<sup>st</sup>, 2020

- ☞ Continue painting in areas B, E, and F
- ☞ Continue installing casework/countertops in areas C & F
- ☞ Begin tiling of bathroom groups in area E
- ☞ Install glasswork in secure media center, area B
- ☞ Install ceiling grid/lighting in area D SPED suite

#### Week ending Friday August 28<sup>th</sup>, 2020

- ☞ Finish flooring and wall finishes in offices in area E
- ☞ Install office furniture in area E
- ☞ Continue with tile install in area E bathrooms
- ☞ Close out gang bathrooms in areas A&C
- ☞ Turn over bulk of classrooms in areas A, B, and C
- ☞ Begin lighting conversions for gym

#### Progress Photos:



SFMS – Lower C bathroom plumbing fixtures and partitions are installed



SFMS – Locker bases installed in upper C/D locker commons



# Weekly Project Report


August 24th, 2020



SFHS – Lockers installed in area A locker rooms



SFHS – Upper J media center nearly complete for owner turn over

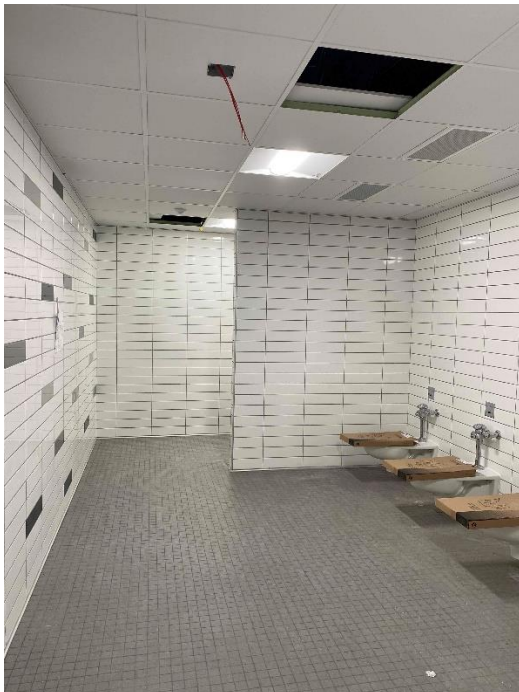

ECFC – Girls bathroom in area B ready for partitions



ECFC – Casework installed in area A classrooms

## Weekly Project Report

August 24th, 2020



CCES – Glass, flooring, and ceiling complete in area D SPED suite



CCES – Cafeteria/multi-purpose ceiling complete

**End of Report**
