

	ICS Weekly Project Report September 18, 2020
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

High School

- Ⓜ Completed week ending Friday, September 18, 2020
 - General
 - Punch list and interior room signage installed
 - Testing, balancing, and commissioning of mechanical systems
 - Boiler Room
 - Exhaust piping
 - Area P Link
 - Temporary window conditions to addressed
 - Painting throughout
 - Lower Level Area F Dance Studio and Weight Room
 - Flooring installation continued
 - Installation of mechanical diffusers and electrical finishes in multipurpose rooms
 - Area C 3rd level science rooms
 - Plumbing rough ins near completion
 - Area C 3rd level restrooms
 - Plumbing rough ins near completion
 - New Athletic Corridor/Elevator
 - Roofing continued and interior wall framing continued
 - Demolition of exterior wall
 - Exterior Work
 - Sod and landscaping throughout
- Ⓜ Planned week ending Friday, September 25, 2020
 - General
 - Punch list
 - Testing, balancing, and commissioning of mechanical systems
 - Boiler Room
 - Mechanical connections to continue
 - Area P Link
 - Window prep
 - Lower Level Area F Dance Studio and Weight Room
 - Finish dance studio flooring.

	ICS Weekly Project Report September 18, 2020
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Flooring installation in multipurpose rooms
- Area C 3rd level science rooms
 - Gyp board install to begin
- Area C 3rd level restrooms
 - Gyp board install to begin
- New Athletic Corridor/Elevator
 - Floor slab to be poured
 - Interior wall framing
 - Elevator work
- Exterior Work
 - Sod and landscaping throughout

Centennial Elementary

- Ⓜ Completed week ending Friday, September 18, 2020
 - Contractors worked to complete punchlist items.
 - Continued testing and balancing of the building mechanical/HVAC systems.
 - Contractors corrected issues noted on the IEA Commissioning corrective action log.
 - Continued working on boiler piping.

- Ⓜ Planned week ending Friday, September 25, 2020
 - Contractor to continue working to address punchlist items.
 - Contractor to continue working through testing and balancing of the mechanical/HVAC equipment.
 - Continue boiler room piping efforts.
 - All State to continue installing security system components.

Sheridan Hills Elementary

- Ⓜ Completed week ending Friday, September 18, 2020
 - Began the exterior brick at the front entry addition.
 - Completed the installation of the tackable wall covering in the Front Entry corridor.
 - Continue Phase 2 mechanical piping in the Lower Level.
 - New boilers were set on their respective housekeeping pads.

	ICS Weekly Project Report September 18, 2020
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- All State to continued installing security system components.
- Completed sodding adjacent to the Front Entry addition.

Ⓜ Planned week ending Friday, September 25, 2020

- Complete the brick at the Front Entry addition.
- Contractor to continue working to address punchlist items.
- Contractor to continue working through testing and balancing of the HVAC/mechanical equipment.
- Continue Phase 2 mechanical piping in the Lower Level.
- All State to continue installing security system components.

Middle School

Ⓜ Completed week ending Friday, September 18, 2020

- Phase 1 punch list work continued
- Phase 2 Area D Special Education/Link
 - Mechanical and electrical rough ins for new Special Education classrooms
 - Demolition of restrooms
- Phase 2 New Conference Room and Staff Lounge
 - Gypsum Board Drywall Installed
 - Mechanical and electrical rough ins

Ⓜ Planned week ending Friday, September 25, 2020

- Phase 1 punch list
 - Remaining Media Center to be delivered and installed
 - Media Center books to be delivered and installed
- Phase 2 Area D Special Education/Link
 - Gypsum Board installation for classrooms
 - Prep for tile work in restrooms
- Phase 2 New Conference Room and Staff Lounge
 - Start mudding and taping wall finishes

STEM

	ICS Weekly Project Report September 18, 2020
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Ⓡ Completed week ending Friday, September 18, 2020
 - Testing, balancing, and commissioning of mechanical systems
 - Completed punch list – Tackable Wall Covering
 - Boiler room work and installation of exterior door
- Ⓡ Planned week ending Friday, September 25, 2020
 - Testing, balancing, and commissioning of mechanical systems
 - Boiler room work oil piping and exhaust ductwork

Dual Language

- Ⓡ Completed week ending Friday, September 18, 2020
 - ICS Commissioning continued performing the commissioning of the building’s mechanical and HVAC systems.
 - Contractors continued working to address items noted on the commissioning corrective action log.
- Ⓡ Planned week ending Friday, September 25, 2020
 - ICS Commissioning to continue performing the commissioning of the building’s mechanical and HVAC systems.
 - Contractors to continue working to address items noted on the commissioning corrective action log.



ICS Weekly Project Report

September 18, 2020



RICHFIELD
PUBLIC SCHOOLS


ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423

CURRENT PROJECT PHOTOS

High School – Exterior Landscaping at Front/District Office Entrances and Loading Dock



High School – New Athletic Corridor Roof and Prep for Concrete Floor

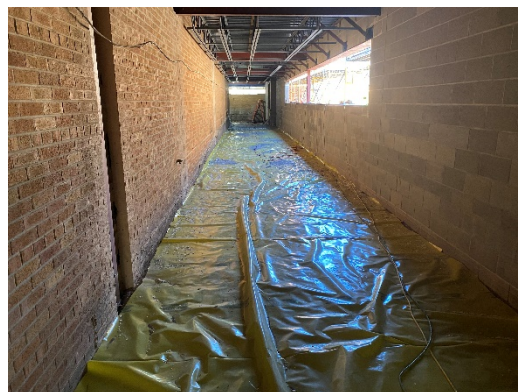



ICS Weekly Project Report

September 18, 2020



RICHFIELD PUBLIC SCHOOLS

ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423


High School – Area C Third Floor Restroom Progress in Wall Plumbing Nearly Complete



High School – Area P New Link Main Level Usable and 2nd Level Painting Progress



High School – Lower Level Multipurpose Rooms, and Dance Studio Flooring Installation

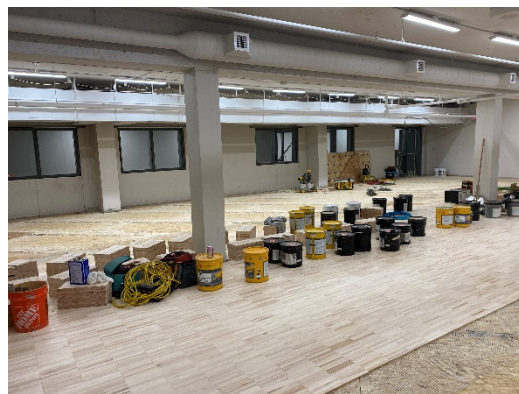



ICS Weekly Project Report

September 18, 2020




RICHFIELD PUBLIC SCHOOLS

ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423

Centennial – Kitchen testing and balancing in progress. Complete Dry Storage/Kitchen Staff Office.



Centennial – Boiler Room piping progress.

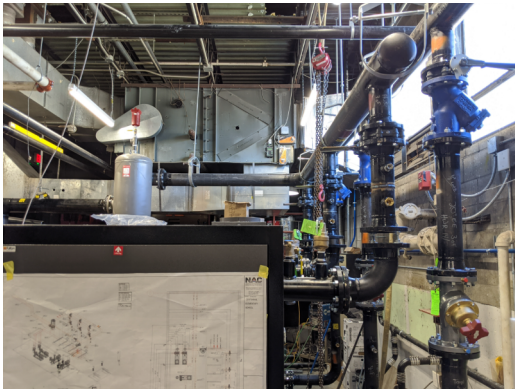

Centennial – Media Area furniture was delivered and installed.



	<p>ICS Weekly Project Report September 18, 2020</p>
 <p>RICHFIELD PUBLIC SCHOOLS</p>	<p>ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423</p>

Sheridan Hills – Front Entry brick work and sodding.



Sheridan Hills – Front Entry and Media Classroom tackable wall covering was installed.



Sheridan Hills – Front Entry secure vestibule and display cases.





ICS Weekly Project Report

September 18, 2020




RICHFIELD PUBLIC SCHOOLS

ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423


Middle School – Area D Restroom Demolition Behind Cafeteria



Middle School Area D Classroom and Corridor Mechanical/Electrical Rough In and Wall Framing

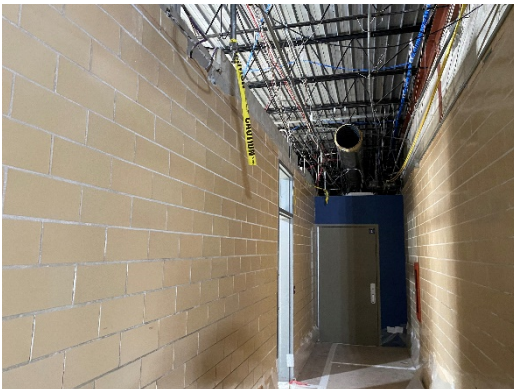

Middle School New Staff Lounge and Conference Room Progress

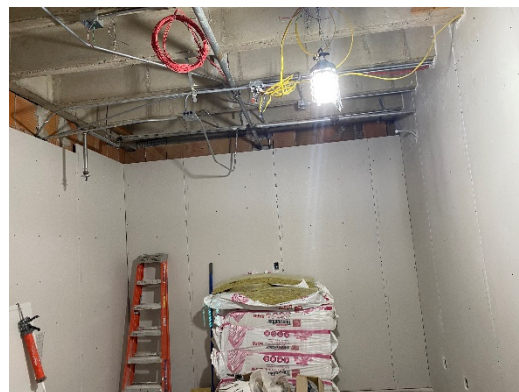



ICS Weekly Project Report

September 18, 2020



RICHFIELD
PUBLIC SCHOOLS

ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423

STEM – Boiler Room Progress Opening Filled, Exterior Door Installed, and Piping Continued

