

	ICS Weekly Project Report October 23, 2020
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

High School

Ⓡ Completed week ending Friday, October 23, 2020

- Boiler Room
 - Continued electrical and mechanical piping connections
- Area P Link
 - Finished carpet and casework installation
 - Installation of vinyl tile flooring in corridors
- Lower Level Area F Dance Studio and Weight Room
 - Finished weight room flooring
- Area C 3rd level science rooms
 - Finished setting cabinets and tops
 - Chemical resistant flooring installation underway
- Area C 3rd level restrooms
 - Finished floor tile and began wall tile installation
- New Athletic Corridor/Elevator
 - Continued elevator installation
 - Continued mechanical and electrical rough ins

Ⓡ Planned week ending Friday, October 30, 2020

- Boiler Room
 - Continue electrical and mechanical piping connections
- Area P Link
 - Furniture installation to take place
 - Window material delivery, reported to take place
- Lower Level Area F Dance Studio and Weight Room
 - Punch list and cleaning
- Area C 3rd level science rooms
 - Seal chemical resistant flooring
 - Fume hood installation
- Area C 3rd level restrooms
 - Plumbing fixtures
 - Begin ceiling installation
- New Athletic Corridor/Elevator
 - Continue elevator installation

	ICS Weekly Project Report October 23, 2020
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Continue mechanical and electrical rough ins

Centennial Elementary

- Ⓜ Completed week ending Friday, October 23, 2020
 - Contractors worked to complete punch list items.
 - IEA Commissioning continued the commissioning of the mechanical/HVAC systems.
 - All-State continued installing security system components.
 - Continued cleaning and flushing the heating and cooling piping system.

- Ⓜ Planned week ending Friday, October 30, 2020
 - Contractors to continue working to address punchlist and IEA Commissioning log items.
 - IEA Commissioning to continue commissioning the mechanical/HVAC systems.
 - All State to complete building security scope.

Sheridan Hills Elementary

- Ⓜ Completed week ending Friday, October 23, 2020
 - Contractors continued working to address punch list items.
 - Continued Phase 2 mechanical piping in the Lower Level.
 - IEA Commissioning continued the commissioning of the mechanical/HVAC systems.
 - All State completed the access control/door security.

- Ⓜ Planned week ending Friday, October 30, 2020
 - Contractors to continue to address punchlist and IEA Commissioning log items.
 - Complete the asphalt patching and curb replacement on W. 64th St.
 - Complete excavation for the Chiller Enclosure addition.
 - Begin chiller addition footing and foundations.

Middle School

- Ⓜ Completed week ending Friday, October 23, 2020

	ICS Weekly Project Report October 23, 2020
 RICHFIELD PUBLIC SCHOOLS	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Phase 2 Area D Special Education/Link
 - Restroom tile installation
- Phase 2 New Conference Room and Staff Lounge
 - Wall painting
- Phase 2 FACS Lab
 - Mechanical and electrical rough ins
- Phase 2 Chiller Tower
 - Continued exterior CMU walls
 - Poured transformer concrete pads
- Phase 3 Third Floor Restrooms
 - Drywall installation continued

Ⓜ Planned week ending Friday, October 30, 2020

- Phase 2 Area D Special Education/Link
 - Finish ceiling pad installation
 - Restroom plumbing fixtures
- Phase 2 New Conference Room and Staff Lounge
 - Ceiling grid installation to begin
- Phase 2 FACS Lab
 - Drywall installation
- Phase 2 Chiller Tower
 - Chiller piping
 - Finish pouring concrete floor
- Phase 3 Third Floor Restrooms
 - Drywall installation to continue in south bathroom
 - Start ceiling and tile to start in north bathroom

STEM

Ⓜ Completed week ending Friday, October 23, 2020

- Furniture punch list items to be delivered and installed

Ⓜ Planned week ending Friday, October 30, 2020

- Continue testing, balancing, and commissioning of mechanical systems

	ICS Weekly Project Report October 23, 2020
	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Dual Language

- Ⓡ Completed week ending Friday, October 23, 2020
 - Contractors continued working to address items noted on the commissioning corrective action log.
 - Contractors worked to address issues identified during the 11-month warranty walkthrough.

- Ⓡ Planned week ending Friday, October 30, 2020
 - Contractors to continue working to address items noted on the commissioning corrective action log.
 - Contractors to continue working to address issues identified during the 11-month warranty walkthrough.



ICS Weekly Project Report

October 23, 2020



RICHFIELD PUBLIC SCHOOLS

ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423

CURRENT PROJECT PHOTOS


High School – Third Level Science Flooring Installation



High School – Third Level Bathroom Tile Installation Complete



High School – Area P Link Vinyl Tile Preparation and Flooring Installation

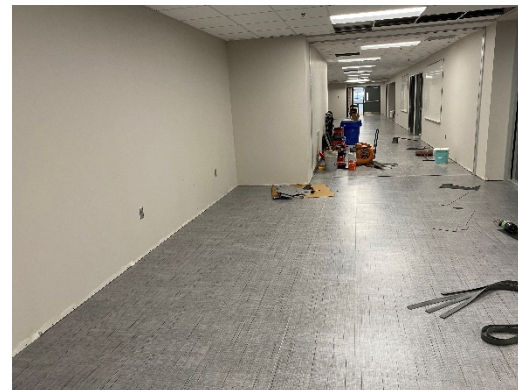



ICS Weekly Project Report

October 23, 2020




RICHFIELD PUBLIC SCHOOLS

ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423

High School – Lower Level Weight Room Flooring Complete



High School – Athletic Corridor and Elevator Progress

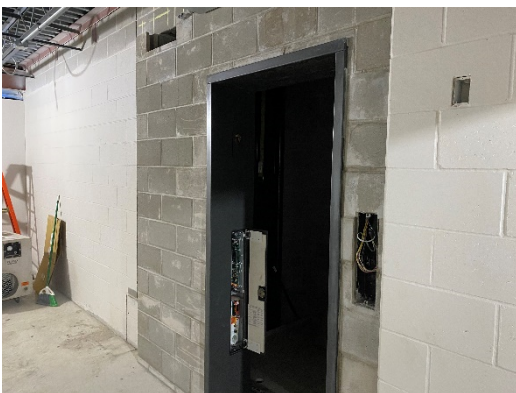

	<p>ICS Weekly Project Report October 23, 2020</p>
 <p>RICHFIELD PUBLIC SCHOOLS</p>	<p>ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423</p>

Sheridan Hills – Boiler Room progress.



Sheridan Hills – Storm water piping connection completed and excavation has been backfilled.



Middle School – Area D Bathroom Tile Installation





ICS Weekly Project Report

October 23, 2020



RICHFIELD
PUBLIC SCHOOLS

ISD #280 Richfield Public Schools
7001 Harriet Avenue S.,
Richfield, MN 55423

Middle School – Second Level FACS Lab Wall Framing and HVAC Ductwork Installation



Middle School – Third Level Bathrooms Plumbing Rough Ins and Drywall Installation

