

Cleveland ISD

Cleveland High School + Cleveland Middle School
Band Renovation and Painting
Construction Update: July 2021

Substantial Completion:

Band Hall Renovation Scheduled for August 1, 2021

Classroom Paint Scheduled for August 1, 2021

Corridor Paint Scheduled for September 7, 2021



Lockwood, Andrews
& Newnam, Inc.
A LEO A DALY COMPANY



Huckabee
MORE THAN ARCHITECTS

Cleveland High School




Lockwood, Andrews
& Newnam, Inc.
A LEO A DALY COMPANY




Huckabee
MORE THAN ARCHITECTS

A schematic diagram of a two-story building. The building is rectangular with a central entrance on the ground floor. The entrance is flanked by two sets of stairs leading to the second floor. On the ground floor, there are several rooms, each containing a table and chairs. On the second floor, there are more rooms, also containing tables and chairs. The diagram is a simple line drawing showing the layout of the building.

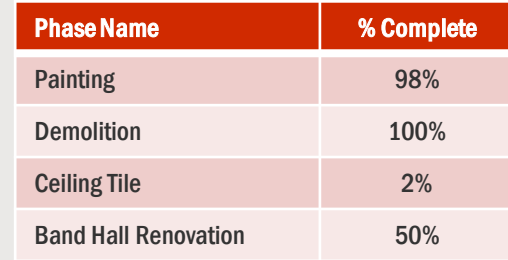

Cleveland High School

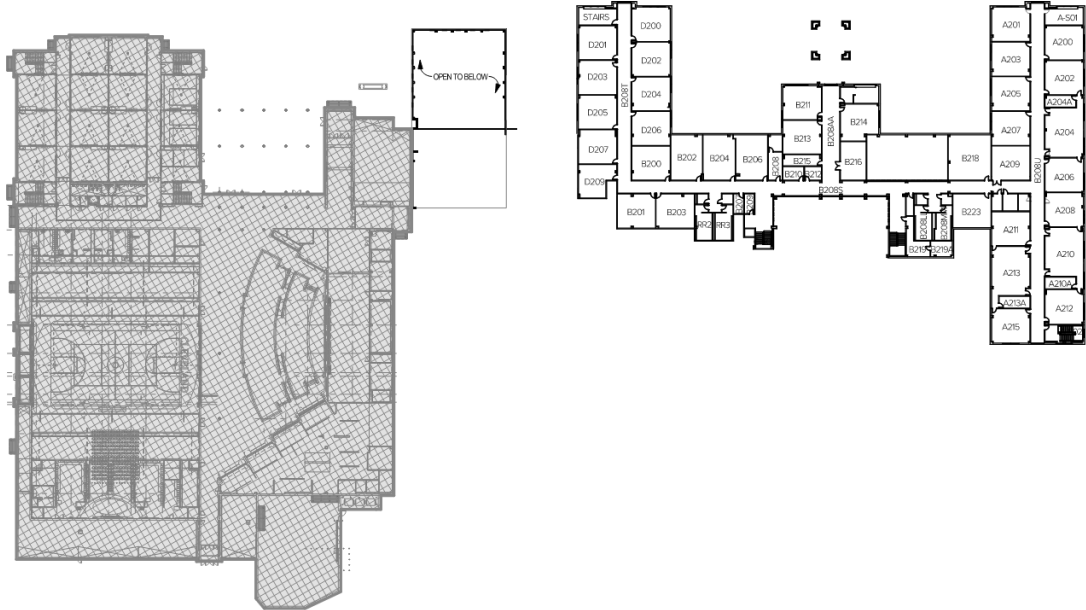

Phase Name	% Complete
Overall Completion	60%
Substantial Completion Band Hall & Classrooms	8 / 1 / 2021
Substantial Completion Corridor Paint	9 / 7 / 2021


LAN Lockwood, Andrews
& Newnam, Inc.
A LEO A DALY COMPANY

PORTFOLIO
BUILDERS

Huckabee
MORE THAN ARCHITECTS



■ Band Hall

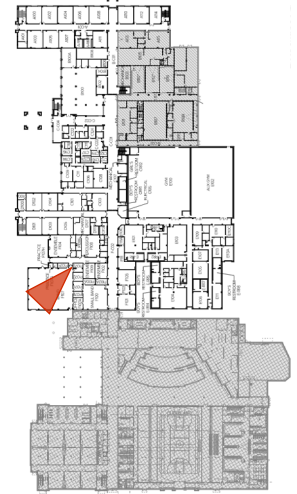


Lockwood, Andrews
& Newnam, Inc.
A LEO A DALY COMPANY

PORTFOLIO
BUILDERS

Huckabee
MORE THAN ARCHITECTS



■ Teaching Wall

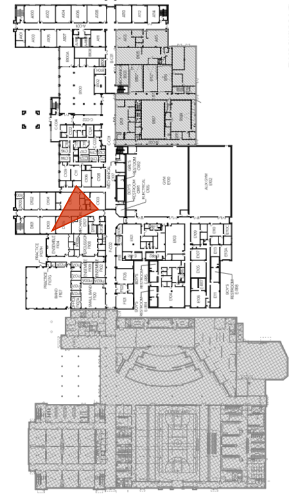

**Lockwood, Andrews
& Newnam, Inc.**


A LEO A DALY COMPANY

**PORTFOLIO
BUILDERS**

Huckabee
MORE THAN ARCHITECTS



■ 1st Floor Main Corridor

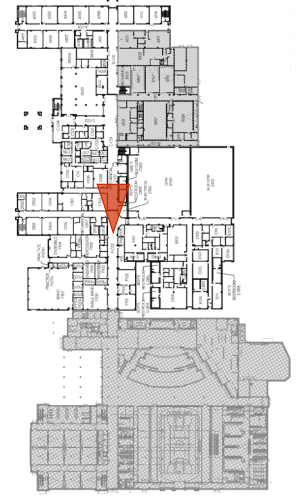


Lockwood, Andrews
& Newnam, Inc.
A LEO A DALY COMPANY

PORTFOLIO
BUILDERS

Huckabee
MORE THAN ARCHITECTS



■ Gymnasium

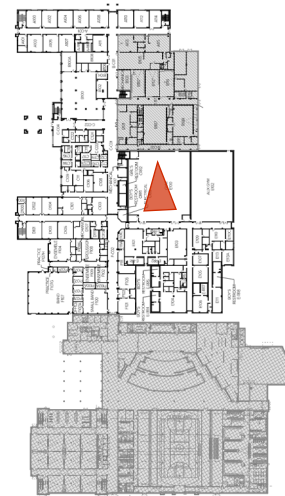

**Lockwood, Andrews
& Newnam, Inc.**

A LEO A DALY COMPANY

**PORTFOLIO
BUILDERS**

Huckabee
MORE THAN ARCHITECTS

Cleveland Middle School Band Hall



Lockwood, Andrews
& Newnam, Inc.
A LEO A DALY COMPANY



Huckabee
MORE THAN ARCHITECTS

Cleveland Middle School Band Hall



Phase Name	% Complete
Demolition	100%
Band Hall	65%
Large Ensemble	65%
Restrooms	95%
Overall Completion	65%
Substantial Completion	8 / 1 / 2021

LAN Lockwood, Andrews & Newnam, Inc.
A LEO A DALY COMPANY

PORTFOLIO
BUILDERS

Huckabee
MORE THAN ARCHITECTS



PORTFOLIO
BUILDERS

Huckabee
MORE THAN ARCHITECTS



- Large Rehearsal Hall



LAN Lockwood, Andrews & Newnam, Inc.
A LEO A DALY COMPANY

PORTFOLIO
BUILDERS

Huckabee
MORE THAN ARCHITECTS




PORTFOLIO
BUILDERS

Huckabee
MORE THAN ARCHITECTS



- HVAC Duct During

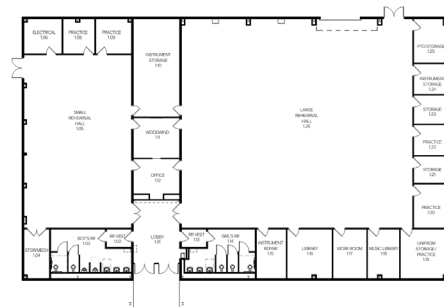

LAN Lockwood, Andrews
& Newnam, Inc.
A LEO A DALY COMPANY

PORTFOLIO
BUILDERS

Huckabee
MORE THAN ARCHITECTS



- HVAC Duct
After



LAN Lockwood, Andrews
& Newnam, Inc.
A LEO A DALY COMPANY

PORTFOLIO
BUILDERS

Huckabee
MORE THAN ARCHITECTS



Lockwood, Andrews
& Newnam, Inc.

A LEO A DALY COMPANY

Huckabee
MORE THAN ARCHITECTS

PORTFOLIO
BUILDERS
