



Projects Update

December 14, 2020

Bond 2017 Project:Leadership Support Center

Bond 2020 Projects:

ES North Classroom Addition ES South Classroom Addition

Bond 2020 Projects:

Intermediate School North Intermediate School South



Bond 2017 – Leadership Support Center

PROJECT SCHEDULE

COMPLETE - Package 1: Demolition, Earthwork, Building Pad and **Underground Utilities**

Demolition - Complete

January 15th - March 15th 2020

COMPLETE - Package 2: Foundation, Structural Steel Purchase and MEP **Underslab**

- Building Pad: Completed on Schedule:
- **Drill & Pour Foundation Piers/Grade Beams Complete:**
 - PCI to give status update of project time line

Package 3: Remaining Building Package

Construction Documents Issue for Proposal: Complete

Issue for Permit: Complete

Develop GMP present to BOT for Approval/Award: Complete

Construction Start - Substantial Completion:

Move - In:

May 18th 2020 May 19th 2020 - June 15th 2021

July 15th 2021

April 6th 2020

April 9th 2020




































































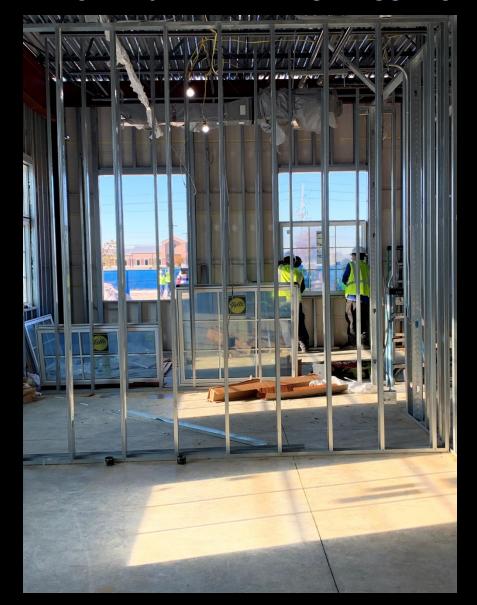
























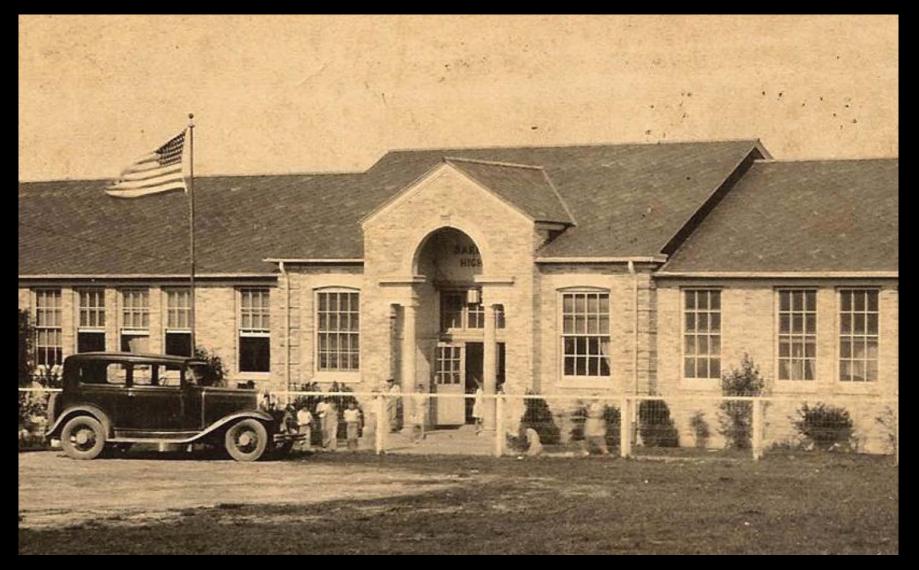














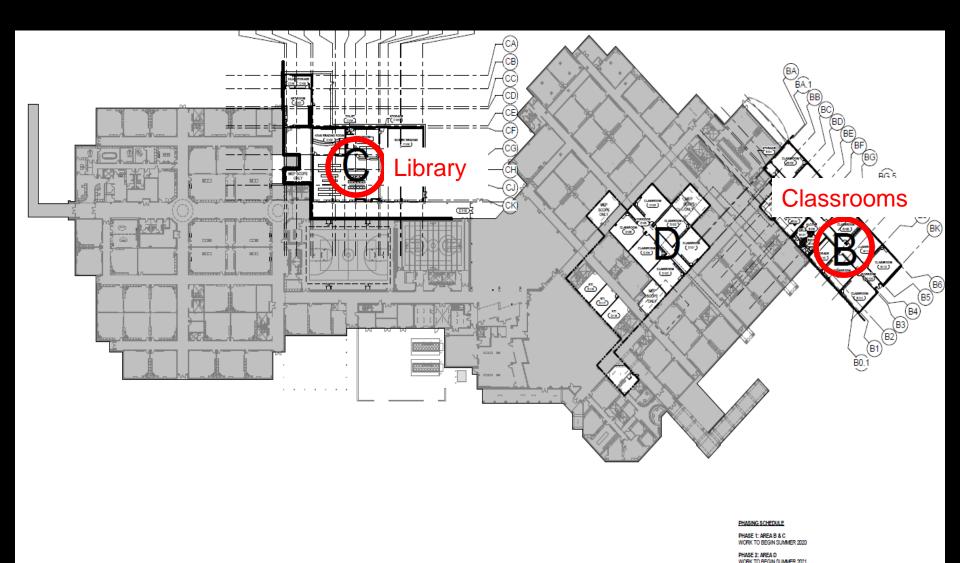






























































































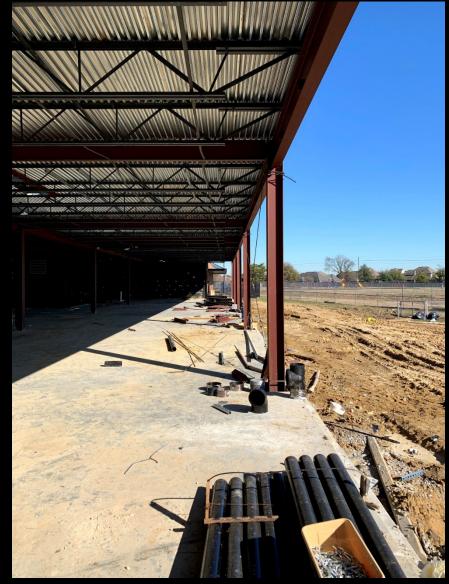





ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS






ELEMENTARY NORTH ADDITIONS



ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS

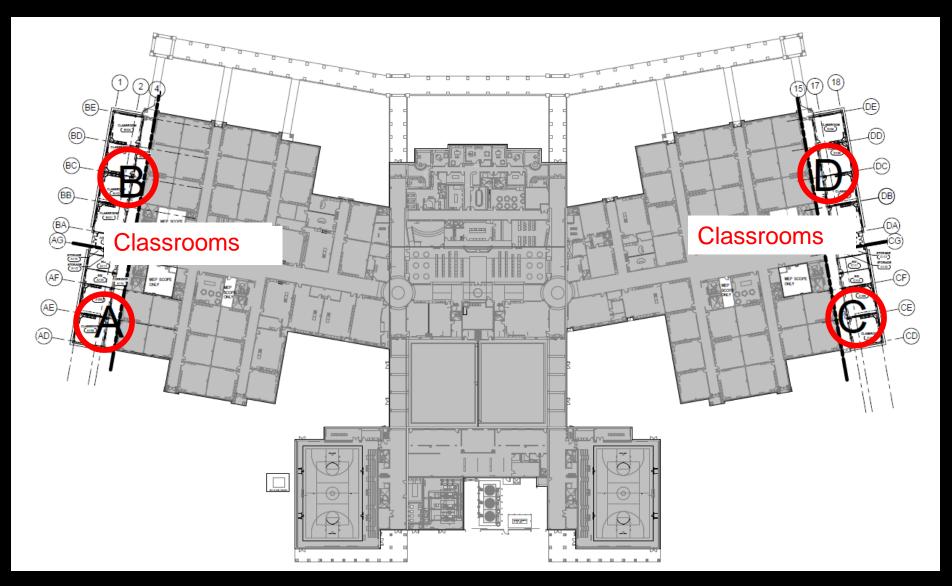





ELEMENTARY SCHOOL NORTH CLASSROOM ADDITIONS












































BOND 2020 – Technology/Administration Building Renovation







BOND 2020 - Technology/Administration Building Renovation

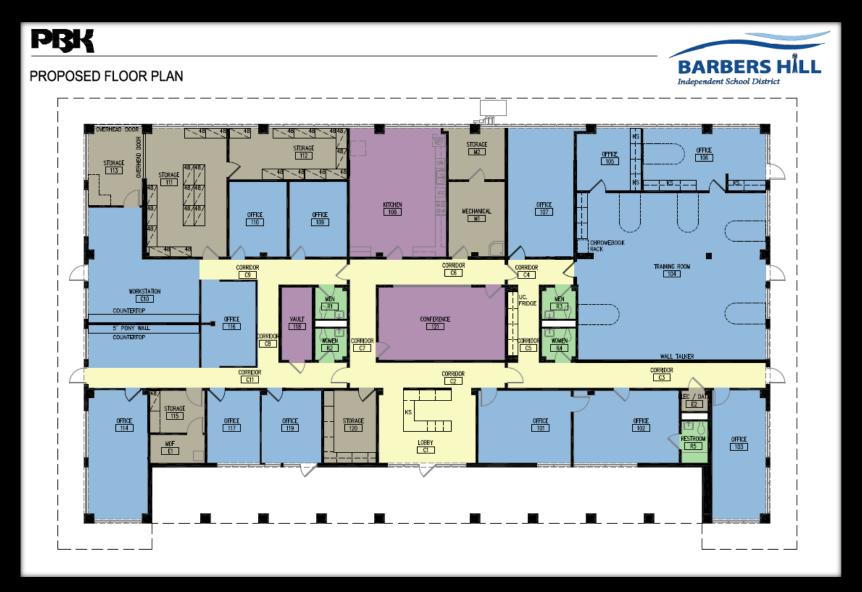





BOND 2020 – Technology/Administration Building Renovation

BARBERS HILL INDEPENDENT SCHOOL DISTRICT

Technology Center Conversion

Project Schedule Issue Date: December 2, 2020

DESIGN DEVELOPMENT (DD) PHASE DD Presentation	
CONSTRUCTION DOCUMENT PHASE	December 10 – March 10, 2021
60% Construction Documents Owner/ AE Review Meeting 90% Construction Documents / Issue For Permit Owner/ AE Review Meeting ISSUE FOR PROPOSAL Preproposal Meeting Receive Subcontractor Bids Develop GMP Recommend Award at BOT Meeting	February 3, 2021 February 17, 2021 February 24, 2021 March 10, 2021 March 17, 2021 March 29, 2021 April 12, 2021
CONSTRUCTION ADMINISTRATION PHASE August 16 - December 17, 2021 (4 months)	
Procurement (3 months)	April 27 – August 16, 2021





BOND 2020 – Road Construction



Perry Road at 1409 Intersection





















INTERMEDIATE SCHOOL SOUTH

























































INTERMEDIATE SCHOOL NORTH





















































































Merry Christmas & Happy New Years

