

This Week

August 30th – September 3rd

- Completed Punchlist in Toilet 120.
- Completed the Site Logistics Plan on the Addition.
- Painted Locker Room 121 in Preparation for Resinous Flooring



Toilet 120 Wall Tile

Next Week

September 6th – September 10th

- Begin Pier Install on the Addition
- Complete The Resinous Flooring and Walls in the Locker Room 121.
- Complete Punchlist in Toilet 120



Site Logistics Plan

Indian Woods Middle School

Construction Report 09/03/21




Toilet Partitions



Temporary Partition



Toilet 121 Shower Rough-in

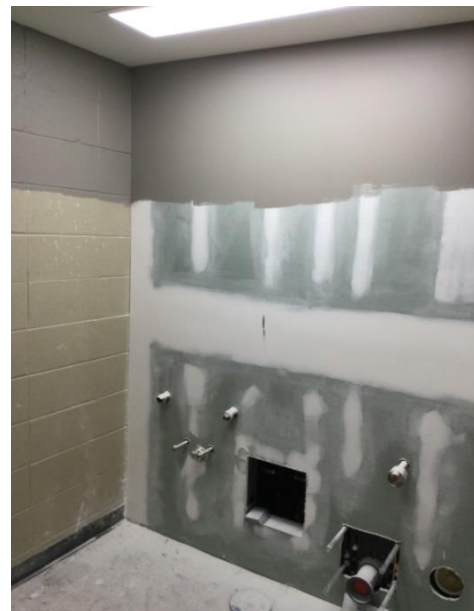

Toilet 121 Wet Wall Rough-in

This Week

August 16th – August 20th

- Installed Wall Tile in Toilet 120
- Completed the Exterior Sheathing/Air Barrier on the Temporary Partition
- Completed the Roof Demolition
- Completed Underground Rough-in in Toilet 121 and Began Framing.



Toilet 120 Wall Tile

Next Week

August 23rd – August 27th

- Paint and Install Toilets/Accessories in Toilet 120.
- Hang/Finish Drywall in Toilet 121
- Begin Installing Utilities for the Addition.



Exterior Temp. Partition

Indian Woods Middle School


Construction Report 08/20/21




Toilet 120 Wall Tile



Toilet 120 Resinous

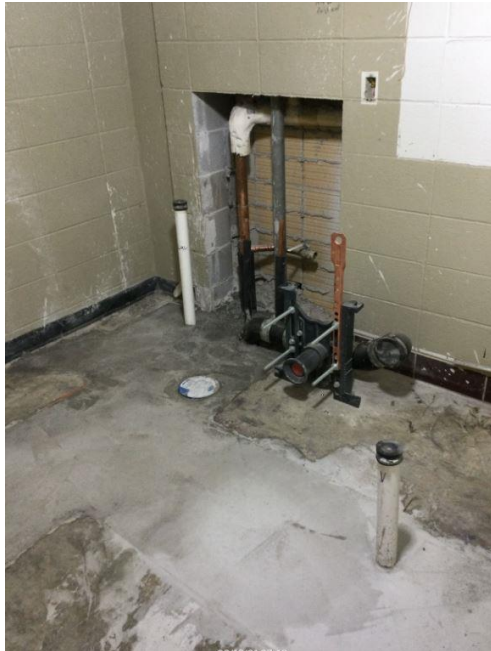

Toilet 121 Rough-in

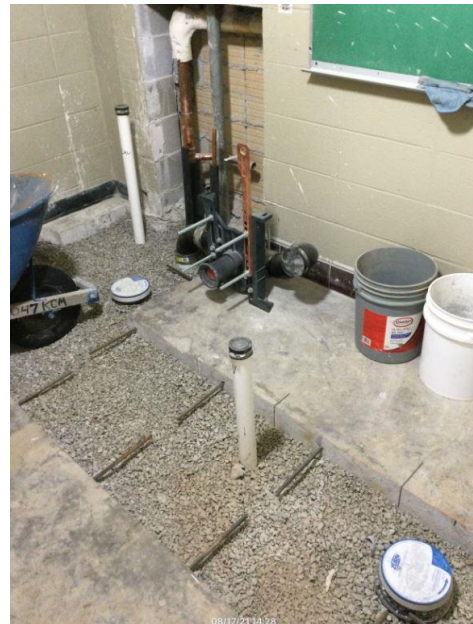

Underground Rough-in Toilet 121
