

MINUTEMAN VOCATIONAL TECHNICAL REGIONAL HIGH SCHOOL PROGRESS

November 15th, 2017 – January 16th, 2018

SKANSKA

Gilbane

KAESTLE BOOS
associates, inc
architects

 **MINUTEMAN**
A REVOLUTION IN LEARNING

December 18th
First Delivery of
Structural Steel



December 21st
View of Area A & B
Structural Steel



December 21st
View of Area G Backfilled
Ready for Steel Erection

Foundation Walls for Green
Houses being formed



January 16th
View of Area G Backfilled
Steel Erection in Progress



December 21st

View of Area C-E
Foundation Prep On-
Going



January 16th
View of Area C-E Foundation
in Area C Complete.
Steel Erection Complete in
Area B



December 12th
Timber Bridge D
Completed with
Temporary Protection
Being Installed for Use.



December 21st
Timber Bridge C
Completed with
Temporary Protection
Installation in Progress



December 12th
Area D heating blankets
placed in anticipation of
concrete pour



December
21st
Workers backfilling
foundations in Area D



December 6th
Placement of
formwork and
rebar in the Lower
Level of Area C



December 12th

View of Area C – Lower
Level Foundation Walls
Formed and Reinforced



January 16th

View of Area C – Lower
Level Foundation Walls
Completed



December 21st
Timber Bridge A
Substantially Complete
Ready for Backfill Operation



December 21st
Timber Bridge B
Substantially Complete
Ready for Backfill Operation



January 16th

Site Overview Facing East



January 16th

Site Overview Facing South



Progress as of
1/16/18

- Walls
- Footings
- Excavated


Area C
Foundation Prep Start: 10/3/17
Foundation Prep Complete: 10/27/17
Footings Rebar Delivery: 10/25/17
Footings Start: 10/27/17
Footings Complete: 12/8/17
Wall Rebar Delivery: 11/9/17
Walls Start: 11/9/17
Walls Complete: 1/10/18
Insulation Complete: 1/17/18
Perimeter Drainage Complete: 12/20/17
Backfill Complete: TBD

Area E
Foundation Prep Start: 11/20
Foundation Prep Complete: 12/6/17
Footings Rebar Delivery: 12/6/17
Footings Start: 12/29/17
Footings Complete: 1/26/18
Wall Rebar Delivery: TBD
Walls Start: TBD
Walls Complete: TBD
Perimeter Drainage Complete: TBD
Insulation Complete: TBD
Backfill Complete: TBD

Area F
Foundation Prep Start: 10/16/17
Foundation Prep Complete: 12/1/17
Footings Rebar Delivery: 12/6/17
Footings Start: 12/12/17
Footings Complete: 1/17/18
Wall Rebar Delivery: 12/14/17
Walls Start: 12/18/17
Walls Complete: 1/19/18
Insulation Complete: 12/28/17
Perimeter Drainage Complete: 1/5/17
Backfill Complete: 1/24/18

Area D
Foundation Prep Start: 10/17/17
Foundation Prep Complete: 11/10/17
Footings Rebar Delivery: 11/9/17
Footings Start: 11/21/17
Footings Complete: 12/8/17
Wall Rebar Delivery: 11/22/17
Walls Start: 11/30/17
Walls Complete: 12/22/17
Insulation Complete: 12/19/17
Perimeter Drainage Complete: 12/22/17
Backfill Complete: 12/28/17

Area G
Foundation Prep Start: 10/16/17
Foundation Prep Complete: 11/9/17
Footings Rebar Delivery: 10/17/17
Footings Start: 10/19/17
Footings Complete: 11/15/17
Wall Rebar Delivery: 10/30/17
Walls Start: 10/31/17
Walls Complete: 11/28/17
Insulation Complete: 11/30/17
Perimeter Drainage Complete: 12/6/17
Backfill Complete: 12/14/17

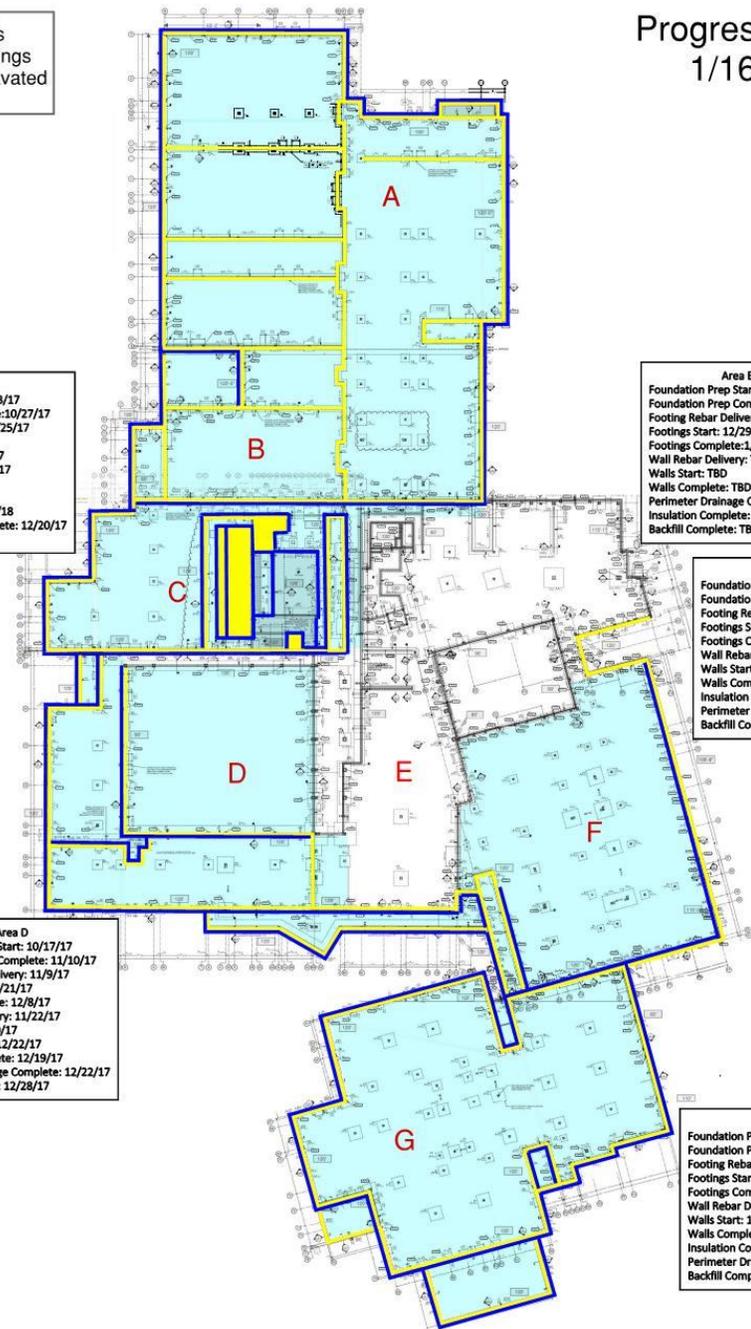

Excavation & Foundation Progress 1/16/18

