

MINUTEMAN VOCATIONAL TECHNICAL REGIONAL HIGH SCHOOL PROGRESS

August 19th 2019 - September 16th 2019

SKANSKA

Gilbane

KAESTLE BOOS
associates, inc
a r c h i t e c t s



MINUTEMAN
A REVOLUTION IN LEARNING

Project Turn-Over Schedule Look Ahead:


Activities	Start	End
Temp Certificate of Occupancy – STUDENTS	8/23	
Building Construction Punch List	7/26	9/24
C of O – Substantial Completion	9/25	
Phase 2 – Exist Building Demo & Construction		
North Marrett Road Construction	9/19	11/19
Building Abatement & Demolition	9/19	2/20
South-East Marrett Road Construction	11/19	12/19
Site Finishes & Plantings (Base Scope)	4/20	6/20

SITE FINISHES & UTILITIES - Spring 2020
 Asphalt Finish from North Mainway Road
 18" x 6" Poly 35-Milim. Road
 Invert Schedule Paragraph 8.03.03

MINUTEMAN REGIONAL VOC. TECH. HIGH SCHOOL
 782 MYRTLE DR.
 LEXINGTON, MA 02421

UTILITIES PLAN (BASE)

C-4.03

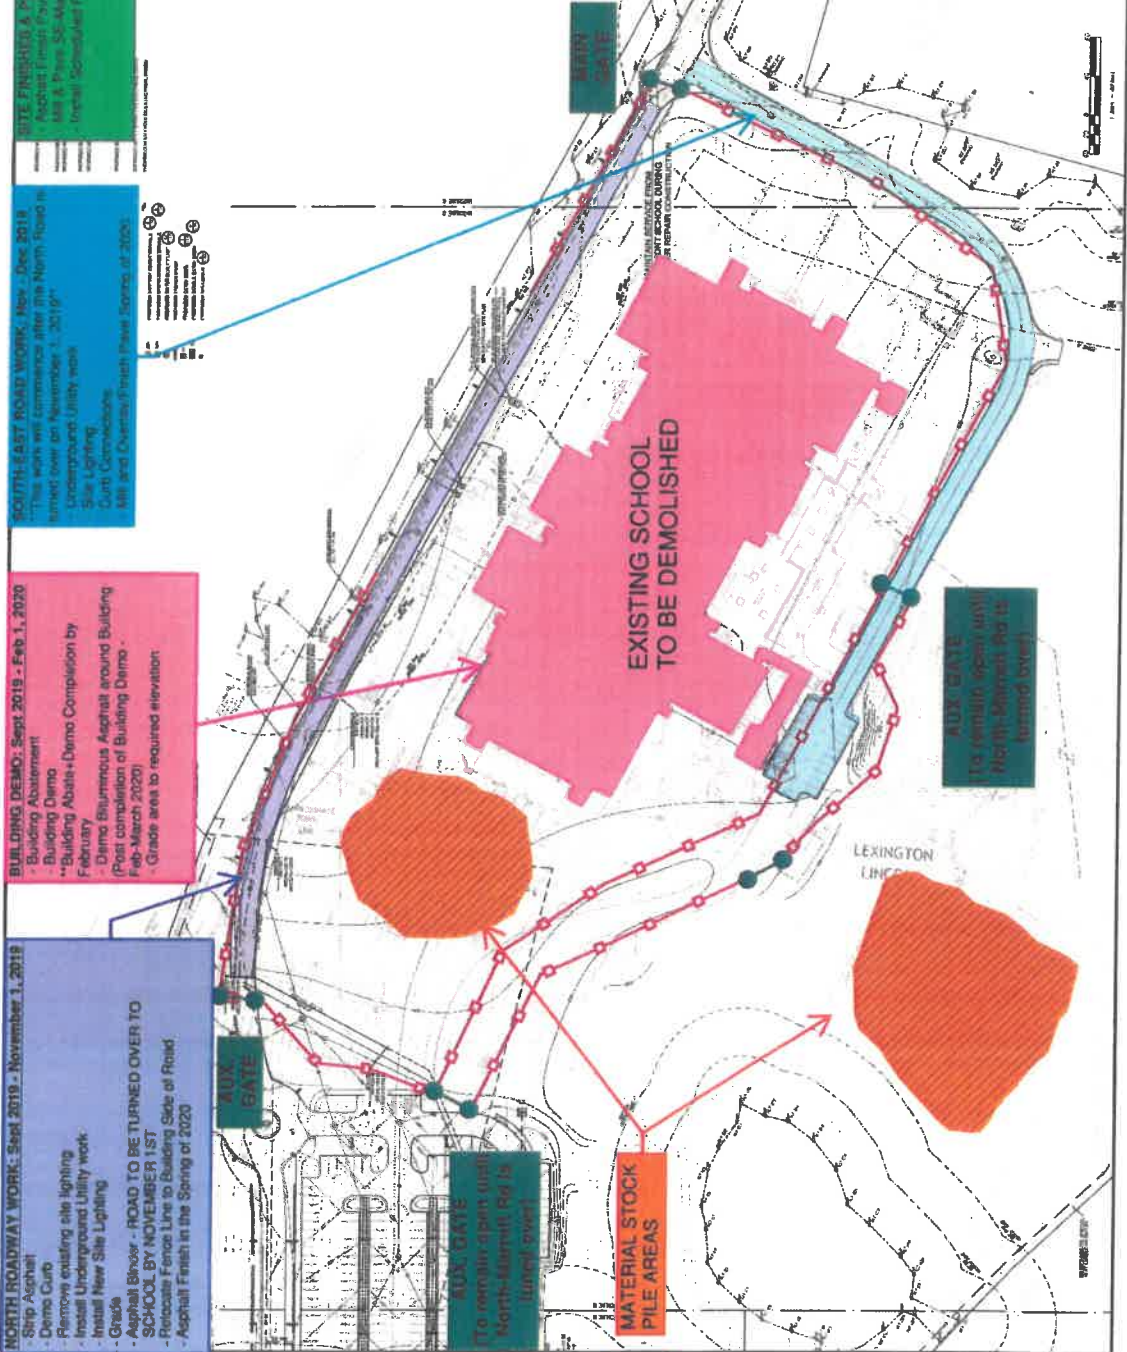

NORTH ROADWAY WORK, Sept 2019 - November 1, 2019

- Strip Asphalt
- Demo Curb
- Remove existing site lighting
- Install Underground Utility work
- Install New Site Lighting
- Grade
- Asphalt Shoulder - ROAD TO BE TURNED OVER TO SCHOOL BY NOVEMBER 1ST
- Relocate Fence Line to Building Side of Road
- Asphalt Finish in the Spring of 2020

BUILDING DEMO; Sept 2019 - Feb 1, 2020

- Building Abatement
- Building Demo
- Building Abate + Demo Completion by February
- Demo Simultaneous Asphalt around Building (Post completion of Building Demo - Feb-March 2020)
- Grade area to required elevation

SOUTH-EAST ROAD WORK, Nov - Dec 2018

- This work will commence after the North Road is turned over on November 1, 2019
- Underground Utility work
- Site Lighting
- Curb Construction
- SB and Concrete Finish Phase Begins in 2020

CONTRACTOR: sembers

DATE: 08/20/2018

PROJECT NO: 18-001

SCALE: AS SHOWN
