

### **COUGAR MOUNTAIN MIDDLE SCHOOL / MS#6**

- Ribbon Cutting/Building Dedication Ceremony was held this last Monday April 25<sup>th</sup>.
- The work on the Sports Field continues and is expected to finish up and be ready for use over the Summer.
- Due to budget the lights for the sports field are not being installed at this time. The land use and permitting for the sports field lights has been done and lights can be installed when funding is available.



View of the Main Entry from the top floor of the Parking Garage



### **COUGAR MOUNTAIN MIDDLE SCHOOL / MS#6**





The Ribbon Cutting/Building Dedication Ceremony Held April 25th



### **COUGAR MOUNTAIN MIDDLE SCHOOL / MS#6**



Sports Field work progressing.



## HIGH SCHOOL #4 ELEMENTARY SCHOOL #17

- We are currently working with the City of Issaquah Staff to determine the construction permit issuance schedule. Current updated schedule shows start of construction Summer-2022.
- City Council voted 7-0 on April 19<sup>th</sup> to approve the Master Site Plan and Site Development Permit for the project. The written decision was issued and the 21-day appeal period started today, April 28<sup>th</sup>.
- Continuing to work with the City of Issaquah and the City of Sammamish to keep permitting processes moving along.
- The Design Team continues to work and design the site, the buildings, etc. to make everything as efficient as possible.



Updated rendering of the site looking to the Southwest.



# ISSAQUAH HIGH SCHOOL STADIUM IMPROVEMENTS


- Work includes updating and expanding the existing press box into 2 press boxes, adding additional seating and ADA accessibility to the Home stands.
- · Permit received from the City of Issaquah.
- A contractor has been chosen and the project is expected to start in early June. Construction expected to begin June 2022 and will work around Fall sports as needed.





## HOLLY STREET CAMPUS EARLY LEARNING CENTER

- The project includes improvements to the Holly Street Building (old Admin Bldg) to accommodate new ECAEP & ECE classrooms, the Child Find Program, a Health Room to serve the campus, among other amenities.
- Additional fire suppression work in the Data Center has delayed the TCO but is not expected to affect the Fall-2022 opening.
- Temporary Certificate of Occupancy (TCO) for project expected in May 2022.

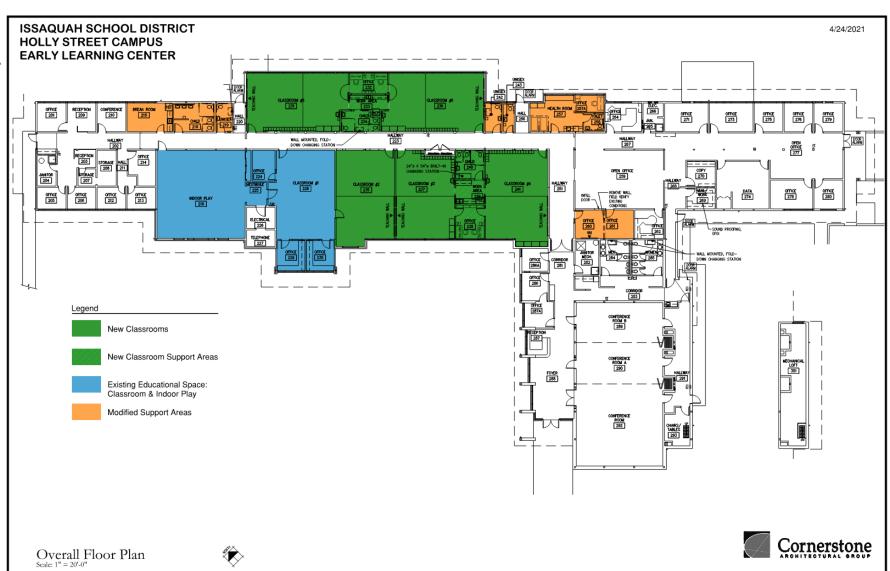



## HOLLY STREET CAMPUS CREEK BANK REPAIRS


- In Spring 2020 the rising waters of Issaquah Creek eroded a portion of the creek bank and undermining of the parking lot at the Holly Street Campus site.
- The Capital Projects Team started the very complex design and permitting for repair work within a salmon/fish bearing stream and approximately ½ mile downstream of a fish hatchery.
- Due to permitting complexities the permitting process was split up into 2 parts; temporary and permanent. The temporary work was completed in Spring 2021 and the permanent work is scheduled to be completed within "the fish window" which is July-August 2022.
- Heavier than normal rain events in January and February have led to additional damage to the creek bank.





# HOLLY STREET CAMPUS CREEK BANK REPAIRS







Temporary stream bank protection work completed

### **CAPITAL PROJECTS UPDATE**

04/28/2022

REVISED AS OF: 04/28/2022

ISSAQUAH SCHOOL DISTRICT CONSTRUCTION PROJECTS

#### PROPOSED/ANTICIPATED PROJECT SCHEDULES

					1								2019						2020						2021						2022							2023						2024						
					١.,	E D4 A		2018			LEM				6 0	N D	1 E N	M A M J J A S			O N						6 0	N D		-   10/1			Λ ς	O N		ГВ	4 A I			6 0	N D	1 6	B4 A				O N			
	START	FINISH	NO. OF	NO. OF	_	2 3 4		-	$\overline{}$	$\overline{}$				$\overline{}$	$\overline{}$	$\overline{}$						$\overline{}$		$\overline{}$		7 8	-		-	_	$\overline{}$	$\overline{}$	_		-			$\overline{}$												
	DATE	DATE	DAYS	MNTHS	1	2 3 4	<del>                                     </del>	<del>                                     </del>	3 10	11 12	1 2 3	++	<del>/  ° </del>	++++	3 10		<del>' -</del>  -	-	+++	+++	, 10	1 12	1 2	3 4	<del>/  °</del>	<del>                                     </del>	3 10	11 12	<del>                                     </del>	<del>-   °   °</del>	+ /	<del>*                                     </del>	-	10 11	12		++	<del>/  `</del>	1	3 10	11 12	1 -	1	+/+	+++*	+	+			
COUGAR MOUNTAIN MS / MIDDL			51110					ш	$\top$	$\top$												$\top \top$	$\top$		$\top$				H		Ħ				Ħ		$\top$	$\top$	+		$\vdash$				+	+	+			
1 PLANNING / DESIGN	06/01/18	02/01/20	611	20	т																																				П				$\Box$	$\top$	$\top$			
2 PERMITTING	04/01/19	07/31/20	488	16						$\Box$																															一				$\top$	$\top$	$\top$			
3 CONSTRUCTION - TCO		02/28/22	699	23												П																									П				П	$\top$	$\top$			
4 CONSTRUCTION - FIELD	03/01/22	09/01/22	185	6																																					П						$\top$			
								Ш								H						$\top \top$	T							П					П			$\Box$			П				П	$\top$	$\Box$			
HIGH SCHOOL #4 / ELEMENTARY S	SCHOOL #17							Ш		П				$\Box$		$\Box$						$\top$							П						П			$\neg \neg$			П				П	$\Box$	$\Box$			
1 PLANNING / DESIGN	06/01/18	09/01/21	1189	40	П																																				П				П		$\Box$			
2 PERMITTING	08/01/19	10/01/22	1158	39																																					П				$\Box$	$\top$				
3 CONSTRUCTION - TCO	10/01/22	09/01/24	702	23																		П	П																											
4 CONSTRUCTION - SITE & FIELDS	09/01/24	09/01/25	366	12																																									Ш					
																																									П						$\Box$			
ISSAQUAH HS - STADIUM IMPROV	/EMENTS																																								П					П	П			
1 PLANNING / DESIGN	10/01/19	11/01/20	398	13																																									П		$\Box$			
2 PERMITTING	12/01/20	05/31/22	547	18																																														
3 CONSTRUCTION	06/01/22	11/01/22	154	5																		$\perp$																			Ш'				ш		Ш			
																						Ш							Ш												Ш		Ш		Ш	Ш	Ш			
HOLLY STREET CAMPUS - EARLY LI	EARNING CEN	NTER																																																
1 PLANNING / DESIGN	01/01/20	02/01/21	398	13																																														
2 PERMITTING	02/01/21	08/03/21	184	6																																					Ш				Ш		Ш			
3 CONSTRUCTION	09/01/21	06/01/22	274	9																		$\perp$																			Ш				ш		Ш			
																						$\perp \perp$							Ш												Ш'		Ш		Ш	Ш	Ш			
HOLLY STREET CAMPUS - CREEK B	ANK REPAIRS	S																																																
1 PLANNING / DESIGN	04/01/20	07/01/22	822	27																																														
2 PERMITTING - TEMP	12/01/20	07/01/21	213	7																																					$\Box$				Ш	Ш				
3 CONSTRUCTION - TEMP	07/01/21	09/01/21	63	2																																														
4 PERMITTING - PERMANENT	10/01/21	07/01/22	274	9												$\perp \perp$						$\perp \perp$	$\perp \perp \mid$																		Ш				$\perp \perp$	$\perp \perp$	$\perp \perp$			
5 CONSTRUCTION - PERMANENT	07/01/22	09/01/22	63	2									Ш			┸																				Ш			$\perp$											
