
MONTHLY REFFERENDUM REPORT DETAILED - as of April 30, 2022



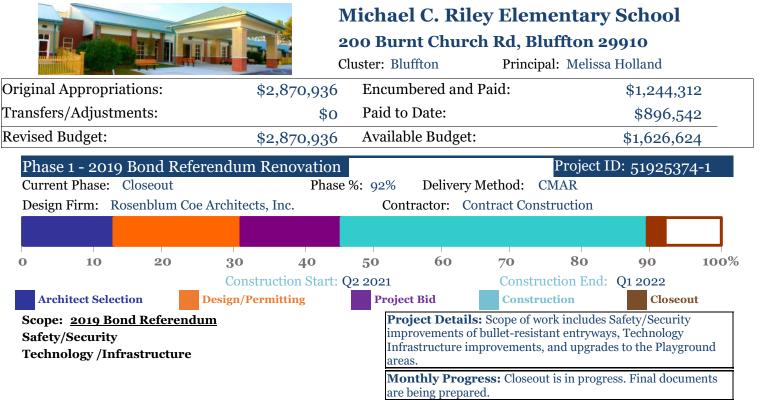

Phase 2 - 2019 Bond Referendum Renovation Project ID: 51925374-2										
Current Phase: Bid and Award Pha					se %: 45%	Delivery	Method: (CMAR		
Design Firm: Rosenblum Coe Architects, Inc. Contractor: AJAX										
0	10	20	30	40	50	60	70	80	90	100%
			Const	ruction Star	rt: Q2 2022	Construction End: Q3 2023				
Architect Selection Design/Permitt			nitting	Projec	t Bid	Construction		Close	Closeout	
Scope:2019 Bond ReferendumProject Details:Scope of work includes Safety/SecurityDesign Services (MCRES)improvements, Technology Infrastructure improvements, and upgrades to the Playground areas.										
Technology /Infrastructure						Monthly Progress: Design is complete. GMP pricing is in progress.				
