

MONTHLY REFFERENDUM REPORT DETAILED - as of April 30, 2021



Hilton Head Island High School 70 Wilborn Rd, Hilton Head Island 29926


Cluster: Hilton Head Principal: Steve Schidrich

Original Appropriations:	\$10,136,415	Encumbered and Paid:	\$1,127,734
Transfers/Adjustments:	\$0	Paid to Date:	\$973,039
Revised Budget:	\$10,136,415	Available Budget:	\$9,008,681

Phase 1 - 2019 Bond Referendum Renovation

Project ID: 51925396-1

Current Phase: Closeout Phase %: 93% Delivery Method: CMAR
Design Firm: Jumper Carter Sease Architects Contractor: M.B. Kahn Construction Company, Inc.



Scope: 2019 Bond Referendum
Athletics
Design for building renovations


Project Details: Phase 1 scope of work includes stadium improvements to the lights.
Monthly Progress: Construction is complete. Design firm reviewing closeout documents.

Phase 2 - 2019 Bond Referendum Renovation

Project ID: 51925396-2

Current Phase: Design Phase %: 11% Delivery Method: CMAR
Design Firm: McMillan Pazden Smith Architecture Contractor: H.G. Reynolds Co, Inc.

Project timeline to be determined.

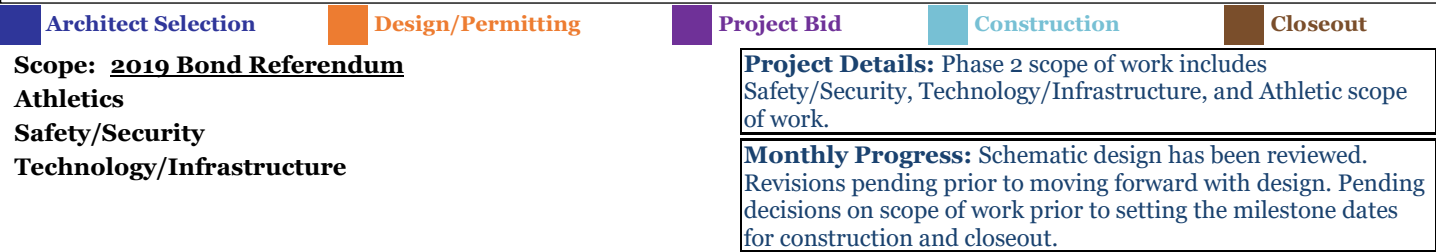

Scope: 2019 Bond Referendum
Athletics
Safety/Security
Technology/Infrastructure

Project Details: Phase 2 scope of work includes Safety/Security, Technology/Infrastructure, and Athletic scope of work.
Monthly Progress: Schematic design has been reviewed. Revisions pending prior to moving forward with design. Pending decisions on scope of work prior to setting the milestone dates for construction and closeout.
