

# MONTHLY REFFERENDUM REPORT DETAILED - as of April 30, 2021



## Whale Branch Elementary School 15 Stuart Point Rd, Seabrook 29940

Cluster: Whale Branch    Principal: Melissa Vogt


Original Appropriations:	\$1,804,823	Encumbered and Paid:	\$2,984,070
Transfers/Adjustments:	\$1,257,441	Paid to Date:	\$296,907
Revised Budget:	\$3,062,264	Available Budget:	\$78,194

### Phase 1 - 2019 Bond Referendum Renovation

Project ID: 51925354-1

Current Phase: Closeout    Phase %: 97%    Delivery Method: CMAR

Design Firm: Rosenblum Coe Architects, Inc.    Contractor: Contract Construction



**Scope: 2019 Bond Referendum**  
**Safety/Security**  
**Technology /Infrastructure**

**Project Details:** Phase 1 scope of work includes Safety/Security improvements for bullet-resistant entryways and Technology/Infrastructure improvements for radio reception and server room upgrades.


**Monthly Progress:** Construction complete. Closeout to take place with Phase 2.

### Phase 2 - 2019 Bond Referendum Renovation

Project ID: 51925354-2

Current Phase: Construction    Phase %: 23%    Delivery Method: CMAR

Design Firm: Rosenblum Coe Architects, Inc.    Contractor: Contract Construction



**Scope: 2019 Bond Referendum**  
**Safety/Security**  
**Technology /Infrastructure**

**Project Details:** Phase 2 scope of work includes Safety/Security upgrades to mass notification, door contacts and cameras. Technology/Infrastructure improvements include emergency generator, cabling sound/lighting systems, and intrusion alarms.


**Monthly Progress:** Construction in progress. Submittals in progress.

# MONTHLY REFFERENDUM REPORT DETAILED - as of April 30, 2021



## Whale Branch Elementary School

### Facilities Update by Project Cont.

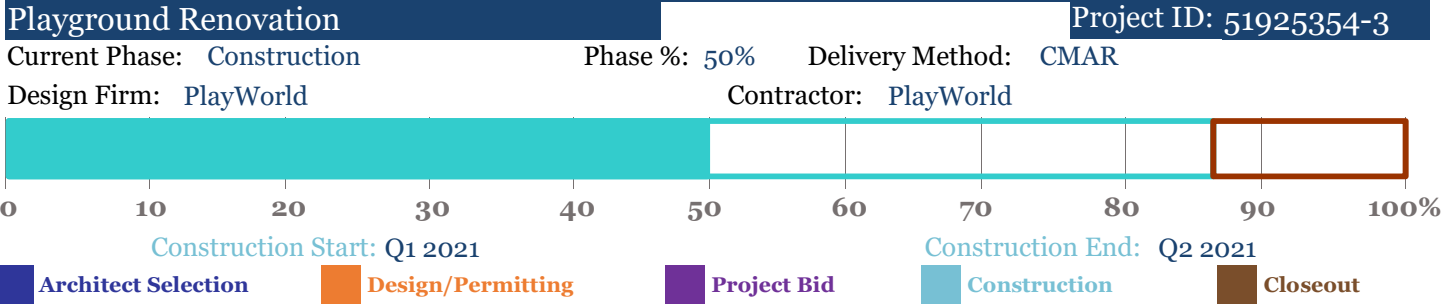

**Scope: 2019 Bond Referendum  
Playgrounds**

**Project Details:** Scope of work includes new playground equipment and surface areas.  
**Monthly Progress:** Construction in progress. Turf surface and soccer field is pending completion prior to closeout.
