

Westwood View Elementary School WEEKLY PROGRESS REPORT 06.17.22



Final Cleaning in Classrooms

This Week: 06/13/22 - 06/17/22

- Cont. Metal Panel Install
- Polished Concrete Grinding & Stain
- Light Fixtures Throughout
- Low Voltage Trim-Out Throughout
- Upper Area C Casework Install
- Electrical Device Trim-Out
- Turf & Playground Equipment
- Grading (Front of Building)
- Curb Staking & Pours
- Continued Flatwork
- Specialties & Finishes

Next Week: 06/20/22 - 06/24/22

- Playground Equip. & Turf
- Doors, Hardware, Specialties
- Cont. Casework Install
- Cont. Elec Trim-Out & Lights
- Entry/Lobby Polished Concrete
- Area C Final Cleaning
- Pre-Punch Work

Weather Days this week:

- (0) Days



Baffle Ceilings



Corridor Wall Panels Installed

Fencing Installation



Additional Photos



Front Outdoor Classroom Progress



Commons Area Polished Concrete (Protected)



Final Grading & Curb Layout



Media Center Outdoor Classroom Footing & Wall Rebar

Westwood View Elementary School WEEKLY PROGRESS REPORT 06.10.22



Playground Equipment Installation



Area C Stair Rails

This Week: 06/06/22 - 06/10/22

- Cont. Metal Panel Install
- Polished Concrete Grinding
- Light Fixtures Throughout
- Low Voltage Cabling Throughout
- Upper Area C Casework Install
- Wood Doors & Storefront Doors
- Electrical Device Trim-Out
- Interior & Exterior Stair Railing
- Playground Equipment
- Grading (Front of Building)
- Doors, Hardware, Specialties

Next Week: 06/13/22 - 06/17/22

- Sitework Phase 2 (Front of Building)
- Cont. Metal Panel Installation
- Playground Equip. & Turf
- Doors, Hardware, Specialties
- Cont. Casework Install
- Outdoor Classroom Steel
- Pre-Punch Work

Weather Days this week:

- (3) Days (Sitework ONLY)



Gym Thin Stone Veneer



Lower Level Polished Concrete Staining

Additional Photos



Site Stair & Ramp Rails



Media Center Lighting & Carpet Flooring



Front Outdoor Classroom Footings & Walls



Commons Area Polished Concrete Grinding

Westwood View Elementary School WEEKLY PROGRESS REPORT 05.27.22



Hardplay Asphalt

This Week: 05/23/22 - 05/27/22

- Cont. Metal Panel Install
- Polished Concrete Stain & Seal
- Light Fixtures Throughout
- Low Voltage Cabling Throughout
- Area C Casework Install
- Unit Start Up - All Areas
- Site Grading - West & South
- Wood Doors & Storefront Doors
- Kitchen Equipment Install
- Cafeteria Coiling Door Install
- Ceiling Tile Borders Throughout

Next Week: 05/30/22 - 06/03/22

- Sitework Phase 2 (Front of Building)
- Cont. Metal Panel Installation
- Cont. Polished Concrete Grinding
- Playground Equip. & Turf
- Doors, Hardware, Specialties
- Cont. Casework Install
- Outdoor Classroom Steel

Weather Days this week:

- (4) Days (Sitework ONLY)



Polished Concrete - Staining & Sealing



Classroom Casework & Countertops



Kitchen Equipment Install

Additional Photos



Window Sill Install



Cafeteria Coiling Door Installed



Main Lobby Light Fixture Install



Ramp & Trash Enclosure Footings

Westwood View Elementary School WEEKLY PROGRESS REPORT 05.20.22



Continued Metal Panels Throughout



Main Entry Canopy Progress

This Week: 05/16/22 - 05/20/22

- Cont. Metal Panel Install
- Hardplay Asphalt & Curbs
- Elevator Install Complete
- Polished Concrete Grinding
- Light Fixtures Throughout
- Low Voltage Cabling Throughout
- Area C Casework Install
- Turf Soccer Field Install
- Permanent Power Start-Up
- Electrical Trim-Out Throughout
- General Site Clean Up

Next Week: 05/23/22 - 05/27/22

- Sitework Phase 2 (Front of Building)
- Cont. Metal Panel Installation
- Cont. Polished Concrete
- Playground Equip. & Turf
- Cont. LV and Intercom Cabling
- Doors, Hardware, Specialties
- Cont. Casework Install

Weather Days this week:

- (2) Days (Sitework ONLY)



Turf Field Progress



Entry Vestibule Storefront Frames

Additional Photos



Area C Polished Concrete Grinding



Classroom Casework Installation



Cafeteria Canopy Metal Panel Work



Corridor Booth Installation

Westwood View Elementary School WEEKLY PROGRESS REPORT 05.06.22



Continued Tectum Panel Installation

This Week: 05/02/22 - 05/06/22

- Area C Metal Panels
- Cont. Aluminum Frames & Glass
- Entry Canopy Masonry
- Gym Tectum Panels & MEP Trim
- Turf Soccer Field Install
- Cont. Interior Storefront
- Final Corridor Paint & Tile
- Light Fixtures Throughout
- Cont. Carpet Flooring Area C
- Elevator Install
- Low Voltage Cabling Throughout

Next Week: 05/09/22 - 05/13/22

- Cont. Site Grading & Sidewalks
- Cont. Metal Panel Installation
- Cont. Elevator Install
- Playground Equip. & Turf
- Asphalt Hardplay Area
- Cont. LV and Intercom Cabling
- Area C Polished Concrete

Weather Days this week:

- (3) Days (EXTERIOR ONLY)



Continued Metal Panel Installation



Media Center Storefront Frames



Front Façade Glazing

Additional Photos



Area B Casework Installation



Continued Wall Tile Throughout



Commons Ceiling Cloud MEP Trim-Out



Corridor Final Paint & Linear Light Fixtures

Westwood View Elementary School WEEKLY PROGRESS REPORT 04.29.22



Gymnasium Equipment & Tectum Panels



Commons Area Ceiling Paint & Clouds

This Week: 04/25/22 - 04/29/22

- Area C Metal Panels
- Cont. Aluminum Frames & Glass
- Area A & B Masonry Veneer
- Gym Paint & Tectum Panels
- Gym Equipment Install
- Cont. Sidewalks at Play Area
- Commons Ceiling Paint & Clouds
- Area A & B Interior Storefront
- North Retaining Wall
- Cont. Site Grading & Black Dirt
- Elevator Delivery & Mobilization

Next Week: 05/02/22 - 05/06/22

- Cont. Site Grading & Sidewalks
- Main Entry Masonry Veneer
- Cont. Metal Panel Installation
- Elevator Install
- Media Center Ceiling Grid
- Playground Equip. & Turf
- Asphalt Hardplay Area

Weather Days this week:

- (0) Days



Metal Panel Installation



Continued East Side Flatwork

Additional Photos



Elevator Equipment Delivered



Casework Delivered



North Side Retaining Wall



Area A/B Masonry Veneer

Westwood View Elementary School WEEKLY PROGRESS REPORT 04.22.22



Gymnasium Equipment Install

This Week: 04/18/22 - 04/22/22

- Area C Metal Panels & Coping
- Cont. Aluminum Frames & Glass
- Area A & B Masonry Veneer
- Gym Wall Paint
- Gym Equipment Install
- Play Area Sidewalks & Stairs
- Upper Level C Corridor Wall Tile
- Area A & B Prime & 1st Coat Paint
- Kitchen Epoxy Flooring
- North Side Retaining Wall



Area A & B Masonry Veneer

Next Week: 04/25/22 - 04/29/22

- Cont. Site Grading & Sidewalks
- Cont. Area A/B Masonry Veneer
- Cont. Metal Panel Installation
- Gym Tectum Wall Panels
- Elevator Delivery & Install
- Media Center Ceiling Grid
- MEP Trim-Out Throughout

Weather Days this week:

- (1) Day (Exterior ONLY)



Area B Corridor Paint



North Side Retaining Wall

Additional Photos



Area C Brick Washdown



Upper Level C Corridor Wall Tile



Gym Stair Pours



Electrical Sub Panels Delivered

Westwood View Elementary School WEEKLY PROGRESS REPORT 04.15.22



East Side Retaining Walls



East Side Flatwork

This Week: 04/11/22 - 04/15/22

- Area A Masonry Veneer
- Area C Upper Carpet Flooring
- Gym Wall Priming
- Area C Bathroom Accessories
- East Side Retaining Walls
- Playground Area Sidewalks
- Main Switch Gear Delivery
- Set DOAS Units
- Metal Panel System Installation
- Area C Corridor Wall Tile

Next Week: 04/18/22 - 04/22/22

- Gym Wall & Ceiling 1st Coat Paint
- Cont. Area A/B Masonry Veneer
- Cont. Metal Panel Installation
- Area C Wire Pull & Trim Out
- Continued Sidewalks
- Area B Prime & 1st Coat Paint
- Gym Wall Tectum

Weather Days this week:

- (1) Day (Exterior ONLY)



Toilet Partition Installation



Corridor Wall Tile

Additional Photos



DOAS Units Set



Gymnasium Wall Priming



Area C Corridor Wall & Ceiling Paint



Bathroom Accessories

Westwood View Elementary School WEEKLY PROGRESS REPORT 04.08.22



Gym Ceiling Tectum Panels



Area C Masonry Veneer Progress

This Week: 04/04/22 - 04/08/22

- Cont. Area C Masonry Veneer
- Cont. Area C Lower Carpet Flooring
- Gym Ceiling Tectum Panels
- Area C Plumbing Fixtures
- East Side Final Grading
- Playground Area Sidewalks
- Upper Level C Corridor Painting
- Roof Gas Piping
- Corridor Wall Tile
- Area A Ceiling Grid

Next Week: 04/11/22 - 04/15/22

- Cont. Area C Corridor Wall Tile
- Gym Wall & Ceiling Paint
- Area A/B Masonry Veneer
- Metal Panel Installation
- Set DOAS Units
- Area C Wire Pull & Trim Out
- Upper Level C Carpet Tile
- East Side Retaining Walls

Weather Days this week:

- (0) Days



Main Entry Sheathing



Upper Level Corridor Painting

Additional Photos



Gym Stair Pours



Reception Soffit Drywall



Media Center Drywall Finishing



East Side Final Grading & Sidewalk Prep

Westwood View Elementary School WEEKLY PROGRESS REPORT 04.01.22



Gym Ductwork and Ceiling Tectum Panels



Learning Stairs & Gym Stair Footings

This Week: 03/28/22 - 04/01/22

- Cont. Area C Masonry Veneer
- Cont. Area C Upper Ceiling Grid
- Cont. Area A Drywall Finish
- Cont. Area C Lower Carpet Flooring
- Gym OH MEP & Tectum
- Area C Plumbing Fixtures
- Gym Learning Stairs
- East Side Site Grading & Haul Off
- Sidewalk Layout & Staking
- Upper Level C Corridor Painting

Next Week: 04/04/22 - 04/08/22

- Cont. Area C Corridor Wall Tile
- Gym Tectum Panels
- Area B & A Prime & 1st Coat Paint
- Area C Elec. Wire Pull & Trim-Out
- East Side Retaining Walls
- East Side Sidewalks
- Area A & B Epoxy Flooring
- Remaining Area C Windows

Weather Days this week:

- (2) Days (Exterior ONLY)



Lower Level Carpet Protection



Upper Level Ceiling Grid & Paint

Additional Photos



East Side Grading & Haul Off



Reception Soffit Framing



Area C Masonry Veneer Progress



Door Frame Paint Throughout

Westwood View Elementary School WEEKLY PROGRESS REPORT 03.25.22



Lower Level Corridor Wall Tile



Upper Level Ceiling Grid & Paint

This Week: 03/21/22 - 03/25/22

- Cont. Area C Masonry Veneer
- Area C Upper Storefront
- Cont. Area C Upper Ceiling Grid
- Cont. Area A Drywall Finish
- Gym Storage/Bathroom CMU Walls
- Area C Corridor Wall Tile
- Cont. Area C Painting
- Area C Lower Carpet Flooring
- Gym OH MEP & Tectum
- Area C Lower Plumbing Fixtures

Next Week: 03/28/22 - 04/01/22

- Gym Stair Footing Pours
- Cont. Area C Corridor Wall Tile
- Gym Tectum Panels
- Area B & A Prime & 1st Coat Paint
- Area C Elec. Wire Pull & Trim-Out
- East Side Site Grading
- Sidewalk Layout & Staking
- East Side Retaining Walls

Weather Days this week:

- (3) Days (Exterior ONLY)



Lower Level Carpet Install



Gymnasium Louvers & Ceiling Tectum

Additional Photos



Interior Storefront & Glass Throughout



Lower Level Plumbing Fixture Install



Upper Level Soffit Drywall Finishing



Area A Drywall Finishing

Westwood View Elementary School WEEKLY PROGRESS REPORT 03.18.22



Lower Level Wall & Ceiling Paint



Bathroom Epoxy Flooring & Wall Tile

This Week: 03/14/22 - 03/18/22

- Cont. Area C Masonry Veneer
- Area C Upper Storefront Frames
- Area C Upper Ceiling Grid
- Cont. Area B Drywall Finish
- Continued Window Frames & Glass
- Gym Stair Footing Excav. & Rebar
- Area C Upper Bathroom Wall Tile
- Area A Drywall Hang
- Epoxy Bathroom Flooring
- Cont. Area C Painting

Next Week: 03/21/22 - 03/25/22

- Gym Stair Footing Pour
- Cont. Area B Drywall Finishing
- Area C Plumbing Fixtures
- Area C Corridor Wall Tile
- Cont. Area C Upper Ceiling Grid
- Cont. Gym Overhead MEP
- Gym Tectum Panels
- East Side Site Grading

Weather Days this week:

- (0) Days



Lower Level MEP Ceiling Trim-Out



VRF Roof Units Delivered & Installed

Additional Photos



Lobby Soffit Drywall



Interior Precast Patchwork



Area C Masonry Veneer Progress



Continued Classroom Paint

Westwood View Elementary School WEEKLY PROGRESS REPORT 03.04.22



Gym Slab-on-Grade Poured

This Week: 02/28/22 - 03/04/22

- Cont. Area C Masonry Veneer
- Area C Lower Storefront Frames
- Area C Lower Ceiling Grid
- Cont. Area C Upper Drywall Finish
- Continued Window Frames & Glass
- Gym Slab-on-Grade Pour
- Area C Lower Bathroom Wall Tile
- Area B Drywall Finishing
- Roofing Membrane Complete
- Area C Upper Level Wall Priming

Next Week: 03/07/22 - 03/11/22

- Gym Stair Footings
- Area A Drywall Hang
- Cont. Area B Drywall Finishing
- Epoxy Bathroom Flooring
- Area C Lower Wall Trim-Out
- Area C Lower Ceiling Trim-Out
- Cont. Wall Tile, Storefront, & Grid
- Gym Overhead MEP

Weather Days this week:

- (0) Days



Continued Area C Brick Veneer



Window Frames Caulked



Continued Wall Tile

Additional Photos



Main Entry Soffit Framing



Continued Interior Storefront & Glass



Area C Corridor Wall Priming



Cafeteria/Kitchen In-Wall & Overhead MEP

Westwood View Elementary School WEEKLY PROGRESS REPORT 02.25.22



Area C - Window Frames & Glass Installed



Door Frames Installed Throughout

This Week: 02/21/22 - 02/25/22

- Cont. Area C Masonry Veneer
- Area A OH MEP Rough-In
- Area C Lower Storefront Frames
- Area C Lower Ceiling Grid
- Area A Interior Framing
- Area C Upper Level Drywall Finish
- Continued Window Frames & Glass
- Gym SOG Prep & Underslab Elec.
- Area C Lower Bathroom Wall Tile
- Doors Frames Installed Throughout

Next Week: 02/28/22 - 03/04/22

- Cont. Area C Masonry Veneer
- Complete Roofing Membrane
- Area B Drywall Finishing
- Cont. Lower C Priming & Painting
- Gym Slab-On-Grade Pour
- Area C Lower Level Wall Trim-Out
- Cont. Wall Tile, Storefront, & Grid

Weather Days this week:

- (2) Day Exterior Work ONLY



Gym SOG Prep & Underslab Elec.



Lower Level C Bathroom Wall Tile

Additional Photos



Lower Area C - Classroom Storefront Frames



Media Center - Soffit Framing & Drywall Hang



Upper Area C - Soffit Framing & Drywall Hang



Kitchen Wall Framing & Overhead MEP

Westwood View Elementary School WEEKLY PROGRESS REPORT 02.18.22



Area C Brick Veneer Progress

This Week: 02/14/22 - 02/18/22

- Area B & A Roofing Membrane
- Cont. Area C Masonry Veneer
- Area B OH & In-Wall MEP Rough-In
- Area A OH MEP Rough-In
- Area C Lower Level Walls Primed
- Area A Interior Framing & Rough-In
- Area C Upper Level Drywall Finish
- Area C Upper Level Soffit Framing
- Clerestory Window Frames
- Final Precast Panel Erection



Clerestory Window Frames & Flashing

Next Week: 02/21/22 - 02/25/22

- Cont. Area C Masonry Veneer
- Area A Roofing Membrane
- Cont. Upper C Drywall Finishing
- Area B Drywall Hang
- Cont. Lower C Priming & Painting
- Gym Slab-On-Grade Pour
- Area C Lower Level Wall Trim-Out

Weather Days this week:

- (2) Day Exterior Work ONLY



Area C Soffit Drywall & Finishing



Area A Wall Framing & Rough-In

Additional Photos



Lower Area C - Cont. Wall Priming



Final Precast Panel Erection



Area B In-Wall Plumbing & Electrical



Window Glass Delivered & Staged

Westwood View Elementary School WEEKLY PROGRESS REPORT 02.11.22



Area A Vapor Barrier

This Week: 02/07/22 - 02/11/22

- Framing & Sheathing Complete
- Remaining Lightweight Roof Pours
- Area A Vapor Barrier
- Area C & B Roofing Membrane
- Cont. Area C Masonry Veneer
- Area B OH & In-Wall MEP Rough-In
- Area A OH MEP Rough-In
- Area C Lower Level Walls Primed
- Area A Interior Framing
- Area C Upper Level Drywall Finish



Area B Roofing Membrane



Area C Soffit MEP Rough-In

Next Week: 02/14/22 - 02/18/22

- Cont. Area C Masonry Veneer
- Area A Roofing Membrane
- Cont. Upper C Drywall Finishing
- Area B Drywall Hang
- Cont. Lower C Priming & Painting
- Area A Interior Framing & Rough-In
- Glazing Mobilization

Weather Days this week:

- (0) Days



Area C Lower Level Priming

Additional Photos



Duct & Pipe Insulation



Cable Tray Installation



Area C Brick Veneer Progress



Area A Overhead MEP

Westwood View Elementary School WEEKLY PROGRESS REPORT 02.04.22



Area C Lower Level Soffit Framing



Area B Overhead Ductwork

This Week: 01/31/22 - 02/04/22

- Area A Ext. Framing & Sheathing
- Area A Parapet Framing & Blocking
- Waterproofing / Vapor Barrier
- Lower C Drywall Finish
- Upper C Drywall Hang
- Area B Interior Framing
- Area B OH MEP Rough-In
- Area B In-Wall Rough-In
- Area B & Gym Roofing
- Gym Piers & Grade Beam

Next Week: 02/07/22 - 02/11/22

- Cont. Area C Masonry Veneer
- Cont. Roofing
- Cont. Waterproofing / Vapor Barrier
- Cont. Upper Level C Drywall Hang
- Cont. Area B MEP Rough-In
- Glazing Mobilization
- Painting Mobilization

Weather Days this week:

- (2) Days (Exterior ONLY)



Area B Lightweight Conc. Roof Pour



Area C Upper Level Drywall

Additional Photos




Area C Masonry Progress



Area B (Admin Area) Framing



Roof Screen Framing Complete

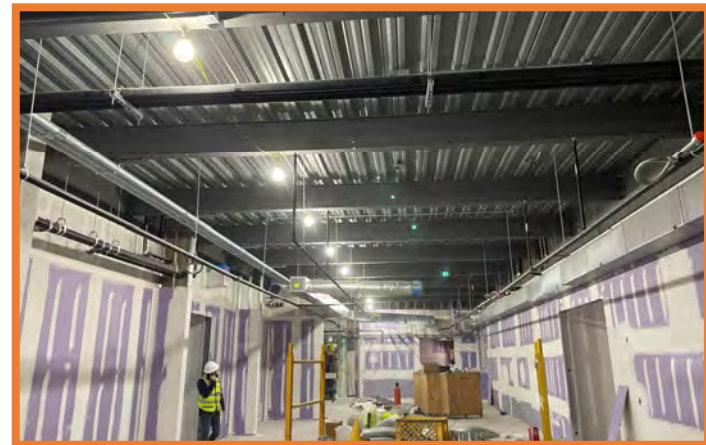

Area C Drywall Finishing & Top-Out

Westwood View Elementary School WEEKLY PROGRESS REPORT 01/28/22



Area C Lower Level Drywall

This Week: 01/24/22 - 01/28/22

- Area A Ext. Framing & Sheathing
- Area A Parapet Framing & Blocking
- Waterproofing / Vapor Barrier
- Lower C Drywall Hang & Finish
- Upper C Cont. Framing & Blocking
- Upper C Cont. OH & In-Wall Rough
- Cont. Area C Brick Veneer
- Area B Interior Framing
- Area B OH MEP Rough-In



Area C Upper Level In-Wall Blocking

Next Week: 01/31/22 - 02/04/22

- Cont. Area C Masonry Veneer
- Cont. Roofing
- Cont. Waterproofing / Vapor Barrier
- Cont. Lower Level C Drywall Finish
- Gym Roofing
- Gym Piers / Grade Beam
- Upper C Drywall Hang
- Area B In-Wall Rough-In

Weather Days this week:

- (2) Days (Exterior ONLY)



Area C Upper Level Corridor Framing



Area C Brick Veneer

Additional Photos



Area C Lower Level Drywall Tape & Finish



Area C Upper Level In-Wall Plumbing



Area C Upper Level Overhead MEP



Area A Continued Parapet Blocking

Westwood View Elementary School WEEKLY PROGRESS REPORT 01/21/22



Area B & A Roof - Primed & Insulated

This Week: 01/17/22 - 01/21/22

- Area A Ext. Framing & Sheathing
- Area A - RTU Screen Framing
- Transformer Set
- Area A Parapet Framing & Blocking
- Waterproofing / Vapor Barrier
- Cont. Gym CMU Wall
- Area A Roof Curbs
- Lower Level C Drywall Hang
- Upper Level C Framing & Blocking
- Upper Level C OH & In-Wall Rough



Gym CMU Wall Progress

Next Week: 01/24/22 - 01/28/22

- Cont. Area C Masonry Veneer
- Cont. Roofing
- Cont. Waterproofing / Vapor Barrier
- Lower Level C Drywall
- Gym Roofing
- Cont. Upper Level C MEP Rough
- Area B OH MEP Rough

Weather Days this week:

- (1) Day



Lower Level C - Drywall Delivered & Staged

Transformer Set & Temp Power Running

Additional Photos



Area B Roofing - Insulated & Membrane



Upper Level C - Framing & In-Wall Rough



Area A - RTU Screen Framing



Area A - Exterior Framing & Sheathing

Westwood View Elementary School WEEKLY PROGRESS REPORT 01/14/22



Area C Roof - Primed & Insulated



Area C Roof - Lightweight Concrete Pours

This Week: 01/10/22 - 01/14/22

- Area A Exterior Framing
- Upper Level C Interior Framing
- Canopy Steel Detailing
- Area B & A Sheathing
- Area A Parapet Framing & Blocking
- Waterproofing / Vapor Barrier
- Gym CMU Wall
- Area B & A Roof Drains
- Lower Level C In-Wall Blocking
- Upper Level C MEP Rough-In

Next Week: 01/17/22 - 01/21/22

- Cont. Area C Masonry Veneer
- Cont. Upper Level C MEP Rough-In
- Cont. Waterproofing / Vapor Barrier
- Area C Door Frames
- Lower Level C Drywall
- Area B & A Roof Curbs
- Area B Roofing

Weather Days this week:

- (0) Days



Gym CMU Wall



Stairs Set - Up to Main Lobby

Additional Photos



Media Center Framing & Sheathing



Classroom VRF Fan Coil Installation



Continued Joint Sealants & Vapor Barrier



Cafeteria Canopy Detailing

Westwood View Elementary School WEEKLY PROGRESS REPORT 12/30/21



Area C Vapor Barrier

This Week: 12/27/21 - 12/30/21

- Exterior / Interior Framing
- Exterior Sheathing
- Area A Steel Detailing
- Lower Level Wall Rough-In
- RTU Screen Wall Steel Supports
- Cont. Window Blocking
- Waterproofing / Vapor Barrier
- Area C Masonry Veneer
- Area C Roofing Mobilization
- Complete Precast Erection



Outdoor Classroom Ceiling Framing

Next Week: 01/03/22 - 01/07/22

- Area C Masonry Veneer
- Area B Framing & Sheathing
- Area C Upper Level Overhead MEP
- Cont. Waterproofing / Vapor Barrier
- Cont. Lower Level Wall Rough-In
- Complete Precast Erection

Weather Days this week:

- (1) Day



Area C Lower Level Wall Rough-In



Outdoor Classroom Brick Veneer

Additional Photos



Area C Upper Level Ductwork



Continued Area C Sheathing



RTU Screen Wall Steel Supports



Lower Level C Copper Pipe

Westwood View Elementary School WEEKLY PROGRESS REPORT 12/17/21



Area C - Exterior / Parapet Framing



Precast Mobilization



Area A - Structural Steel & Joists



Precast Panels Delivered

This Week: 12/13/21—12/17/21

- Cont. Area C Roof Decking
- Exterior Framing
- Exterior Sheathing
- Area A Structural Steel & Joists
- Area C Overhead MEP
- Parapet Framing & Sheathing
- Temp Windows & Handrails
- Precast Mobilization

Next Week: 12/20/21—12/24/21

- Cont. Area C Overhead MEP
- Cont. Exterior Framing & Sheathing
- Lower Level Interior Framing
- Cont. Area A Steel & Joists
- Gym Precast Panel Erection
- Masonry Veneer Mobilization
- Roof Drains & Curbs
- Area C Vapor Barrier

Weather Days this week:

- (0) Days

Additional Photos



Area C - Overhead Electrical Conduit



Fire Sprinkler Piping Prep



Area C - Sheathing & Temp Windows



Area A - Cafeteria Structural Steel & Joists

Westwood View Elementary School WEEKLY PROGRESS REPORT 12/10/21



Area C - Exterior Framing



Area C - Slab-on-Deck Pour #1

This Week: 12/06/21—12/10/21

- Area C Steel Detailing
- Cont. Area C Roof Decking
- Area C SOD Pour #2 & 3
- Exterior Framing
- Exterior Sheathing
- Area B Structural Steel & Joists
- Area C OH Plumbing Rough-In
- Area C Ductwork

Next Week: 12/13/21—12/17/21

- Complete Area C Roof Decking
- Temp Windows & Handrails
- Cont. Area C OH Plumbing
- Cont. Area C Ductwork
- Area C OH Electrical
- Cont. Exterior Framing & Sheathing
- Lower Level Interior Framing
- Area A Structural Steel

Weather Days this week:

- (0) Days



Transformer Pad Set



Area C - Stairs

Additional Photos



Area C - Exterior Sheathing



Area C - Overhead Ductwork



Area B - Structural Steel



Area C - Slab-on-Deck Pours 2 & 3

Westwood View Elementary School WEEKLY PROGRESS REPORT 12/03/21



Area C Structural Steel Progress



Area C Slab-on-Deck Prep

This Week: 11/29/21—12/03/21

- Area C Steel Detailing
- Cont. Area C Roof Joists
- Cont. 2nd Floor Metal Decking
- Cont. Area C Slab-on-Deck MEP
- Area C SOD Pour #1
- Exterior Framing Layout

Next Week: 12/06/21—12/10/21

- Complete Area C Roof Joists
- Area C Roof Decking
- Area C SOD Pour #2
- Area C SOD Pour #3
- Lower Level C Overhead MEP
- Temp Windows & Handrails

Weather Days this week:

- (0) Days



Slab-on-Deck MEP




Area C Stairs

Westwood View Elementary School WEEKLY PROGRESS REPORT 11/26/21



Area C Structural Steel Progress

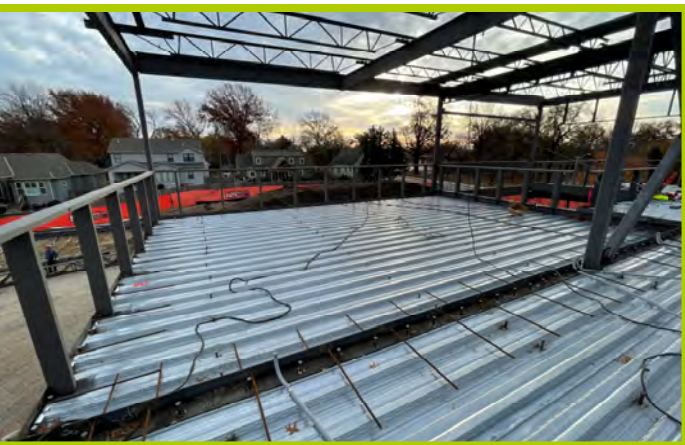

Area C Outdoor Classroom

This Week: 11/22/21—11/24/21

- Gym Vestibule CMU Walls
- Cont. Area C Steel Erection
- Area C 2nd Floor Metal Decking
- Area C Slab-on-Deck MEP
- Area C Roof Joists

Next Week: 11/29/21—12/03/21

- Cont. Area C Steel Erection
- Cont. Area C Metal Decking
- Cont. Area C Roof Joists
- Slab-on-Deck Pour 1 Prep & Pour
- Slab-on-Deck Pour 2 Prep
- Exterior Framing

Weather Days this week:

- (0) Days



Gym Vestibule CMU Walls



Area C 2nd Floor Steel & Roof Joists

Westwood View Elementary School WEEKLY PROGRESS REPORT 11/19/21



Area C Structural Steel Progress



Area C 2nd Floor Metal Decking

This Week: 11/15/21—11/19/21

- Slab-on-Grade Pours 5 & 6
- Gym Vestibule CMU Walls
- Cont. Area C Steel Erection
- Area C Metal Decking
- Area C Slab-on-Deck MEP

Next Week: 11/22/21—11/26/21

- Cont. Area C Steel Erection
- Cont. Area C Metal Decking
- Cont. Area C Slab-on-Deck MEP
- Area C Joists
- Slab-on-Deck Pour 1 Prep

Weather Days this week:

- (0) Days



Slab-on-Grade Pours 5 & 6



Gym Vestibule CMU Walls

Westwood View Elementary School WEEKLY PROGRESS REPORT 11/12/21



Area C Structural Steel



Area C Structural Steel



Area B Underground Electrical

This Week: 11/08/21—11/12/21

- Area B Grade Beams & Pads
- Area B Underslab MEP
- Area B Slab-on-Grade Prep
- Struct. Steel Mob. & Crane Delivery
- Area C Structural Steel Erection

Next Week: 11/15/21—11/19/21

- Slab-on-Grade #5 & 6 Pours
- Gym Vestibule CMU Walls
- Cont. Area C Steel Erection
- Area C Metal Decking
- Area C Slab-on-Deck MEP
- Area C Joists

Weather Days this week:

- (0) Days



Area B Slab-on-Grade Prep

Westwood View Elementary School WEEKLY PROGRESS REPORT 11/05/21



Area C Foundation Drainage & Backfill



Area B Grade Beam Reinforcement

This Week: 11/01/21—11/05/21

- Area B Grade Beams & Pads
- Area B Underslab MEP
- Steel Anchor Bolt Survey
- Struct. Steel Mob. & Crane Delivery
- General Site Housekeeping

Next Week: 11/08/21—11/12/21

- Area B Grade Footing Pours
- Area B Underslab MEP
- SOG #5 & 6 Prep
- Gym Vestibule CMU Base Courses
- Area C Steel Erection & Decking

Weather Days this week:

- (3) Days



Area B Footing Layout



Area B Underground Electrical

Westwood View Elementary School WEEKLY PROGRESS REPORT 10/29/21



Elevator Shaft Complete



Retaining Wall Backfilled & Compacted

This Week: 10/25/21—10/29/21

- Elevator Shaft Work
- Remaining Piers
- General Site Grading Cleanup
- Retaining Wall Backfill Complete
- Safety Rails at Retaining Wall
- Area A/B Column Pads
- Gymnasium CMU Base Courses

Next Week: 11/01/21—11/05/21

- Area B Grade Beams & Pads
- Area B Underslab MEP
- SOG #5 Prep
- Gym Vestibule CMU Base Courses
- Structural Steel Mobilization
- Steel Anchor Bolt Survey

Weather Days this week:

- (1) Day



Area A/B Column Pad Pours



Gymnasium CMU Base Courses

Westwood View Elementary School WEEKLY PROGRESS REPORT 10/22/21



Area A - Slab-on-Grade #4 Pour

This Week: 10/18/21—10/22/21

- Cont. Retaining Wall Backfill
- Area A SOG #4 - Prep & Pour
- Elevator Shaft Work
- Area B Remaining Piers
- Area B Column Pads
- Area B Grade Beams

Next Week: 10/25/21—10/29/21

- Gym CMU Base Courses
- Complete Elevator Shaft
- Area B Cont. Foundation Work
- Area B Underslab MEP
- Area A SOG #5 - Prep
- Steel Anchor Bolt Survey

Weather Days this week:

- (1) Day



50th ST Road Closure Work Complete



Retaining Wall Waterproofing & Backfill



Elevator Shaft Wall Progress

Westwood View Elementary School WEEKLY PROGRESS REPORT 10/15/21



Area C - Slab-on-Grade #3 Pour

This Week: 10/11/21—10/15/21

- Retaining Wall Bracing
- Cont. Retaining Wall Backfill
- Area C SOG #3 - Pour
- Area A Underslab Plumbing & Elec.
- Area A SOG #4 - Prep
- 50th Street Water Line Connection
- Elevator Shaft Mobilization



Underslab Electrical & Slab-on-Grade #4 Prep

Next Week: 10/18/21—10/22/21

- Elevator CMU Shaft Walls
- Area A SOG #4 - Pour
- Cont. Retaining Wall Backfill
- Area B Remaining Piers
- Area B Column Pads
- Area B Grade Beams
- Area B Underslab MEP

Weather Days this week:

- (2) Days



Gym Retaining Wall Backfill & Safety Rails



Retaining Wall Bracing & Elevator Shaft Mob.

Westwood View Elementary School WEEKLY PROGRESS REPORT 10/06/21



Area C - Slab-on-Grade #3 Prep & Pour

This Week: 10/04/21—10/08/21

- Wall Pour #3 (Gym) - Poured
- Cont. Retaining Wall Waterproofing
- Area C SOG #3 - Prep & Pour
- Area A Underslab Plumbing & Elec.
- Area A Stem Wall Forms & Pours
- Site Storm Water Piping
- Domestic Water Line Connections

Next Week: 10/11/21—10/15/21

- Cont. Site Utility Work
- Elevator CMU Shaft Walls
- Area A Slab-on-Grade Pour #4
- Retaining Wall Bracing
- Retaining Wall Backfill
- Area B Remaining Geopiers
- Area B Column Pads

Weather Days this week:

- (0) Days



Electrical Service - Building Entry Conduits



Area A - Stem Wall Formwork & Pours



Gym Retaining Wall - Interior Backfill

Westwood View Elementary School WEEKLY PROGRESS REPORT 09/29/21



Wall Pour #1 - Waterproofing



Area A Footing Pours & Stem Wall Rebar

This Week: 09/27/21—10/01/21

- Wall Pour #1 - Waterproofing
- Wall Pour #2 - Forms Stripped
- Wall Pour #3 (Gym) - Rebar & Form
- Domestic Water Lines
- Elevator Pit Footing
- Area A Footing Pours & Rebar
- Area A Underslab Plumbing & Elec.

Next Week: 10/04/21—10/08/21

- Cont. Domestic Water Lines
- Elevator Pit Foundation Walls
- Area A Column Pads
- Cont. Retaining Wall Waterproofing
- Area C Slab-on-Grade Pour #3
- Wall Pour #3 - Pour & Strip Forms
- Retaining Wall Bracing & Backfill

Weather Days this week:

- (0) Days



Domestic Water Lines



Elevator Pit Footing & Underslab Plumb.

Westwood View Elementary School WEEKLY PROGRESS REPORT 09/22/21



Retaining Wall Pour #2 - Rebar & Formwork

This Week: 09/20/21—09/24/21

- Wall Pour #1 - Forms Striped
- Wall Pour #2 - Rebar & Forms
- Retaining Wall Pour #2
- Cont. Storm Piping & Inlets
- Retaining Wall Waterproofing
- Cafeteria Footing Excavation
- Cafeteria Footing Reinforcement

Next Week: 09/27/21—10/01/21

- Cont. Storm Piping & Inlets
- Elevator Pit Footings & Slab
- Cafeteria Footing/Stem Wall Pours
- Cont. Retaining Wall Waterproofing
- Area C Slab-on-Grade Pour #3
- Gymnasium Retaining Wall
- Cafeteria Underground Electrical

Weather Days this week:

- (1) Day



Retaining Wall Pour #1 - Formwork Striped



Storm Sewer Piping & Inlets



Cafeteria Footing Excavation

Westwood View Elementary School WEEKLY PROGRESS REPORT 09/15/21



Area C - Slab-on-Grade Pour #2



Underground Storm Sewer Piping

This Week: 09/13/21—09/17/21

- CIP Retaining Wall Pour #1
- Slab-on-Grade Pour #2
- Gym Underground MEP
- Detention Basin Piping
- Detention Basin Backfill
- Underground Storm Sewer Piping
- Cafeteria Footing Excavation

Next Week: 09/20/21—09/24/21

- CIP Retaining Wall Pour #2
- Cont. Storm Piping & Inlets
- Elevator Pit Footings & Slab
- Gym Underground Electrical
- Cont. Cafeteria Footings
- Cafeteria Stem Walls
- Cont. Underslab MEP throughout

Weather Days this week:

- (0) Days



CIP Retaining Wall Pour #1



Gymnasium Underground Plumbing

Westwood View Elementary School WEEKLY PROGRESS REPORT 09/08/21



Classroom Wing - Retaining Wall Pours



Cafeteria Footing Excavation

This Week: 09/07/21—09/10/21

- Classroom Wing Grade Stem Walls
- CIP Retaining Wall Formwork
- Slab-on-Grade Pour #2 Prep
- Gym North Footing Excavation & Pour
- Gym Underground MEP
- Detention Basin Excavation
- Cafeteria Footing Excavation
- Cafeteria Underground MEP

Next Week: 09/13/21—09/17/21

- Cont. Sitework @ Detention Basin
- Storm Inlets
- CIP Retaining Wall Pours
- Gym Underground Plumbing Piping
- Slab-on-Grade Pour #2
- Cont. Underslab MEP throughout
- Cont. Cafeteria Footings

Weather Days this week:

- (2) Days



Underground Detention Basin Excavation



Gym Footings & Precast Embed Plates

Westwood View Elementary School WEEKLY PROGRESS REPORT 09.01.21



Classroom Wing - Slab-on-Grade Prep



Classroom Wing - Slab-on-Grade Pour #1

This Week: 08/30/21—09/03/21

- Classroom Wing Grade Stem Walls
- CIP Retaining Wall Formwork
- Classroom Wing Underslab Electrical
- Slab-on-Grade Prep and Pour #1
- Slab-on-Grade Pour #2 Base Rock
- Gym East & West Grade Beams
- Gym Underground MEP
- Detention Basin Excavation

Next Week: 09/07/21—09/20/21

- Cont. Sitework @ Detention Basin
- Storm Inlets
- CIP Retaining Wall Pour
- Dust Control Watering
- Slab-on-Grade Pour #2
- Cont. Underslab MEP
- Cafeteria Column Pads & Footings

Weather Days this week:

- (1) Day



Gymnasium - Footing Reinforcement



Underground Detention Excavation

Westwood View Elementary School WEEKLY PROGRESS REPORT 08.27.21



Classroom Wing CIP Wall Reinforcing



Classroom Wing Underslab Electrical

This Week: 08/23/21—08/27/21

- Classroom Wing Grade Beam Footings
- Dust Control Watering
- CIP Retaining Wall Forms
- Gym Foundation Concrete Pour
- CIP Retaining Wall Reinforcing
- Classroom Wing Underslab Electrical

Next Week: 08/30/21—09/03/21

- Classroom Stem Wall Concrete Pour
- CIP Retaining Wall Pour
- Dust Control Watering
- Gym Concrete Footings
- Concrete Stem Walls
- Cafeteria Concrete Grade Beams
- Classroom Slab on Grade Prep & Pour

Weather Days this week:

- (0) Days



Gym Concrete Footing Pour



Classroom Wing Progress

Westwood View Elementary School WEEKLY PROGRESS REPORT 08.13.21



Classroom Wing Underground Plumbing



Gym CIP Footing Excavation

This Week: 08/09/21—08/13/21

- Classroom Wing Grade Beam Footings
- Classroom Wing Underground MEP
- Dust Control Watering
- Gym Footing Excavation
- CIP Retaining Wall Footings

Next Week: 08/16/21—08/20/21

- Classroom Grade Beam Footings
- Building CIP Retaining Wall Footings
- Classroom Wing Underground Plumbing
- Dust Control Watering
- Gym Concrete Footings
- Concrete Stem Walls

Weather Days this week:

- (2) Days



Classroom Wing CIP Retaining Wall Footings



Classroom Wing Progress

Westwood View Elementary School WEEKLY PROGRESS REPORT 08.06.21



Classroom Wing Footings Progress

This Week: 08/02/21—08/06/21

- Temporary Access Roads
- Classroom Wing Grade Beam Footings
- Classroom Wing Underground MEP
- Dust Control Watering
- Gym Footing Excavation
- CIP Retaining Wall Footings

Next Week: 08/09/21—08/13/21

- Classroom Grade Beam Footings
- Building CIP Retaining Wall Footings
- Classroom Wing Underground Plumbing
- Dust Control Watering
- Gym Footing Excavation
- CIP Retaining Wall Footings
- Concrete Stem Walls

Weather Days this week:

- (0) Days



Classroom Wing Grade Beams



CIP Retaining Wall Footings



Gym Concrete Footing Excavation

Westwood View Elementary School WEEKLY PROGRESS REPORT 07.23.21



Area C Classroom Wing Footings

This Week: 07/19/21—07/23/21

- Temporary Access Roads
- Temporary Lay Down Pads
- Classroom Wing Spread Footings
- Classroom Wing Grade Beam Footings
- Dust Control Watering

Next Week: 07/26/21—07/30/21

- Classroom Wing Spread Footings
- Classroom Wing Grade Beam Footings
- Classroom Wing Underground Plumbing
- Dust Control Watering

Weather Days this week:

- (0) Days



Area C Classroom Wing Grade Beams



Temporary Gravel Lay Down Area



Dust Control Watering

Westwood View Elementary School WEEKLY PROGRESS REPORT 06.25.21



Building Pad Installation

This Week: 06/21/21—06/25/21

- Jobsite Office Delivered
- Site Grading
- Temporary Access Roads
- Building Pad

Next Week: 06/28/21—07/02/21

- Site Grading
- Building Pad
- Temp Access Roads & Laydown
- Jobsite Office Temporary Power
- Rammed Aggregate Pier Locates
- Rammed Aggregate Pier Mobilization
-

Weather Days this week:

- (2) Days



Site Grading



Site Grading



Dust Control Watering
