

# SM East High School WEEKLY PROGRESS REPORT 06/17/2022



**Level 1 Door Frames**



**Site Overview**

## **This Week: 06/13/22—06/17/22**

- Install Level 1 Restroom Underground Plumbing
- Pour back Level 1 Restroom Slab
- Install Level 1 Restroom Door Frames
- Continue Renovation OH Electrical Install
- Pour Interior Learning Stair CIP Walls
- Waterproof Elevator Pit

## **Next Week: 06/20/22—06/24/22**

- Continue Renovation OH Install
- Begin Renovation Wall Patch Back
- Continue Prep for Level 3 Footings & Foundations
- Roof Drain Tie-In to Existing Sewer

## **Weather Days this week:**

- (0) Days



**Level 1 Underground Plumbing**



**Form & Pour CIP Foundation Wall**



# SM East High School WEEKLY PROGRESS REPORT 06/10/2022



**Level 1 Demolition**



**Level 4 Demolition**

## **This Week: 06/06/22—06/10/22**

- Finished Installing Summer Temp. Protection.
- Continued Demo. At Level 1 ,2 & 4 Restrooms
- Formed & Poured CIP Foundation Walls
- Pour CIP Foundation Walls

## **Next Week: 06/13/22—06/17/22**

- New Openings At Level 1 ,2 & 4 Restrooms
- Summer Renovation MEP OH Install
- Waterproof Foundation Walls
- Foundation Drain and Backfill
- Prep for Level 3 Footings & Foundations

## **Weather Days this week:**

- (1) Days



**Level 2 Demolition**



**Form & Pour CIP Foundation Wall**



# SM East High School WEEKLY PROGRESS REPORT 06/03/2022



**Summer Renovation Temp. Protection**



**Site Overview**

## **This Week: 05/31/22—06/03/22**

- Redirect Roof Drain Away From Building Pad
- Touch Up Site Grading
- Continue Layout of Footings & Foundations
- Install Summer Renovation Temp. Protection
- Summer Renovation Bathroom Demolition

## **Next Week: 06/06/22—06/10/22**


- Continue Summer Renovation Bathroom Demolition
- Continue Pouring Footings & Foundations
- Wall Crew to Prep & Pour Foundation Walls

## **Weather Days this week:**

- (2) Days



**Temporarily Reroute Roof Drain**

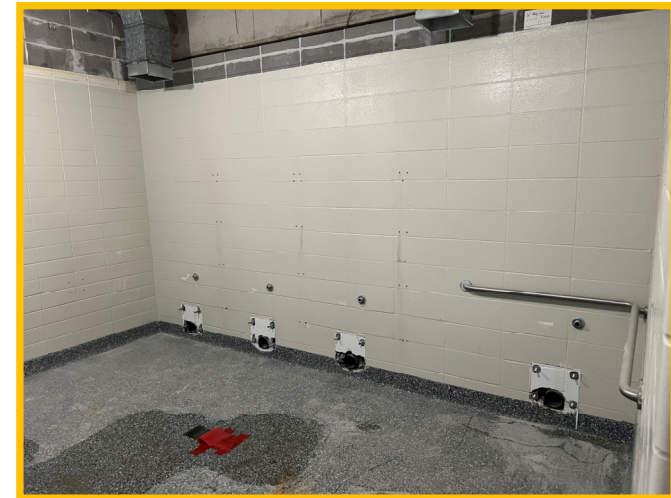

**Restroom Demolition**



# SM East High School WEEKLY PROGRESS REPORT 05/27/2022



**Began Pouring Footings & Foundations**



**Poured Gridline 3/A**

## **This Week: 05/23/22—05/27/22**

- Began Pouring Lower level Footings
- Continued Layout Of Footings & Foundations
- Begin Mobilization For Summer Work

## **Next Week: 05/31/22—06/03/22**

- Install Temp. Protection For Summer Renovations
- Make Safe Utilities For Demolition
- Continue to Pour Footings & Foundations

## **Weather Days this week:**

- (4) Days



**Poured Gridline 5/A**



**Maintaining Laydown Area**



# SM East High School WEEKLY PROGRESS REPORT 05/20/2022



**Layout Footings & Foundations**



**Site Utility Install**

## **This Week: 05/16/22—05/20/22**

- Site Utility Install
- Rebar & Reinforcement Delivery
- Layout Footings & Foundations
- Relocate Existing Fiber Line
- Begin Pouring Lower level Footings

## **Next Week: 05/23/22—05/27/22**

- Begin Mobilization For Summer Work
- Continue Site Utility Install
- Continue Pouring Footings & Foundations

## **Weather Days this week:**

- (2) Days



**Relocate Existing Fiber Line**



**Site Overview**



# SM East High School WEEKLY PROGRESS REPORT 05/13/2022



**Saw Cut Existing Footing/Haunch**



**Continue Site Grading & Compaction**

## **This Week: 05/09/22—05/13/22**

- Begin Site Utility Install
- Begin West Building Pad
- Structurally Upgrade Existing Footing/Haunch
- Lay rock for Laydown Area
- Investigate & Relocate Existing Fiber Line

## **Next Week: 05/16/22—05/20/22**

- Rebar Delivery
- Layout Footings & Foundations
- Concrete Deliveries

## **Weather Days this week:**

- (0) Days



**Added SWPP Around Stock Pile**



**Finalize Renovation Routing & Barricade Plan**



# SM East High School WEEKLY PROGRESS REPORT 05/06/2022



**Site Clearing & Grading**



**Stock Pile Haul Off**

## **This Week: 05/02/22—05/06/22**

- Site Clearing & Site Grading
- Misc. Site Demolition and Haul Off
- Connected Temp. Power
- Relocated Existing Sheds

## **Next Week: 05/09/22—05/13/22**

- Relocate Existing Fiber Cable
- Structurally Upgrade Existing Footing/Haunch
- Begin West Building Pad
- Begin Site Utilities

## **Weather Days this week:**

- (0) Days



**Relocated Existing Shed**



**Structurally Upgrade Existing Footing**



# SM East High School WEEKLY PROGRESS REPORT 04/22/2022



**Site Clearing & Grading**



**Erosion Control & Tree Protection**

## **This Week: 04/18/22—04/22/22**

- Construction Site Fencing Install
- Site Demolition
- Site Clearing & Site Grading
- Install Temp. Roads
- Begin Erosion Control
- Install Tree Protection
- Mobilize Trailer

## **Next Week: 04/25/22—04/29/22**

- Site Clearing & Site Grading
- Finish Erosion Control
- Relocate Existing Sheds
- Connect Temp. Power

## **Weather Days this week:**

- (0) Days



**Temporary Roads**



**Construction Fencing Install**
