



**GARMANN
MILLER**
ARCHITECTS
ENGINEERS

Construction Weekly

Project: Elida Local Schools

Week of: 06/07/2021

PROJECT TEAM

Owner: Elida Local Schools
Architect: Garmann/Miller
Construction Manager: Peterson Construction Company

FUTURE MEETING DATES

Date	Time	Location	Topic
06-14-2021	1300hrs	Peterson Job Trailer	Contractor Progress Meeting
06-14-2021	1030hrs	Peterson Job Trailer	Owner Project Update Meeting
06-16-2021	1000hrs	Elida District Office	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Terrazzo prep in the main entry corridor
- Ceiling installation continues in A and B
- Sitework continues for concrete
- Carpet and vinyl flooring installation taking place in the classroom wings
- Painting continues
- MEP finishes continue
- Testing and air balance has started

Planned Activities for Next Week:

- Carpet and vinyl tile installation will continue
- Terrazzo pours in the main corridor
- Ceiling pad installation continues
- Site concrete continues
- Site work will take place around the main entry
- Hazardous material abatement continues on the old elementary building
- Wood door installation will begin
- Devices will be installed by HVAC and Electrician

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Masonry work taking place on the main entry sign




Demo of the existing building is taking place

PHOTOS



Another view of the elementary demo

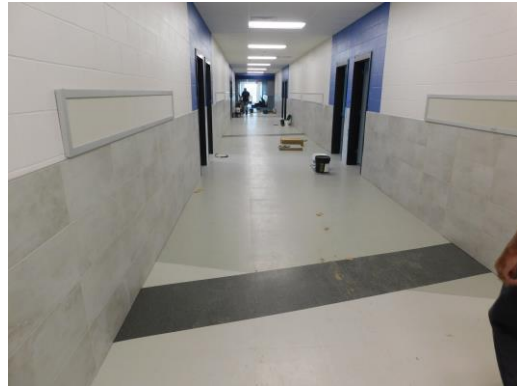

Flooring installed in the main 5th grade corridor



5th grade classroom flooring complete



Stone prep for concrete pours at main entry



More concrete pours taking place today for the playground area



Ceiling installed in the media center
