



**GARMANN
MILLER**
ARCHITECTS
ENGINEERS

Construction Weekly

Project: Elida Local Schools

Week of: 05/24/2021

PROJECT TEAM

Owner: Elida Local Schools
Architect: Garmann/Miller
Construction Manager: Peterson Construction Company

FUTURE MEETING DATES

Date	Time	Location	Topic
06-01-2021	1300hrs	Peterson Job Trailer	Contractor Progress Meeting
06-07-2021	1030hrs	Peterson Job Trailer	Owner Project Update Meeting
06-16-2021	1000hrs	Elida District Office	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Terrazzo grouting is taking place in the student dining
- Ceiling installation continues in A and B
- Sitework has started at the playgrounds
- Ceramic tile work continues throughout the 1st floor
- Roof completion items are taking place
- MEP finishes are continuing
- Air Handlers are running and have conditioned air

Planned Activities for Next Week:

- Carpet and vinyl tile installation will start in the classroom wings
- Terrazzo pours in the main corridor
- Ceiling pad installation continues
- Site concrete continues
- Site work will take place around the main entry
- Hazardous material abatement continues on the old elementary building
- Demo of the old elementary building will begin around 01 June 2021
- Devices will be installed by HVAC and Electrician

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		




Playground prep work continues



Site concrete pours taking place on the east side

PHOTOS

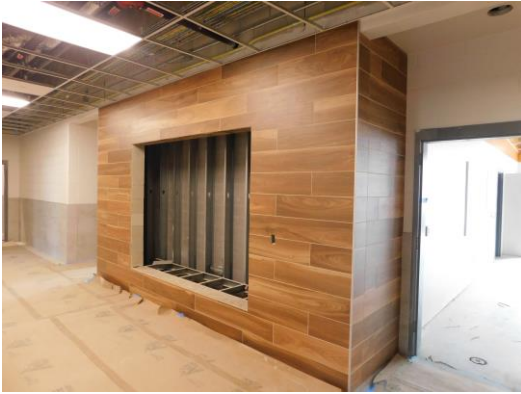

Tile installation around the display case area outside the art rooms



Epoxy flooring installed in the kitchen areas



Tech room racks and ladders installed in the main tech room



Entry door installation to the admin reception area



Toilet partition installation in one of the girls group restrooms



Toilet partition installation in one of the boys group restrooms
