



**GARMANN
MILLER**
ARCHITECTS
ENGINEERS

Construction Weekly

Project: Elida Local Schools

Week of: 05/17/2021

PROJECT TEAM

Owner: Elida Local Schools
Architect: Garmann/Miller
Construction Manager: Peterson Construction Company

FUTURE MEETING DATES

Date	Time	Location	Topic
05-24-2021	1300hrs	Peterson Job Trailer	Contractor Progress Meeting
05-24-2021	1030hrs	Peterson Job Trailer	Owner Project Update Meeting
05-19-2021	1000hrs	Elida District Office	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Terrazzo pouring is taking place in student dining
- Ceiling installation continues in A and B
- Casework installation continues on 1st floor
- Ceramic tile work continues throughout the 1st floor
- Roof completion items are taking place
- MEP finishes are continuing
- Finish paint continues on 1st floor

Planned Activities for Next Week:

- Roof finishes should be complete
- Terrazzo pours continue in the student dining and then moving to the main corridor
- Epoxy flooring will be completed in the kitchen area
- Paint continues on the 1st floor
- Casework installation will continue on 1st floor
- Playground work will continue
- Classroom flooring installation should start
- Site concrete will start back up

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Playground prep work has started



More playground prep work

PHOTOS



Window framing for the 1st floor science lab sign out room is installed



Wall tile installation continues on the main corridor




Casework installation in the main office reception area



Paint and ceiling installation in the main entryway



Wall tile installation outside of the art rooms for the display case

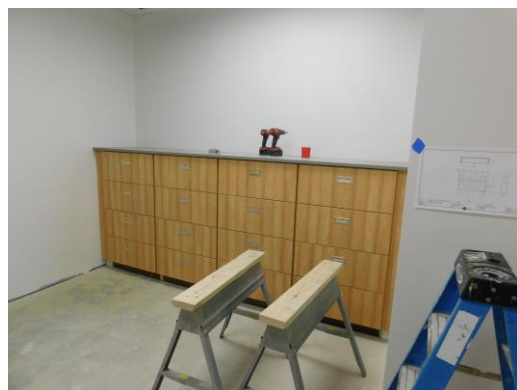

More casework installation in the admin area
