



Project: Elida Local Schools

Week of: 04/12/2021

PROJECT TEAM

Owner: Elida Local Schools.....
Architect: Garmann/Miller.....
Construction Manager: Peterson Construction Company.....

FUTURE MEETING DATES

Date	Time	Location	Topic
04-19-2021	1300hrs.....	Peterson Job Trailer.....	Contractor Progress Meeting
04-19-2021.....	1030hrs.....	Peterson Job Trailer.....	Owner Project Update Meeting
04-21-2021.....	1000hrs.....	Elida District Office.....	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Elevator installation has started
- Terrazzo grinding and polishing continue in C, D, and E
- Casework installation continues on 1st floor
- Ceramic tile work continues throughout
- Roofing work continues
- Ceiling grid continues on 1st floor pad installation on 2nd floor
- Finish paint continues on 1st floor

Planned Activities for Next Week:


- Roof panel and soffit will continue
- Terrazzo pours will start in the student dining
- MEP above ceiling on the 1st floor classroom wings continues
- Paint continues on the 1st floor
- Casework installation will continue on 1st floor
- Downspout installation continues
- Ceramic wall tile will continue
- Drywall finish and ceiling grid continues

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Ceiling tile installation in the Unit E
ELA

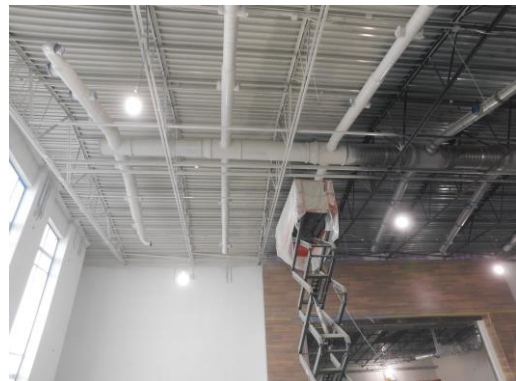


Painting of the ceiling in the student dining
has started

PHOTOS



Casework installation in the art room has started to be installed

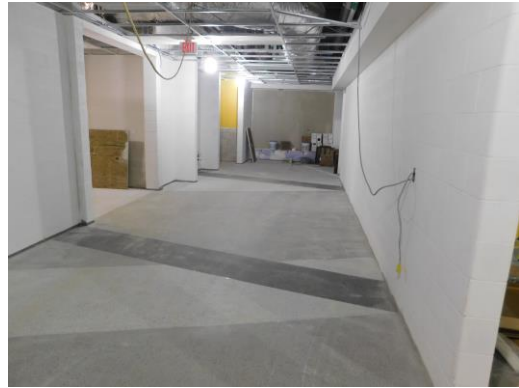

Terrazzo work in the Unit C hub area



Elevator installation has started



Ceiling pad installation in 2nd floor classroom



Marker board installation has started on the 2nd floor



Tack board installation has started on the 2nd floor
