



**GARMANN
MILLER**
ARCHITECTS
ENGINEERS

Construction Weekly

Project: Elida Local Schools

Week of: 03/29/2021

PROJECT TEAM

Owner: Elida Local Schools.....
Architect: Garmann/Miller.....
Construction Manager: Peterson Construction Company.....

FUTURE MEETING DATES

Date	Time	Location	Topic
04-05-2021	1300hrs.....	Peterson Job Trailer.....	Contractor Progress Meeting
04-05-2021.....	1030hrs.....	Peterson Job Trailer.....	Owner Project Update Meeting
04-21-2021.....	1000hrs.....	Elida District Office.....	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Ductwork continues in Units throughout 1st floor
- Terrazzo pours and grindings continue in C, D, and E
- Casework installation continues in Unit C1
- Ceramic tile work continues on 2nd floor
- Roofing work continues
- Ceiling grid continues on 1st floor
- Finish paint continues on 1st floor

Planned Activities for Next Week:

- Roof panel installation will continue
- Terrazzo grinding will continue
- MEP above ceiling on the 1st floor classroom wings continues
- Paint continues on the 1st floor
- Casework installation will continue on 1st floor
- Sound panel installation in the gym will continue
- Ceramic wall tile will continue
- Drywall finish and ceiling grid continues

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Generator has been set in place on the north side of the building




Chiller has been set on the north side of the building

PHOTOS



Stenciling is being put in place on the gym walls in preparation for painting

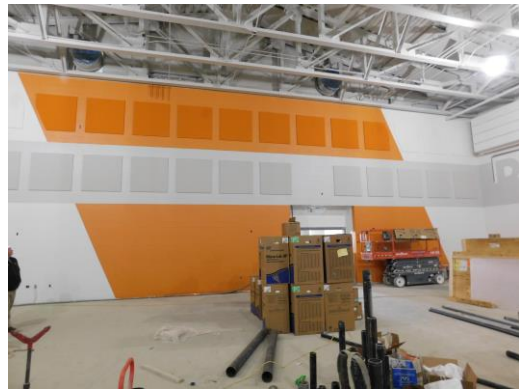

Acoustical paneling installation continues in the gym




Paint work continues in the student dining



Ceiling grid installation has taken place in one of the art rooms



Lighting is complete on the 2nd floor C "hub" classroom

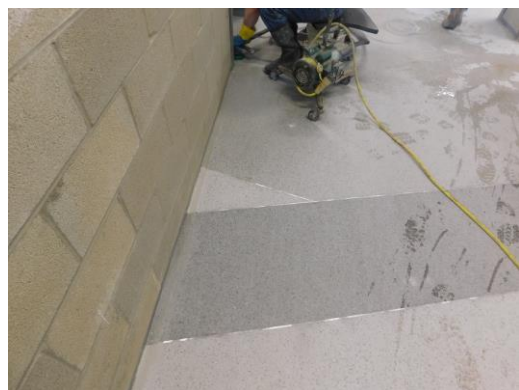

Terrazzo grinding has started in Unit C
