



Project: Elida Local Schools

Week of: 03/15/2021

PROJECT TEAM

Owner: Elida Local Schools.....
Architect: Garmann/Miller.....
Construction Manager: Peterson Construction Company.....

FUTURE MEETING DATES

Date	Time	Location	Topic
03-22-2021	1300hrs.....	Peterson Job Trailer.....	Contractor Progress Meeting
03-22-2021.....	1030hrs.....	Peterson Job Trailer.....	Owner Project Update Meeting
04-21-2021.....	1000hrs.....	Elida District Office.....	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Ductwork continues in Units C, D, E 1st floor
- Terrazzo prep and pours continue in C and E
- Casework installation continues in Unit C1, E2
- Ceramic tile work continues on 2nd floor
- Roofing work continues
- Ceiling grid continues on 1st and 2nd floor
- Finish paint continues on 1st and 2nd floor

Planned Activities for Next Week:


- Roof panel installation will continue
- Terrazzo pours will continue E1
- MEP above ceiling on the 1st floor classroom wings continues
- Paint continues on the 1st and 2nd floor
- Casework installation will continue in D and E
- Interior masonry walls will be completed
- Ceramic wall tile will continue
- Drywall finish and ceiling grid continues

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Accent painting in the 2nd floor Unit C hub

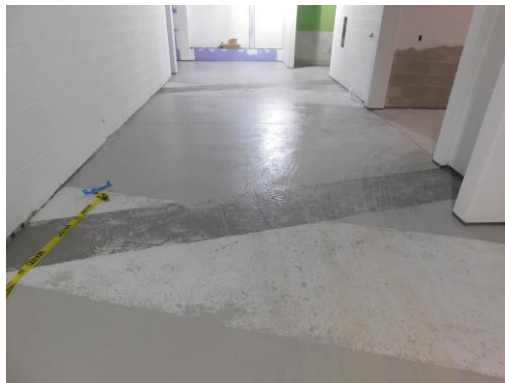

Terrazzo pours for Unit C have taken place

PHOTOS



Painting in the kitchen has started




Ceiling grid and pads installed above the stairwell Unit C




Final paint color being installed in the administration area



Clearstory windows being installed In Unit C

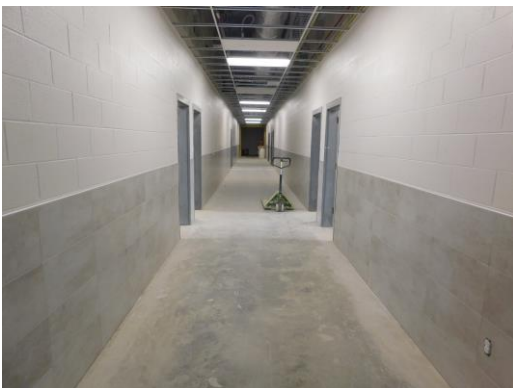

Wall tile installation along the corridor of Unit C2

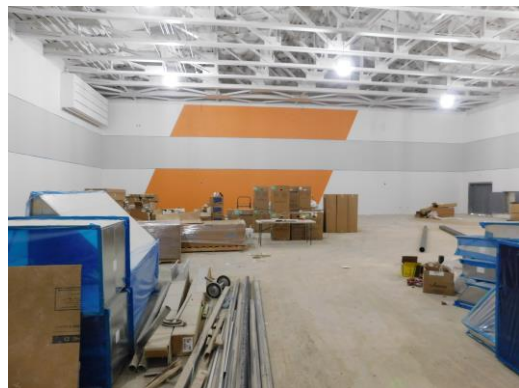

Gym accent paint continues
