



Project: Elida Local Schools

Week of: 03/08/2021

PROJECT TEAM

Owner: Elida Local Schools.....
Architect: Garmann/Miller.....
Construction Manager: Peterson Construction Company.....

FUTURE MEETING DATES

Date	Time	Location	Topic
03-15-2021	1300hrs.....	Peterson Job Trailer.....	Contractor Progress Meeting
03-15-2021.....	1030hrs.....	Peterson Job Trailer.....	Owner Project Update Meeting
03-17-2021.....	1000hrs.....	Elida District Office.....	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Ductwork continues in Units C, D, E 1st floor
- Terrazzo prep has taken place
- Casework installation continues in Unit D2, E2
- Ceramic tile work continues on 2nd floor
- Interior CMU is finishing up
- Ceiling grid continues on 1st and 2nd floor
- Finish paint continues on 1st and 2nd floor

Planned Activities for Next Week:


- Roof panel installation will continue
- Terrazzo pours will start in C1 and E1
- MEP above ceiling on the 1st floor classroom wings continues
- Paint continues on the 1st and 2nd floor
- Casework installation will continue in D and E
- Interior masonry walls will be completed
- Ceramic wall tile will continue
- Drywall finish and ceiling grid continues

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Paint continues in the gym

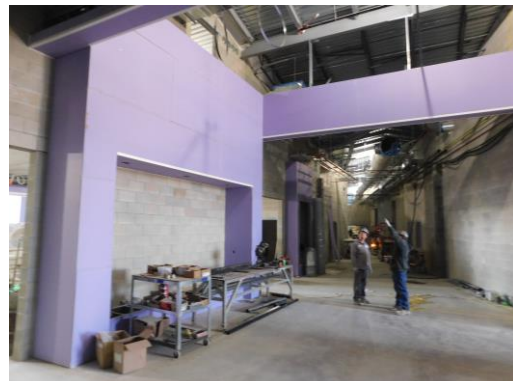

Drywall work is taking place around the main entry area

PHOTOS



Accent painting continues at the stairwell




Accent striping and layout prep is taking place on the 2nd floor




Grid installation has taken place in the 2nd floor hub classroom



Exterior door installation has taken place at the south end of Unit E

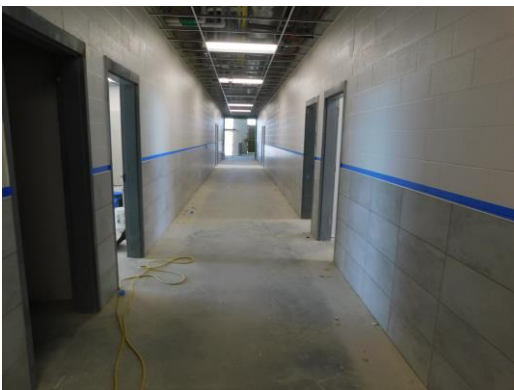

Wall tile installation along the corridor of Unit C2

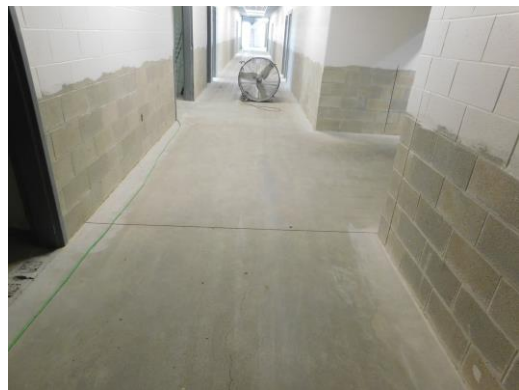

Floor prep for the terrazzo pour in the corridor C1
