



Project: Elida Local Schools

Week of: 02/22/2021

PROJECT TEAM

Owner: Elida Local Schools.....
Architect: Garmann/Miller.....
Construction Manager: Peterson Construction Company.....

FUTURE MEETING DATES

Date	Time	Location	Topic
03-01-2021	1300hrs.....	Peterson Job Trailer.....	Contractor Progress Meeting
03-01-2021.....	1030hrs.....	Peterson Job Trailer.....	Owner Project Update Meeting
03-16-2021.....	1000hrs.....	Elida District Office.....	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Ductwork continues in Units C, D, E 1st floor
- Window installation continues as glazing becomes available
- Casework installation has started in Unit D2
- Ceramic tile work continues on 2nd floor
- Interior CMU work continues in Units A and B
- Ceiling grid continues on 2nd floor
- Finish paint continues on 1st floor

Planned Activities for Next Week:

- Roof panel installation will continue soon as weather is breaking
- Glass installation will continue in Units as glazing comes in
- MEP above ceiling on the 1st floor classroom wings continues
- Paint continues on the 1st and 2nd floor
- Casework installation will continue in C and D
- Interior masonry walls will continue
- Ceiling grid will start on the 1st floor as areas become available
- Terrazzo will start next week in the C and E corridors

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Block fill paint has started on the gym walls.




Masonry walls continue in the kitchen area

PHOTOS



Cooler/Freezer installation in the kitchen area

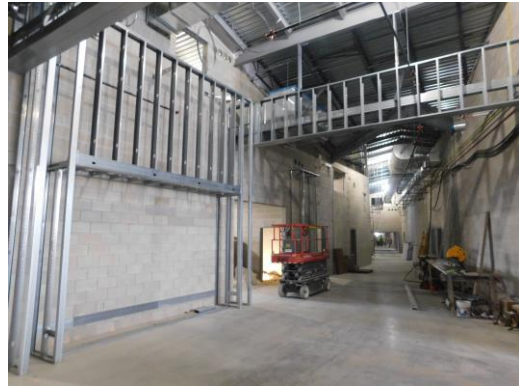

Metal stud walls and bulkhead installation around the main entry area



Casework installation has started in Unit D
2nd floor



Restroom wall and floor tile ready for
grout in group restroom on 2nd floor



Accent paint striping has started in Unit E
2nd floor ELA area



Room with casework and permanent
lighting installed and operational
