



Project: Elida Local Schools

Week of: 02/15/2021

PROJECT TEAM

Owner: Elida Local Schools.....
Architect: Garmann/Miller.....
Construction Manager: Peterson Construction Company.....

FUTURE MEETING DATES

Date	Time	Location	Topic
02-22-2021	1300hrs.....	Peterson Job Trailer.....	Contractor Progress Meeting
02-22-2021.....	1030hrs.....	Peterson Job Trailer.....	Owner Project Update Meeting
02-17-2021.....	1000hrs.....	Elida District Office.....	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:


- Ductwork continues in Units C, D, E and F 1st floor
- Window installation continues as glazing becomes available
- Casework installation has started in Unit C2
- Ceramic tile work has started on 2nd floor
- Interior CMU work continues in Units A and B
- Ceiling grid has continues on 2nd floor
- Finish paint continues on 2nd floor

Planned Activities for Next Week:

- Roof panel installation will continue as weather permits
- Glass installation will continue in Units as glazing comes in
- MEP above ceiling on the 1st floor classroom wings continues
- Paint continues on the 1st and 2nd floor
- Casework installation will continue in C and D
- Interior masonry walls will continue
- Ceiling grid will start on the 1st floor as areas become available

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		

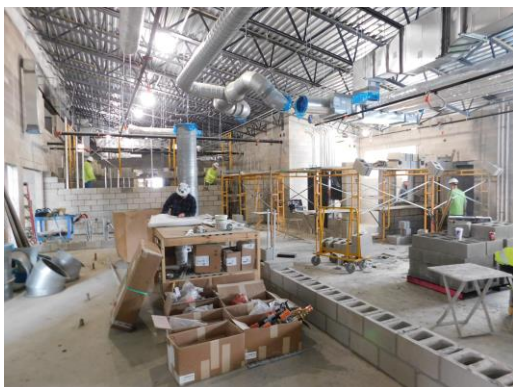

Interior walls being installed at the kitchen area



Masonry walls for the media center completed

PHOTOS




Drywall wall installed to separate the music rooms



Casework installation has started on the 2nd floor of unit C



More casework installation in Unit C 2nd floor

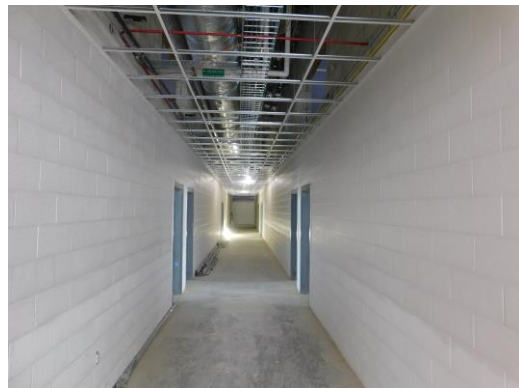

Grid installation in Unit C 2nd floor corridor



Ceramic tile being installed on the restroom wall on the 2nd floor



Ceramic tile installed on the restroom floor of a 2nd floor boys restroom
