



Project: Elida Local Schools

Week of: 01/18/2021

PROJECT TEAM

Owner: Elida Local Schools
Architect: Garmann/Miller
Construction Manager: Peterson Construction Company

FUTURE MEETING DATES

Date	Time	Location	Topic
01-25-2021	1300hrs	Peterson Job Trailer	Contractor Progress Meeting
01-25-2021	1030hrs	Peterson Job Trailer	Owner Project Update Meeting
01-20-2021	1000hrs	Elida District Office	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Ductwork continues in Units C, D, E and F 2nd floor
- Window installation continues in Units E and F
- Roof panel installation continues
- Drywall installation continues and drywall mud continues
- Interior CMU work is taking place
- Electric rough in continues in D, E and F 2nd floor
- Finish paint has started on 2nd floor this is the 2nd coat

Planned Activities for Next Week:

- Roof panel installation will continue
- Glass installation will continue in Units as glazing comes in
- MEP above ceiling on the 2nd floor classroom wings continues
- Paint in available rooms will continue
- Drywall installation will continue
- Interior masonry walls will continue
- Ceiling grid will start on 2nd floor Unit C classrooms

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Main entry stone veneer complete



Unit C hub classroom started on 2nd floor

PHOTOS



Unit C hub classroom walls being started
on 1st floor




2nd coat of paint being installed on 2nd
floor Unit C classrooms



Drywall and block fill installed for 2nd
floor classroom with operable wall



Block fill in one of the group restrooms

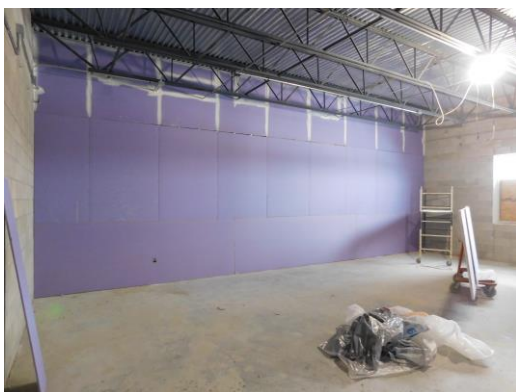

Drywall installation continues on 2nd floor
Unit D classrooms



Electrical and Ductwork continues on the
Unit B mechanical mezzanine
