



**GARMANN
MILLER**
ARCHITECTS
ENGINEERS

Construction Weekly

Project: Elida Local Schools

Week of: 11/23/2020

PROJECT TEAM

Owner: Elida Local Schools.....
Architect: Garmann/Miller.....
Construction Manager: Peterson Construction Company.....

FUTURE MEETING DATES

Date	Time	Location	Topic
11-30-2020	1300hrs.....	Peterson Job Trailer.....	Contractor Progress Meeting
11-30-2020.....	1030hrs.....	Peterson Job Trailer.....	Owner Project Update Meeting
12-16-2020.....	1000hrs.....	Elida District Office.....	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Ductwork continues in Units C, D, E and F 2nd floor
- Window installation continues in Units C, D and E
- Metal wall panel installation has started
- Metal studs are being installed on 2nd floor classroom wings
- Veneer work continues at D and E
- Electric rough in continues in D, E and F
- Overhead plumbing drains continue

Planned Activities for Next Week:

- Veneer will continue for Units D, E and F
- Glass installation will continue in Unit C, D and E
- MEP above ceiling on the 2nd floor classroom wings continues
- Paint in mechanical rooms will continue
- Metal roof panels will continue
- Interior masonry walls will continue
- MEP in wall rough continues

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Light pole bases are being drilled for placement



Metal wall panel installation is taking place on the gym

PHOTOS




Metal wall panel installation over the student dining area



In-wall blocking taking place in the admin area




HVAC above ceiling rough in taking place in the 2nd floor classroom wings

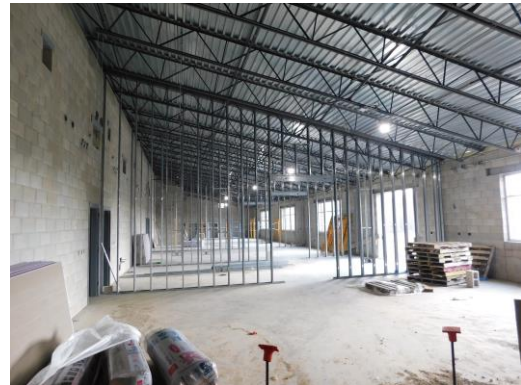

Metal studs being installed in the 2nd floor classroom wing area



Wire being pulled to panels throughout the building

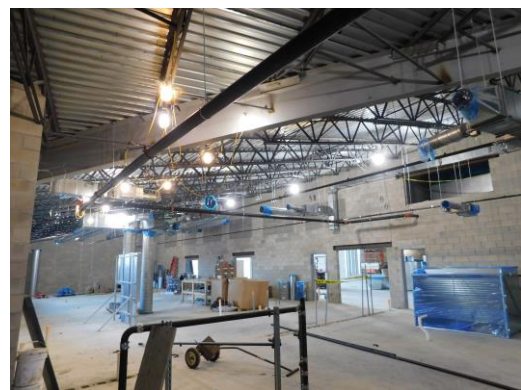

Fire suppression piping being installed in the kitchen area
