



Project: Elida Local Schools

Week of: 11/16/2020

PROJECT TEAM

Owner: Elida Local Schools
Architect: Garmann/Miller
Construction Manager: Peterson Construction Company

FUTURE MEETING DATES

Date	Time	Location	Topic
11-23-2020	1300hrs	Peterson Job Trailer	Contractor Progress Meeting
11-23-2020	1030hrs	Peterson Job Trailer	Owner Project Update Meeting
11-18-2020	1000hrs	Elida District Office	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Ductwork continues in Units A and B
- Window installation continues in Unit B and C
- Roof dry in starts on Units E and F
- Drywall top going on in classroom wings
- Veneer work continues at C and D
- Electric rough in continues in D, E and F
- Overhead plumbing drains continue

Planned Activities for Next Week:

- Veneer will continue for Units C, D and E
- Steel installation for the elevator shaft will start
- Glass installation will continue in Unit C
- Roof dry in will continue over E and F
- Concrete pads will be poured for the chiller and generator
- Metal roof panels should start soon as well as metal wall panels
- Ductwork installation continues
- MEP in wall rough continues

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Window installation taking place on Unit C 2nd floor taking place




View of Unit B veneer

PHOTOS




Veneer installed on the East side of Unit B
and window install taking place

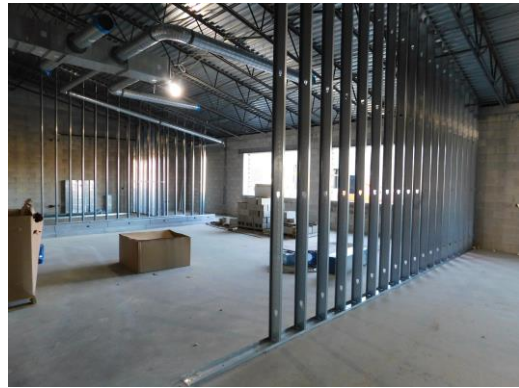


Metal stud installation taking place in the
music room



Exterior door installation being started
from the art room

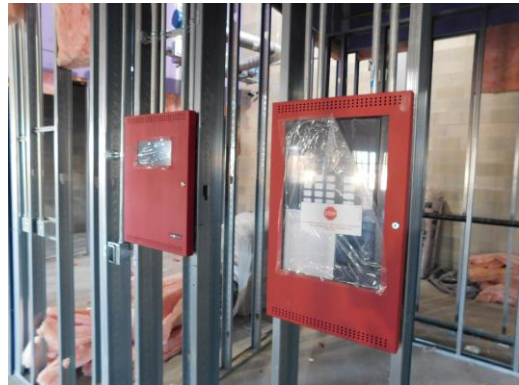

Panel installations starting in the admin
area

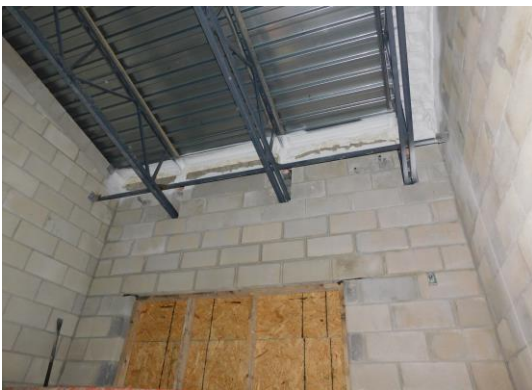

Spray foam insulation in Unit B



Louver installation in Unit A
