



**GARMANN
MILLER**
ARCHITECTS
ENGINEERS

Construction Weekly

Project: Elida Local Schools

Week of: 10/052020

PROJECT TEAM

Owner: Elida Local Schools
Architect: Garmann/Miller
Construction Manager: Peterson Construction Company

FUTURE MEETING DATES

Date	Time	Location	Topic
10-12-2020	1300hrs	Peterson Job Trailer	Contractor Progress Meeting
10-12-2020	1030hrs	Peterson Job Trailer	Owner Project Update Meeting
10-21-2020	1000hrs	Elida District Office	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- Ductwork continues in Units A and B
- Spray foam at roof to wall transitions has started in A and B
- Drywall top in the admin area has continues
- Unit E and F concrete pour for the 2nd floor is complete
- Veneer work continues at A, B and C
- Stairs are being worked on in Unit C
- Overhead plumbing drains continue

Planned Activities for Next Week:

- Veneer will continue for Units B and C
- CMU will continue in Unit C, D and E 2nd floor
- Drywall installation at the tops of wall in Admin will continue
- Roof dry in will continue
- Curtain wall windows will start in the student dining area
- Concrete pour over the Unit E will be prepped and poured
- Ductwork installation continues
- MEP in wall rough continues

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Veneer complete on the East side of the student dining



Stone veneer installation continues on the West side by the main entrance

PHOTOS




Concrete pour for the 2nd floor units E and F is complete



Steel installation is taking place at the B to C connector



Admin area drywall top out continues

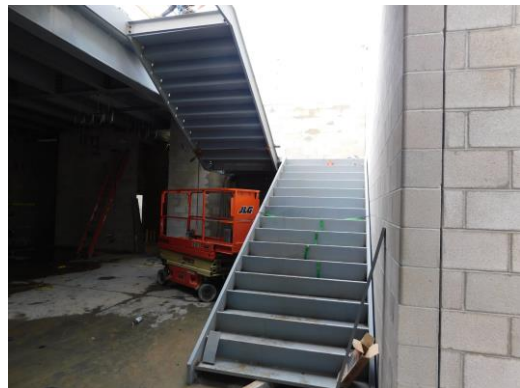

Stair installation is taking place at the C “hub”



Electrical grounding grid installation has started



Grease interceptor is on site and ready for installation outside the kitchen this week
