



**GARMANN
MILLER**
ARCHITECTS
ENGINEERS

Construction Weekly

Project: Elida Local Schools

Week of: 09/14/2020

PROJECT TEAM

Owner: Elida Local Schools.....
Architect: Garmann/Miller.....
Construction Manager: Peterson Construction Company.....

FUTURE MEETING DATES

Date	Time	Location	Topic
09-21-2020	1300hrs.....	Peterson Job Trailer.....	Contractor Progress Meeting
09-21-2020.....	1030hrs.....	Peterson Job Trailer.....	Owner Project Update Meeting
09-16-2020.....	1000hrs.....	Elida District Office.....	Core Meeting

PROGRESS UPDATE

Activities Taking Place This Week:

- CMU being installed in Units C, 2nd
- Stud welding on gym roof deck has started
- Electrical rough in for metal studs continues
- Steel installation and decking is taking place in Unit B
- Wood blocking is taking place in Unit A and B
- Roof dry in continues on Unit B
- Veneer work continues at Unit A and started on Unit B

Planned Activities for Next Week:

- Veneer will continue for Unit A and B
- CMU will continue in Unit C 2nd floor
- Rebar will be installed on roof of the gym
- Roof dry in will continue
- Electrical home runs being pulled
- Steel installation in B will continue
- Metal stud installation will start in the admin area
- MEP in wall rough continues

PROJECT ISSUES AND ACTION PLAN

Issue	Date Needed	Action
1. None currently		



Gas line installation to the North side of
Unit A



Roof decking being installed over the B/C
connector

PHOTOS




Studs installed up the East side rake wall of the gym roof for the concrete pour



Veneer work is taking place on the B/C connector above the 1st floor



View of the classroom 2nd floor area of Unit C masonry being installed

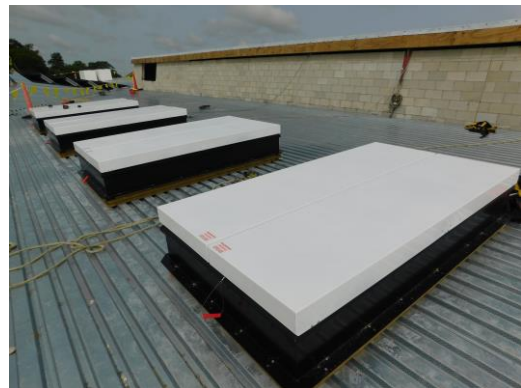

Smoke hatches installed above the stage area



View of weep tests taking place and performing properly



Duct work being brought to site and stored properly
