

Westridge Middle School

Construction Report 10/07/2022



Last Week

November 14th – November 18th

- Punch list items In Addition Area
- Punch list items in Level 1
- Remove construction fencing
- State Fire Marshal Approval of the spaces

This Week

October 24th – October 28th

- Remaining Punch list items



Addition Finished Space



Front Entry Finished Space (1)

Westridge Middle School

Construction Report 10/07/2022



Front Entry Finished Space (2)



Level 1 Finished Space



Courtyard Finished Space



Outdoor Learning Canopy Finished Space

Last Week

October 17th – October 21st

- Install Solid Surface in addition and Level 1
- Install sod at Courtyard
- Begin metal panel installation at east storefront of addition
- Complete South exterior metal panel installation
- Complete flooring in Level 1
- Complete painted wall graphic in level 1
- Begin flooring in addition
- Begin paint in addition




This Week

October 24th – October 28th

- Install remainder of glass
- Complete flooring in addition
- Complete paint in addition
- Complete solid surface install in addition
- Complete metal panel installation on east and west storefronts of addition
- Complete lighting installation in addition

Painted graphic in Level 1

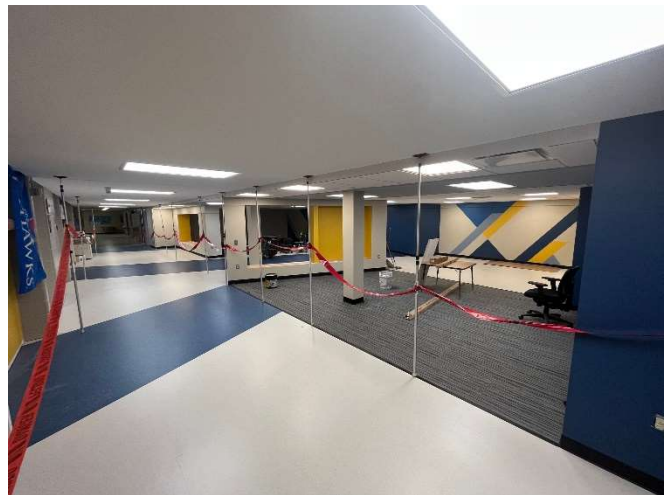

Flooring installation in Level 1

Westridge Middle School

Construction Report 10/07/2022




Courtyard sod installation complete



Flooring installation in the Addition



Solid surface installation in Level 1

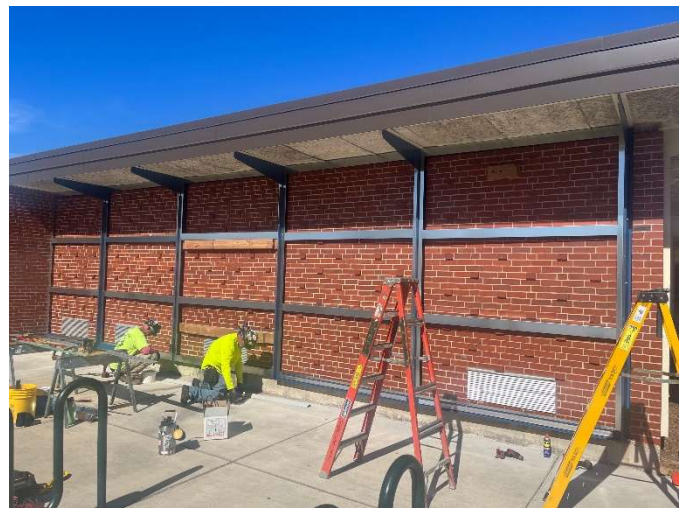

Metal wall panel installation on South Exterior

Westridge Middle School

Construction Report 07/15/2022

This Week

June 11th – June 15th

- Continued hanging and finishing drywall in 2nd floor bathroom and office area
- Began framing and ceiling grid on 1st floor area
- Poured new sidewalk as well as slab in courtyard
- Poured concrete footing as part of the 2nd floor addition



Poured new sidewalk and slab in courtyard area

Next Week

June 18th – June 22nd

- Continue MEP installation in 2nd floor bathroom
- Pour new slab in 2nd floor addition area
- Continue hanging and finishing drywall in 2nd floor conference room and offices



Poured footing in 2nd floor addition

Westridge Middle School


Construction Report 07/15/2022



Finishing drywall and doorframe installation
in 2nd floor offices



Continuing drywall installation in 2nd floor
bathrooms

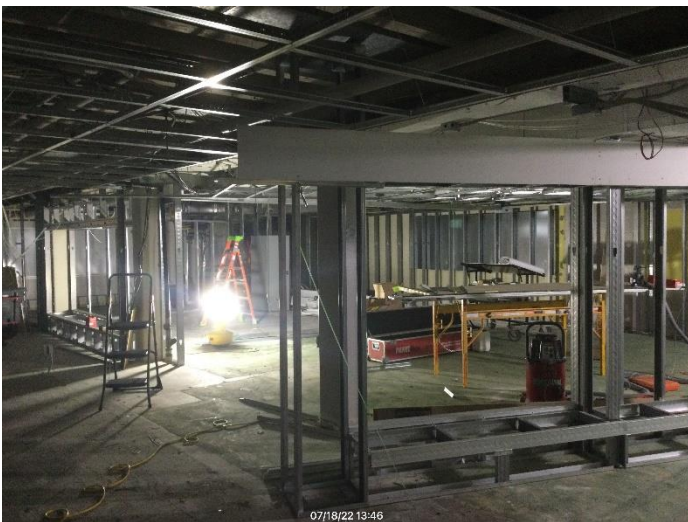

Continuing wall framing in 1st floor area



Installation of corridor ceiling grid in 1st floor
area

Westridge Middle School

Construction Report 06/17/2022

This Week

June 13th – June 17th

- Finished demolition in level 2 bathroom
- Finished demolition of level 1
- Finished demolition of level 2 offices and classrooms
- Began framing on level 2 bathroom and offices



Demolition of front entranceway

Next Week

June 20th – June 25th

- Continue wall framing in all areas
- Begin overhead MEP on level 2
- Begin rough grading for level 2 addition and courtyard



Level 1 demolition

Westridge Middle School

Construction Report 06/17/2022



Level 1 wall framing



Framing of new office space



Grading in east courtyard



Demolition of old offices
